

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #4
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 766
- » Total Man Hours on Project: 3322
- » Crafts On Project This Week: 3
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued steam line removal east of water tower
- » Began water tower removal
- » Mobilization of crane for water tower



Began Water Tower Demo



Steam Line Removal East of Tower



NEXT WEEK'S ACTIVITIES

- » Begin removal of water tower cross bracing
- » Begin removal water tower risers



Continue Removal of Water Tower



Begin Removal of Water Tower Risers

- » Continue removal of steam line east of water tower

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #4
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

18	19	20	21	22	23	24
Actual: 60 36 0.00	Actual: 66 42 0.00	Actual: 69 45 0.00	Actual: 68 45 0.00	Actual: 59 34 0.00	Actual: 48 39 0.79	Actual: 51 41 0.04
Average: 51 29 0.17	Average: 52 31 0.21	Average: 51 29 0.25	Average: 51 29 0.24	Average: 51 29 0.19	Average: 52 31 0.19	Average: 53 30 0.15

Rain Days This Week = 1

Rain Days To Date = 3

SAFETY REVIEW LOG

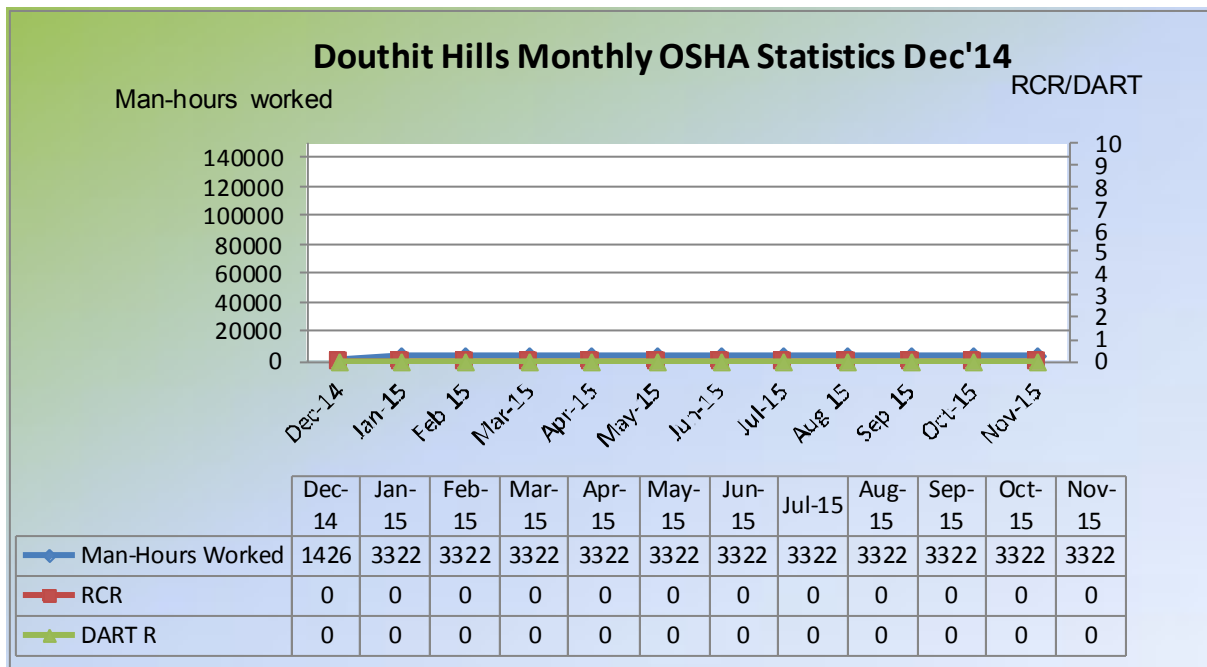

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #4
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	5	250	870
CNC Fence	Site Fence	0	0	480
Hutch-N-Son	Early Site Work	0	0	600
JBR Construction	Steam Line Removal	5	200	550
Labor Finders	Labor Force	2	116	462
R.E. Mclean Tank	Tank Demo	4	200	360
TOTAL		16	766	3322

REPORTS



INSPECTIONS/TESTING

- DHEC Erosion Control Inspection
- S&ME Steam line Inspections
- BLE — Soils & Erosion Control Inspections





MANPOWER CHART

