

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #10  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 909
- » Total Man Hours on Project: 10421
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

- » Continued installation of orange tree save on tree protection fence
- » Completed utility demo work at trailer compound
- » Began grading and stone at trailer compound
- » Completed root pruning around tree protection areas



Holder Trailer Compound

- » Site work contractor began mobilization



Root Pruning at Tree Protection Areas



## NEXT WEEK'S ACTIVITIES

- » Continue installation of orange tree save on tree protection fence
- » Continue stone work at trailer compound area
- » Begin installation of electrical duct bank for trailer compound



Began Grading Trailer Compound



Utility Demo at Trailer Compound

- » Begin installation of jobsite erosion control
- » Continue mobilization of site contractor

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #10  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER


### CURRENT WEEK

19	Rain	20	Tstorm	21	Clear	22	Rain	23	Clear	24	Clear	25	Rain
Actual: 70°   66° 0.77 in	Actual: 73°   61° 0.33 in	Actual: 73°   50° 0.00 in	Actual: 81°   45° 0.18 in	Actual: 77°   54° 0.00 in	Forecast: 71°   55° 0.13 in	Forecast: 68°   61° 0.68 in							
Average: 74°   49° 0.12 in	Average: 74°   47° 0.09 in	Average: 74°   48° 0.08 in	Average: 74°   49° 0.11 in	Average: 74°   48° 0.18 in	Average: 74°   49° 0.13 in	Average: 75°   48° 0.05 in							

Rain Days This Week = 1

Rain Days To Date = 10

### SAFETY REVIEW LOG

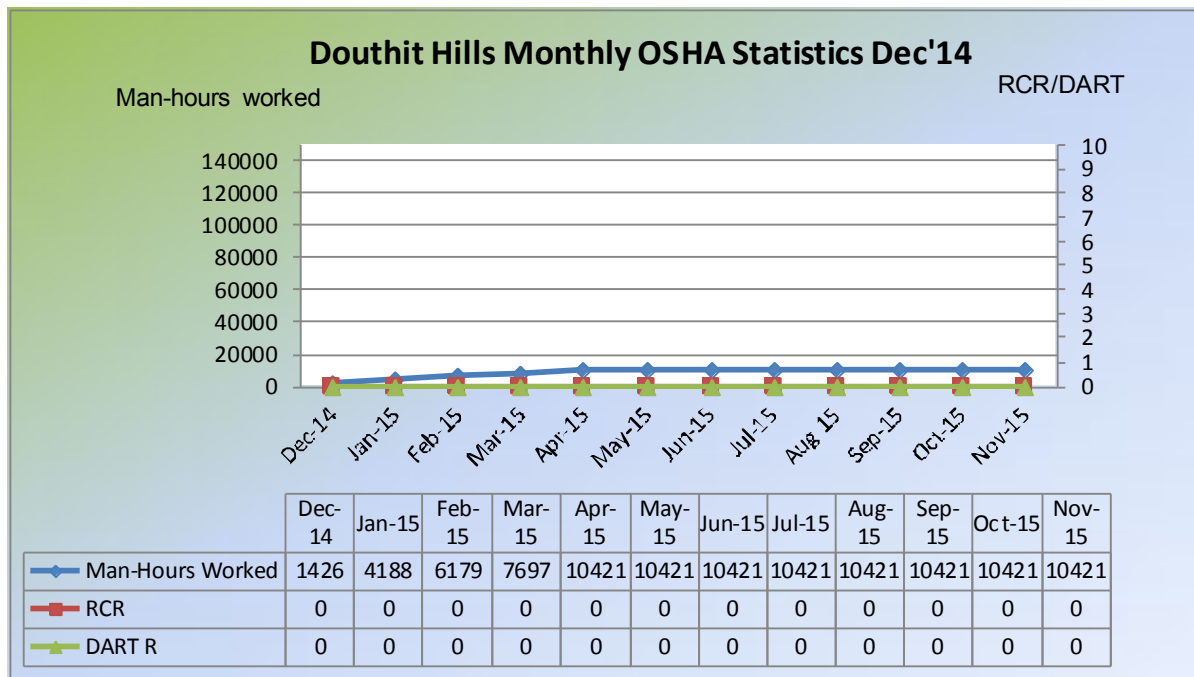

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #10  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	10	550	4811
CNC Fence	Site Fence	3	30	675
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Labor Finders	Labor Force	2	96	1102
R.E. Mclean Tank	Tank Demo	0	0	660
Hutch-N-Son	Early Site Work	5	225	1025
Tree South	Arborist	2	8	18
<b>TOTAL</b>		<b>22</b>	<b>909</b>	<b>10421</b>

## REPORTS



### INSPECTIONS/TESTING

- DHEC Erosion Control Inspection
- S&ME Steam line Inspections
- BLE — Soils & Erosion Control Inspections





## MANPOWER CHART

