

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #28
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 2306
- » Total Man Hours on Project: 46031
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation.
- » Continued cutting grass in tree save areas.
- » Continued to patch damaged asphalt on Daniel Dr.
- » Continue to rough grade Pecan Grove.
- » Continue Installation of Chiller Pipe



Rough Grading for Newman temporary Rd.



Concrete patching on Daniel Dr.

- » Continued electrical underground installation east of Newman Rd. entrance.
- » Commenced rough grading at new Daniel square entrance.
- » Commenced underground utilities at Gate 1.



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control.
- » Continue storm line 4B near Gate 1.
- » Continue installation of chiller pipe.
- » Continue rough grading of Newman temporary Rd.



Grading at new Daniel Square entrance



Continue Underground Electrical Conduit

- » Continue cutting grass on site.
- » Continue installation of underground electrical utilities.
- » Commence final grading at Daniel Square entrance.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #28
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	13	585	16323
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	240
Labor Finders	Labor Force	5	200	4707
Metro Power	Underground Electrical	5	170	290
Osteen	Chill Water pipe	5	160	320
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	22	1056	14816
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	0	0	532
Valley Farm Construction	Tree removal/Grading	3	135	255
TOTAL		53	2306	46031

REPORT



INSPECTIONS/TESTING

DHEC Erosion Control Inspection

August 31, 2015

Page | 4



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #28
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

23 Tstorm Actual: 84° 69° 1.90 in Average: 86° 66° 0.17 in	24 Clear Actual: 90° 71° 0.00 in Average: 86° 66° 0.13 in	25 Clear Actual: 89° 71° 0.00 in Average: 87° 66° 0.12 in	26 Scattered Clouds Actual: 87° 68° 0.00 in Average: 86° 66° 0.19 in	27 Scattered Clouds Actual: 86° 68° 0.00 in Average: 87° 66° 0.04 in	28 Partly Cloudy Forecast: 87° 67° 0.0 in Average: 87° 65° 0.14 in	29 Partly Cloudy Forecast: 86° 69° 0.0 in Average: 87° 65° 0.07 in
---	--	--	---	---	---	---

Rain Days This Week = 1

Rain Days To Date = 23

SAFETY REVIEW LOG

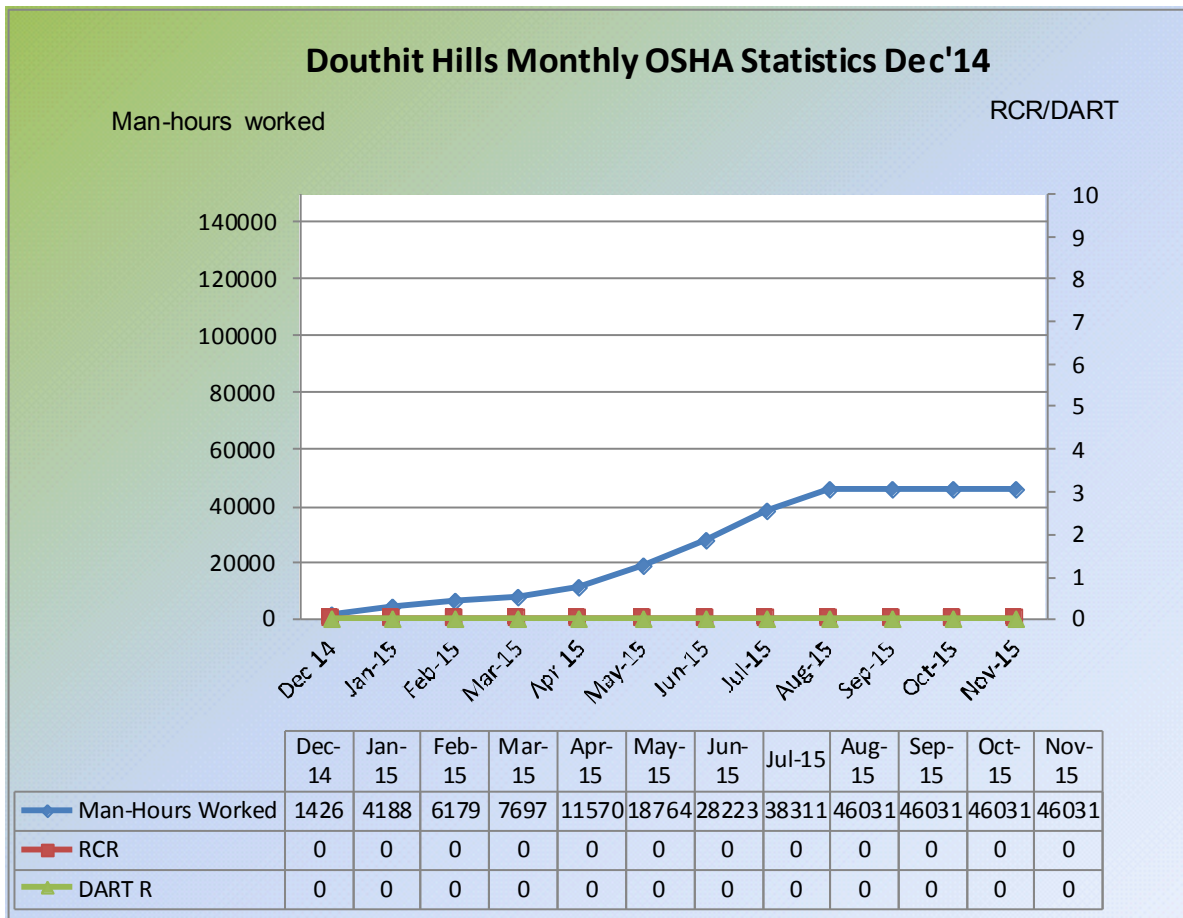

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #28
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

