



SAFETY

- » Total Man Hours Worked This Week: 4151
- » Total Man Hours on Project: 63417
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued temp power for east buildings.
- » Completed installation of Storm Line 5A and 5B.
- » Continued grading North Lot.
- » Continued grading on the Hub building pad.



Continued installation of manholes 11 and 12



Completed Dissipater at detention pond.

- » Commenced grading at West Zone.
- » Poured footings at level 1 Building G.
- » Continued pouring basement walls at Bldg G
- » Continued silt fence and erosion control installation as needed.
- » Continued cutting grass in tree save areas.



NEXT WEEK'S ACTIVITIES

- » Continue grading for East lot.
- » Commence installation of Storm line 6A.
- » Continue water line installation at North Lot.
- » Complete Storm Line 2.
- » Continue installation of East zone crane and access roads for Building E.



Continued grading on Hub building pad.



Forming and Pouring of Building G east wall and south wall.

- » Continue forming and pouring walls at Building G basement and commence waterproofing.
- » Continue installation of underground electrical from manhole #11 to #9.
- » Continue cutting grass on site.
- » Continue installation of jobsite erosion control as needed.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #35
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	19	855	21588
American Deep Foundation	Auger cast piles	0	0	280
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	682
Labor Finders	Labor Force	8	360	6359
Metro Power	Underground Electrical	7	284	1917
Osteen	Chill Water pipe	5	20	500
Precision	Concrete	25	1250	1250
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	27	1350	21430
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	2	32	732
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		93	4151	63417




HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #35
 Douthit Hills Student Community, Clemson University Project
 Joe Jett




WEATHER

CURRENT WEEK



SAFETY REVIEW LOG

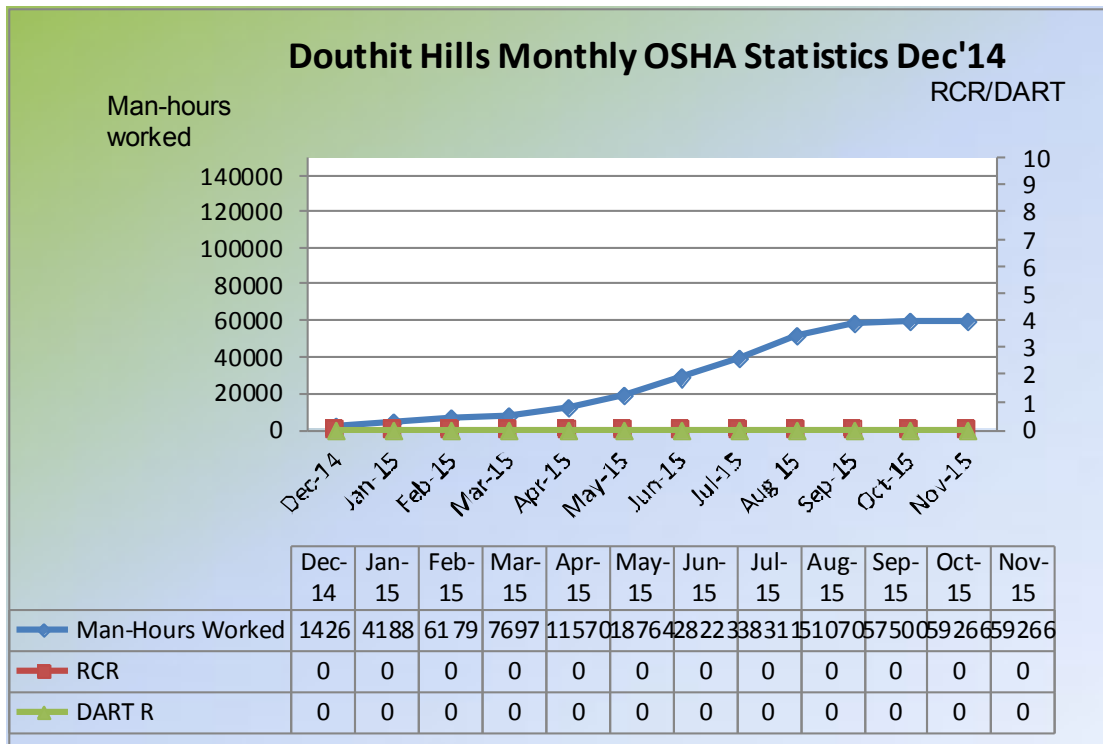

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #35
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

