

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #62
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY


- » Total Man Hours Worked This Week: 7374
- » Total Man Hours on Project: 179412
- » Crafts On Project This Week: 12
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES


- » Installed Drywall @ Building G 4th Floor.
- » Continued Domestic Water Rough-In @ Building G Bathrooms.
- » Continued Window Frame Installation @ Building E.
- » Continued Brick Masonry @ Building G.
- » Continued Shingles @ Building F.
- » Continued Installing Roof Trusses @ Building E Sequence 1.
- » Continued Interior Wall Framing @ Building F 3rd Floor.
- » Poured Building E 4th Floor Topping Slab.

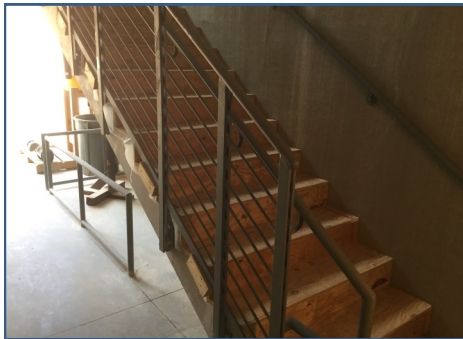

Bldg. G Stair Rails



Bldg. E Plumbing

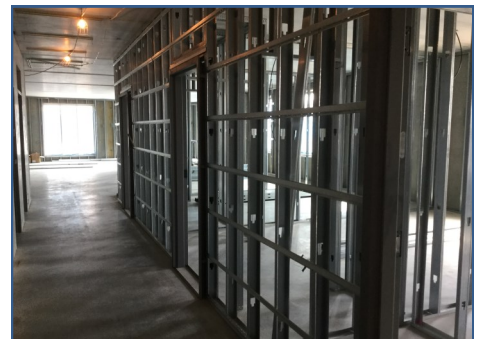

Bldg. F Framing

SITE, HUB, & WEST ZONE

- » Continued Forming Walls and Columns @ HUB.
- » Continued Backfilling @ HUB.
- » Continued Forming Elevated Deck @ HUB.
- » Paved Northwest Lot.
- » Continued CIP Walls @ Building A.
- » Continued Foundations @ Building B.
- » Continued Backfill @ Building A.
- » Continued Retaining Wall @ HUB.



Retaining Wall @ HUB



Elevated Deck @ HUB



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Shingles @ Building F.
- » Continue Electrical Rough-In @ Building G.
- » Continue Brick @ Building G.
- » Continue Glazing @ Building E.
- » Pour Building E 3rd Floor Topping Slab.
- » Continue Aboveground Sanitary Risers @ Building F.



Building A Backfill



Paving @ NW Parking Lot

SITE, HUB, & WEST ZONE

- » Continue Storm Line 10.
- » Continue Foundations @ Building A.
- » Continue Retaining Wall @ HUB.
- » Continue Foundations @ Building B.
- » Auger Cast Piles @ HUB.
- » Pour HUB Elevated Deck.
- » Install Duct Bank From MH4 to MH3.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #62
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	26	1040	42920
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	6	360	2376
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	8910
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	9	432	3060
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	5	140	1968
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	8	320	1820
King Asphalt	Asphalt	16	272	2264
Labor Finders	Labor Force	11	520	18318
Metro Power	Underground Electrical	10	355	11027
Osteen	Chill Water pipe	0	0	2066
Precision	Concrete	50	1000	23040
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	810	36420
Rival Construction Inc.	Concrete	24	960	2193
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	17	760	5518
Silt Fence Installation	Site Erosion Control	0	0	974
Southern Mechanical Inc.	Electrical/Plumbing	9	360	3360
Tree South	Arborist	3	45	1231
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	0	0	250
TOTAL		209	7374	179412



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #62
 Douthit Hills Student Community, Clemson University Project
 Joe Jett




WEATHER

CURRENT WEEK

10 Scattered Clouds Actual: 57° 37° 0.00 in Average: 70° 43° 0.13 in	11 Rain Actual: 71° 46° 0.12 in Average: 70° 43° 0.04 in	12 Tstorm Actual: 75° 57° 0.04 in Average: 73° 44° 0.09 in	13 Partly Cloudy Actual: 68° 55° 0.00 in Average: 72° 47° 0.22 in	14 Scattered Clouds Actual: 71° 54° 0.00 in Average: 72° 48° 0.16 in	15 Clear Forecast: 68° 50° 0.0 in Average: 71° 49° 0.20 in	16 Clear Forecast: 72° 48° 0.0 in Average: 73° 46° 0.06 in
---------------------------------------------------------------------------------------------	---------------------------------------------------------------------------------	-----------------------------------------------------------------------------------	------------------------------------------------------------------------------------------	---------------------------------------------------------------------------------------------	-----------------------------------------------------------------------------------	-----------------------------------------------------------------------------------

Rain Days This Week = 1 Rain Days To Date = 46

SAFETY REVIEW LOG

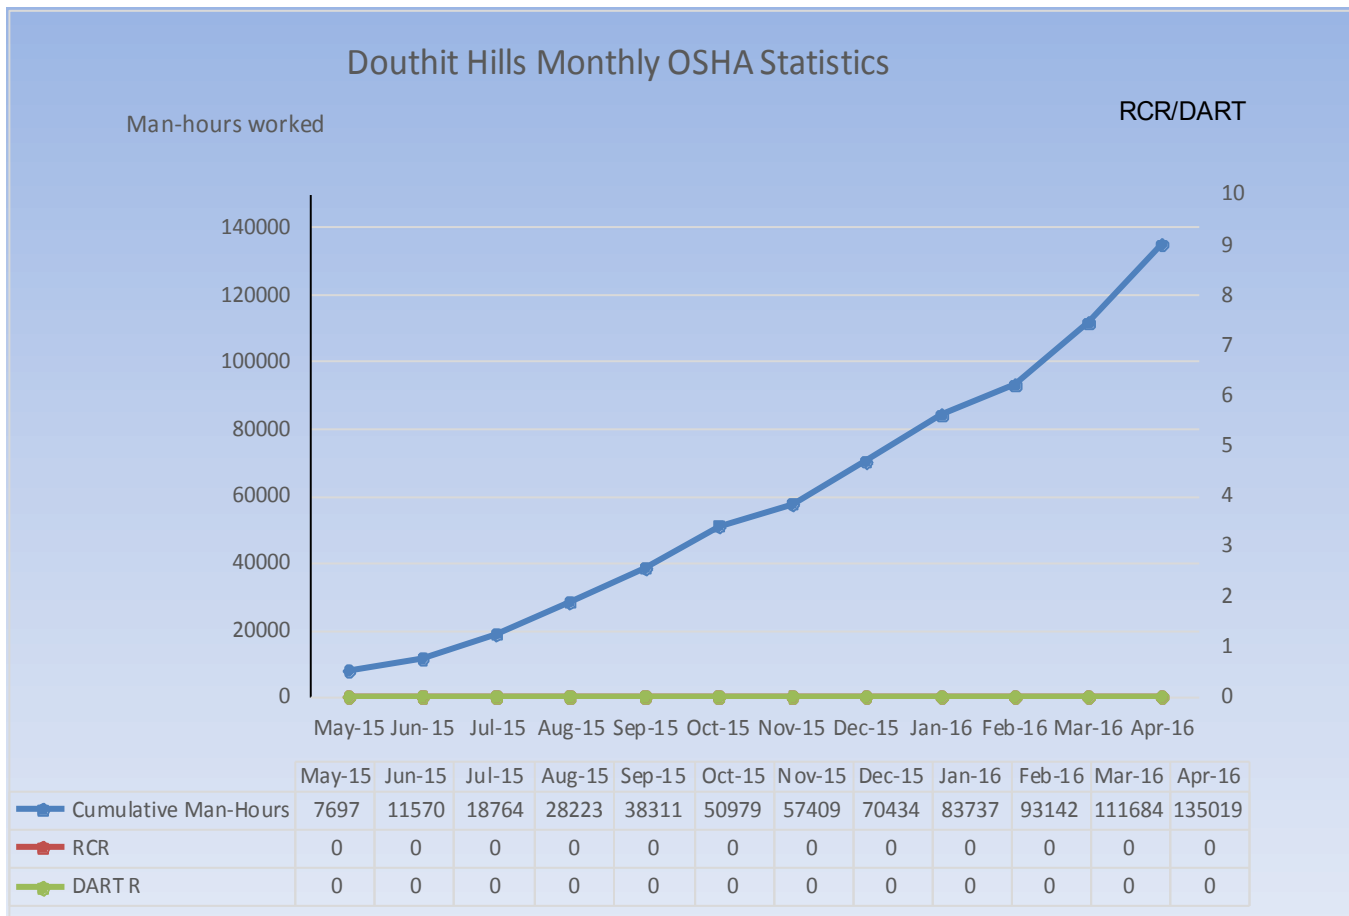

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #62
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

