



SAFETY


- » Total Man Hours Worked This Week: 9086
- » Total Man Hours on Project: 188636
- » Crafts On Project This Week: 13
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

- » Continued Domestic Water Rough-In @ Building G Bathrooms.
- » Continued Window Frame Installation @ Building E.
- » Continued Brick Masonry @ Building G.
- » Continued Shingles on Building F.
- » Began Installing Roof Trusses @ Building E Sequence 2.
- » Poured Building E 3rd Floor Topping Slab.
- » Continued Installing Stair Rails @ Building G.
- » Continued Electrical Rough-In @ Building G.
- » Installed Building F Water Tie Ins.

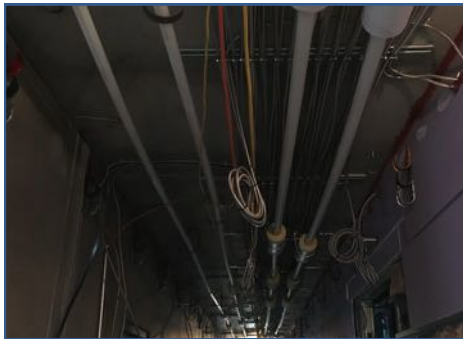

Bldg. G Overhead Rough-In

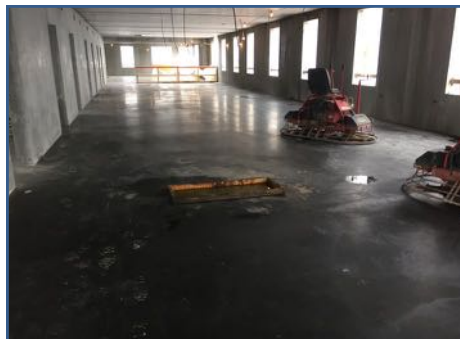

Bldg. E 3rd Floor Slab



Bldg. F Water Tie Ins

SITE, HUB, & WEST ZONE

- » Continued Forming Elevated Deck B @ HUB.
- » Continued Foundations @ Building B.
- » Began Auger Cast Piles @ HUB .
- » Continued Retaining Wall @ HUB.
- » Continued Racking Manholes.
- » Transformer Pad Prep for Buildings E,F,& G.
- » Continued Medium Voltage Cable.
- » Installed Ductbank From MH4 to MH3.



Retaining Wall @ HUB




Access Road @ HUB



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Shingles @ Building F.
- » Continue Electrical Rough-In @ Building G.
- » Continue Brick @ Building G.
- » Continue Glazing @ Building E.
- » Pour Building E 2nd Floor Topping Slab.

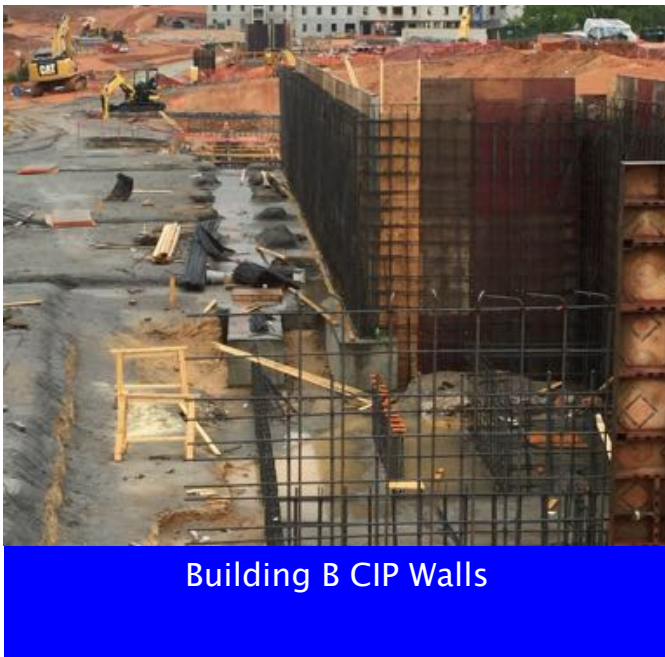

SITE, HUB, & WEST ZONE

- » Continue Storm Line 10.
- » Begin Precast @ Building A.
- » Begin Retaining Wall @ Magnolia Tree.
- » Continue Foundations @ Building B.
- » Continue Auger Cast Piles @ HUB.
- » Pour Elevated Deck 1st Section @ HUB.
- » Continue Forming HUB Elevated Deck.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #63
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	26	1040	43960
American Deep Foundation	Auger cast piles	7	280	4572
Baker Roofing	Sheathing and Shingles	6	360	2736
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	4	120	8910
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	13	624	3684
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	240	2208
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	8	320	2140
King Asphalt	Asphalt	0	0	2264
Labor Finders	Labor Force	11	520	18838
Metro Power	Underground Electrical	10	370	11397
Osteen	Chill Water pipe	0	0	2066
Precision	Concrete	56	2240	25840
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	750	37170
Rival Construction Inc.	Concrete	36	1440	3633
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	24	1022	5518
Silt Fence Installation	Site Erosion Control	0	0	974
Southern Mechanical Inc.	Electrical/Plumbing	9	360	3720
Tree South	Arborist	3	120	1351
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	0	0	250
Total		234	9806	188636



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #63
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

17	Clear		18	Clear		19	Clear		20	Clear		21	Scattered Clouds		22	Thunderstorm		23	Clear	
Actual: 77° 48°		Actual: 84° 50°		Actual: 87° 55°		Actual: 82° 62°		Forecast: 80° 62°		Forecast: 77° 56°		Forecast: 84° 56°								
0.00 in		0.00 in		0.00 in		0.00 in		0.28 in		0.27 in		0.0 in								
Average: 72° 46°		Average: 74° 47°		Average: 74° 49°		Average: 74° 47°		Average: 74° 48°		Average: 74° 49°		Average: 74° 48°								
0.07 in		0.12 in		0.12 in		0.09 in		0.08 in		0.11 in		0.18 in								

Rain Days This Week = 1

Rain Days To Date = 47

SAFETY REVIEW LOG

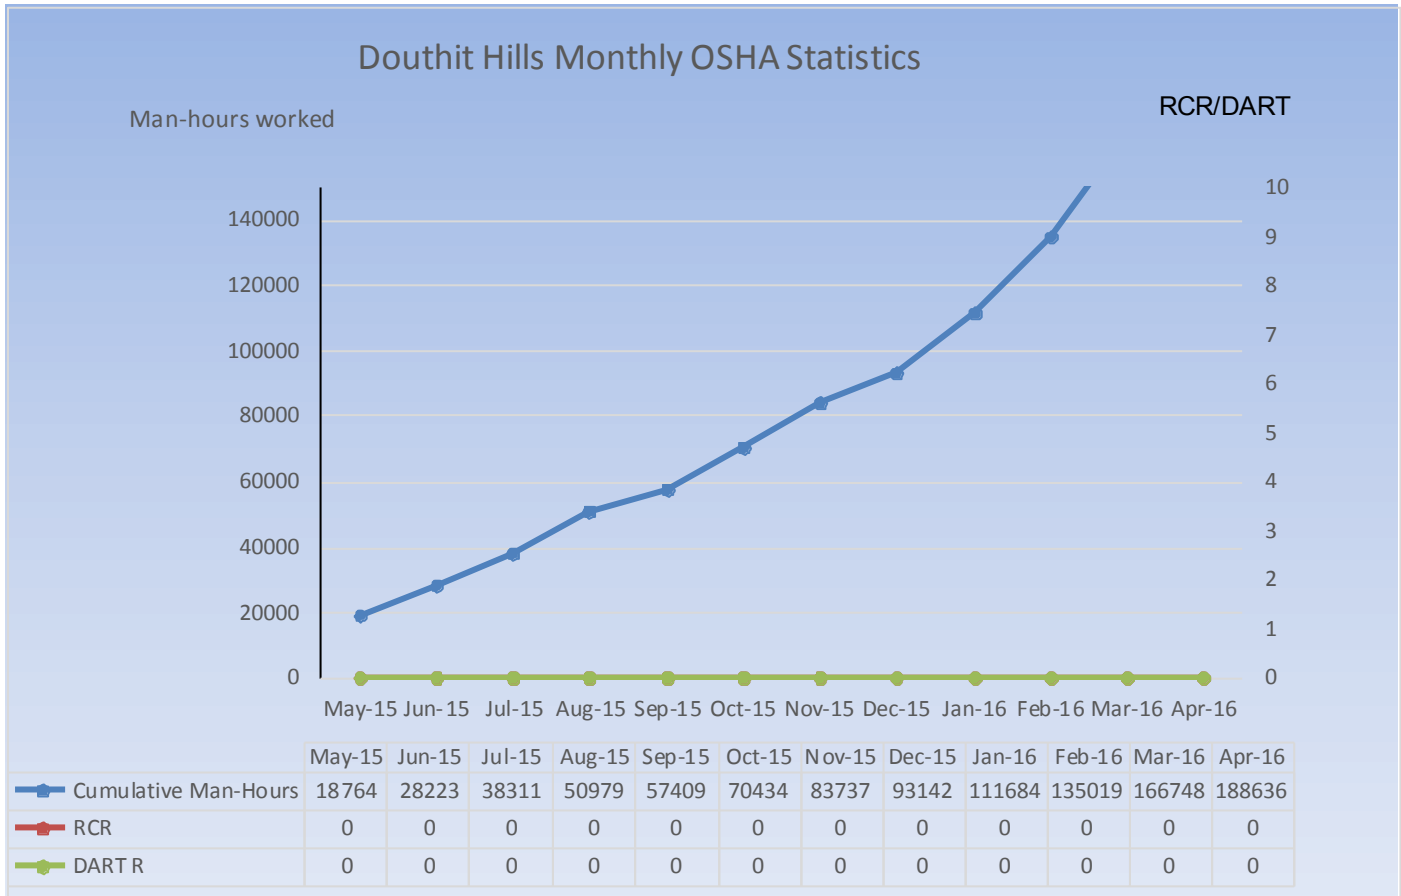

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #63
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

