

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #102
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 24215
- » Total Man Hours on Project: 890118
- » Crafts On Project This Week: 23
- » OSHA Recordable Rate: 0



HOLDER CONSTRUCTION COMPANY


Superintendents Weekly Activity Report #102
Douthit Hills Student Community, Clemson University Project
Joe Jett



CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued MEP Rough-In @ Building E.
- » Continued Wood Doors @ Building E.
- » Installed Mirrors @ Building G.
- » Continued Finishing Drywall @ Building E.
- » Continued Painting Walls @ Buildings G, F, & E.
- » Continued Wall Tile @ Building G.
- » Continued Lights and Devices @ Building F.
- » Began Punch-List @ Building G 2nd Floor.
- » Continued ACT Grid @ Buildings E, F.
- » Set Vanities @ Building G.
- » Installed Closet Trim @ Building F.
- » Continued Point Up on 4th Floor @ Building G.

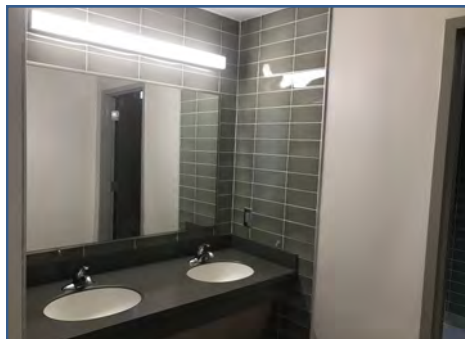

Bldg. G Vanity and Accessories




Ductwork @ HUB



Bldg. E Terrace

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B and Building C.
- » Continued Brick Masonry @ HUB & Bldg. C.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Hanging Duct @ HUB.
- » Continued Glass Installation @ HUB & Building C.
- » Continued Window Frames @ Building C.
- » Poured SOG @ Building E Terrace.
- » Continued Topping Slab Prep @ Building D.
- » Continued Newman Rd Intersection Roadwork.
- » Began Building D Load Bearing Walls.
- » Poured Base Slabs @ Bldgs. G & F.
- » Continued setting Site Lighting Fixtures

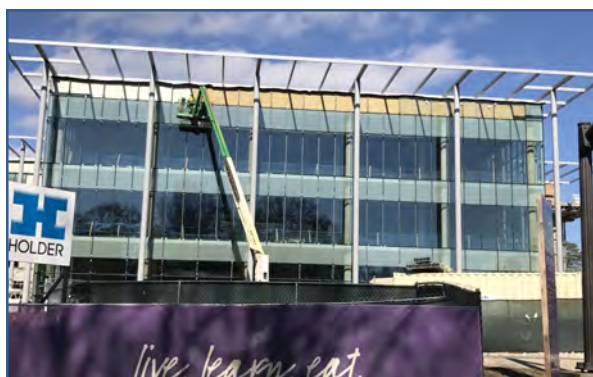

HUB Curtain Wall



Site Stabilization @ East Monumental Stairs





NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Finishing Drywall @ Building E.
- » Continue Finishing on Building G 1st Floor.
- » Continue Wall Tile @ Building F & G.
- » Begin Wall Tile @ Building E.
- » Continue Installing Lights & Devices @ Building F & E.
- » Continue Point Up 4th Floor @ Building G.
- » Continue Building E Terrace.
- » Continue Trim Punch-List @ Building G.



Building G 1st Floor Corridor Lights



Building C Masonry- West Elevation



Building B - Interior Framing

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB & Building C.
- » Continue MEP Rough-In @ Bldgs A, B, & HUB.
- » Continue Interior Framing & Drywall @ Bldg B.
- » Continue Roof Decking @ Building C.
- » Continue Building D Loadbearing Walls @ Building D.
- » Continue Pouring Building E Terrace.
- » Continue Topping Slab Prep @ Building D.
- » Continue Framing Interior Walls @ Building C.
- » Continue Coring @ Building C For Plumbing.
- » Continue HWY 93 Work @ Newman Road.
- » Continue Site Lighting



HUB Interior Framing



Building E Terrace

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #102
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1755	105880
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	5	200	4700
Cabinets By Design	Millwork	2	80	240
Carolina Fire Protection	Sprinklers	16	800	22645
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	10	500	3370
Feltman Brothers	West - Masonry	25	1250	18435
Gainesville Mechanical	Ductwork	14	700	60419
Gill Plumbing	Plumbing	32	1600	29830
Graham Hodge	Glass	9	360	4330
Gregory Electric	Aboveground Electric	17	850	17950
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	14	700	13152
Johnson Controls	Building Controls	9	450	5885
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	30	1200	41722
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	3063
Labor Finders	Labor Force	17	680	42908
Metro Power	Underground Electrical	4	160	21707
Nations Roofing	Roofing	11	440	7435
Old North State Masonry	East - Masonry	0	0	28769
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	6	300	83710
Pro Door	Doors & Hardware	5	250	500


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #102
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER

CURRENT WEEK




SAFETY REVIEW LOG

Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

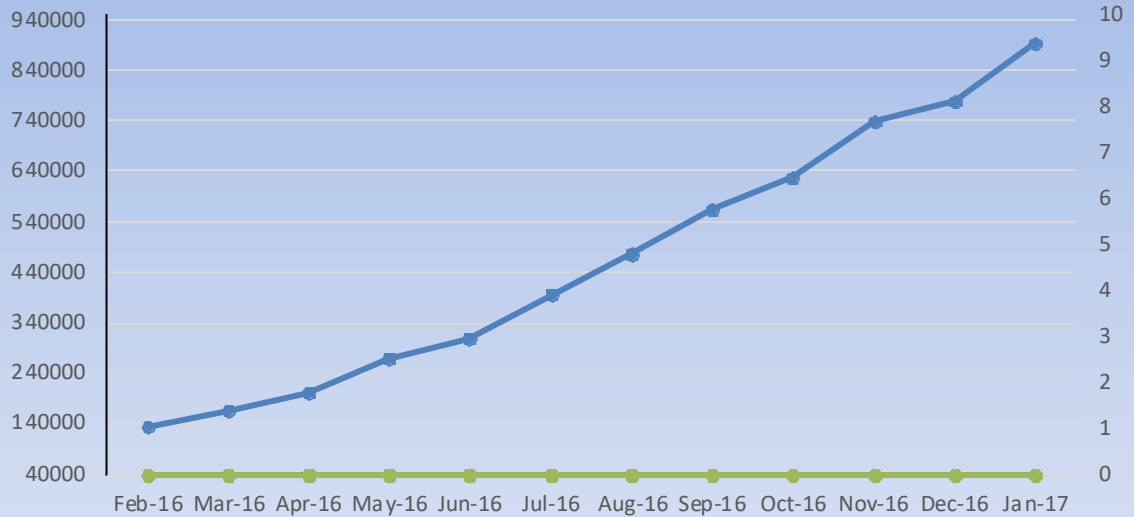

	Feb-16	Mar-16	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17
Cumulative Man-Hours	135019	166748	201384	268272	307534	395795	475812	563897	627462	738504	776399	890118
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #102
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

Douthit Hills Workforce

