

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #99
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 15280
- » Total Man Hours on Project: 822019
- » Crafts On Project This Week: 23
- » OSHA Recordable Rate: 0







CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued Wood Door Install @ Building F.
- » Continued Hanging Drywall @ Building E.
- » Continued Painting Walls @ Building F.
- » Continued Wall Tile @ Building G.
- » Continued Lights and Devices @ Building G.
- » Continued Fire Protection Upfit @ Building E.
- » Continued ACT Grid @ Building G & F.
- » Installed Dorm Lights @ Building F.
- » Set Plumbing Fixtures @ Building G.

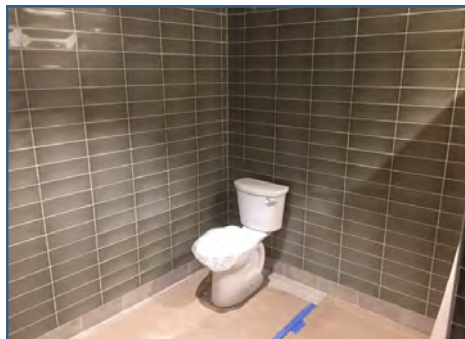

Bldg. G Plumbing Fixtures

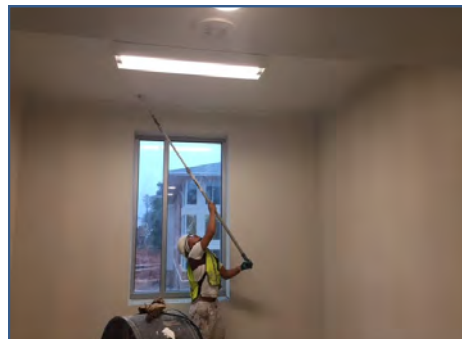

Paint in Bldg. G



Bldg. G Mech. Room

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Bldg. C.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Roofing @ Building B.
- » Continued Glass Installation @ HUB.
- » Continued Window Frames @ Building C.
- » Continued Elevator Install @ Bldg. A.
- » Installed Storm Line @ Building B Courtyard.
- » Completed Precast @ Building D.
- » Continued Drywall Finishing @ Building A.



Storm Drains @ Bldg. B



Duct Shaft Rough-in @ HUB



NEXT WEEK'S ACTIVITIES

East Zone


- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Install Doors & Hdwe @ Bldgs. F & G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Hanging Drywall @ Building E.
- » Continue Finishing Drywall @ Building E & F.
- » Continue Wall Tile @ Building G.
- » Continue ACT Grid @ Building F.
- » Continue Installing Lights & Devices @ Building F.
- » Continue Plumbing Fixtures @ Building G.
- » Continue Painting Walls @ Building F.



Finishing Corridors @ Bldg. E



Bedding & Taping @ Bldg. E

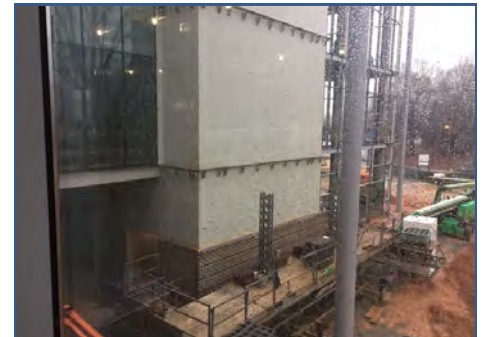

HUB Masonry Continues

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB, Building B & C.
- » Continue MEP Rough-In @ Bldgs. A, B, & HUB.
- » Continue Roofing @ Building B.
- » Continue Interior Framing & Drywall @ Bldg A.
- » Continue Interior Framing @ Building B.
- » Continue Roof Decking @ Building C.
- » Continue Window Frames @ Building C.
- » Continue Precast @ Building D.
- » Install Storm Line @ Building B Courtyard.
- » Begin Sunshade Infill @ HUB
- » Prep/Pour Terrace Bldg. E East Side
- » Complete Bldg. B Courtyard Storm Structures



Precast Complete/Crane Gone



Bldg. C Brick @ South Side

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #99
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	27	1080	101005
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	0	0	4125
Carolina Fire Protection	Sprinklers	11	550	20495
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	11	440	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	0	0	2070
Feltman Brothers	West - Masonry	25	950	15570
Gainesville Mechanical	Ductwork	18	720	58069
Gill Plumbing	Plumbing	25	1000	25380
Graham Hodge	Glass	8	360	3290
Gregory Electric	Aboveground Electric	13	520	15750
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	9	360	11102
Johnson Controls	Building Controls	0	0	4685
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	31	1240	37522
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	20	2763
Labor Finders	Labor Force	17	680	40868
Metro Power	Underground Electrical	4	140	21267
Nations Roofing	Roofing	5	200	6420
Old North State Masonry	East - Masonry	0	0	28619
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	0	0	82810
Pyramid Masonry	Hub-Masonry	15	600	8560
R.E. Mclean Tank	Tank Demo	0	0	660

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #99
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Reeves Young	Site Grading & Utilities	6	240	58678
Rival Construction Inc.	Concrete	13	520	36856
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	93	3720	100982
Silt Fence Installation	Site Erosion Control	0	0	1031
Simplex	Controls	0	0	1400
Southern Mechanical Inc.	Electrical/Plumbing	31	1240	59640
Specialty Finishes	Painting	8	320	2885
Steel Toe	Labor Force	10	400	11215
Tree South	Arborist	0	0	2073
Upstate Curb	Curb and Gutter	0	0	684
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	0	0	3104
Total		382	15280	822019



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #99
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Precipitation	Average High/Low	Average Precipitation
25	Scattered Clouds	72° 48°	0.00 in	51° 32°	0.22 in
26	Rain	60° 54°	0.04 in	50° 30°	0.09 in
27	Rain	66° 53°	0.01 in	51° 30°	0.02 in
28	Scattered Clouds	60° 43°	0.00 in	52° 33°	0.27 in
29	Tstorm	64° 44°	0.59 in	52° 31°	0.13 in
30	Clear	54° 37°	0.00 in	53° 31°	0.06 in
31	Rain	48° 32°	0.05 in	51° 33°	0.23 in

Rain Days This Week = 1

Rain Days To Date = 59

SAFETY REVIEW LOG

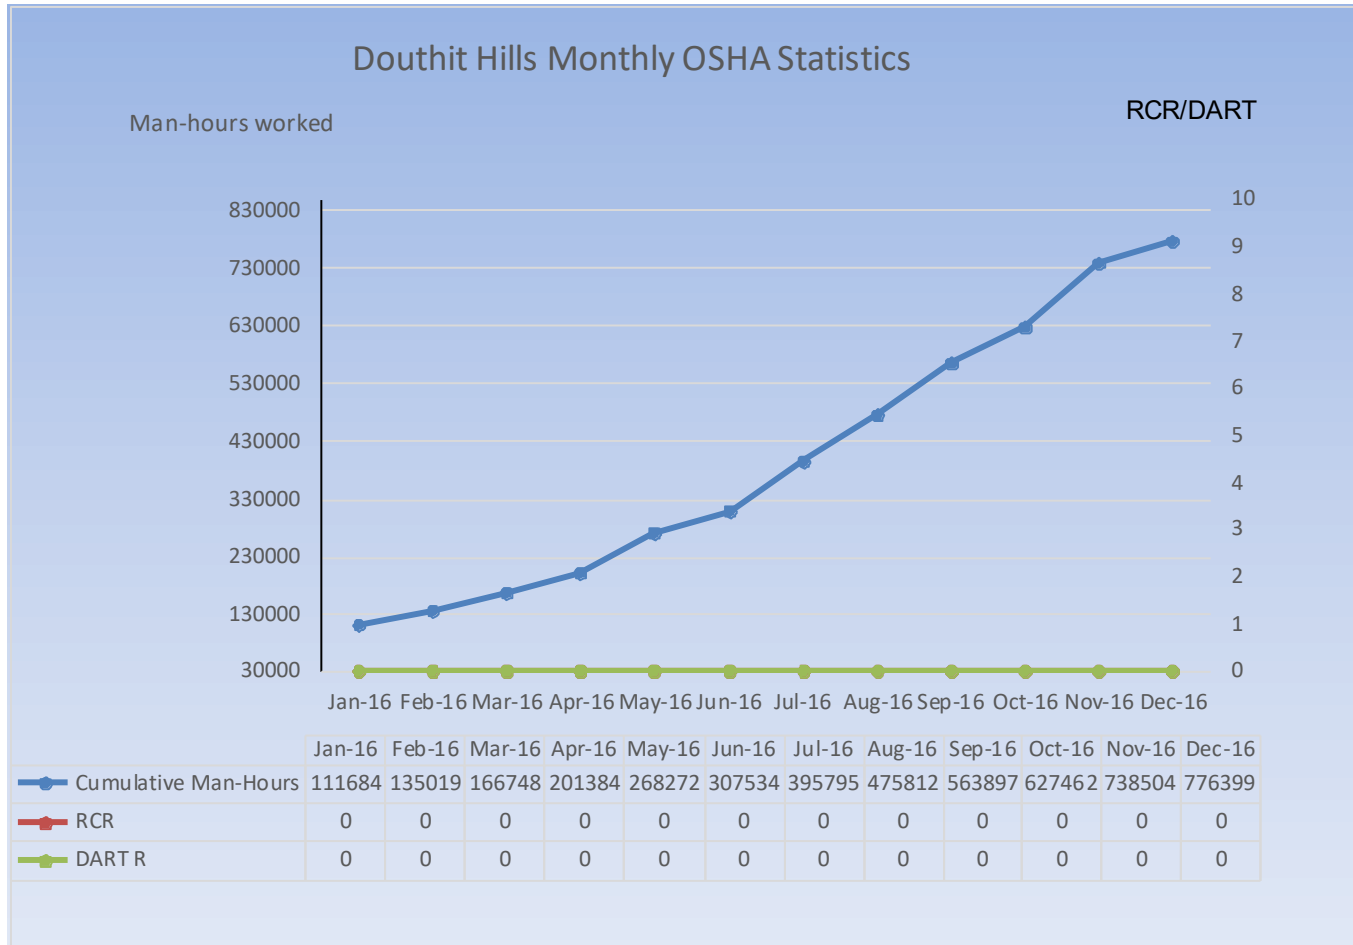


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #99
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

Douthit Hills Workforce

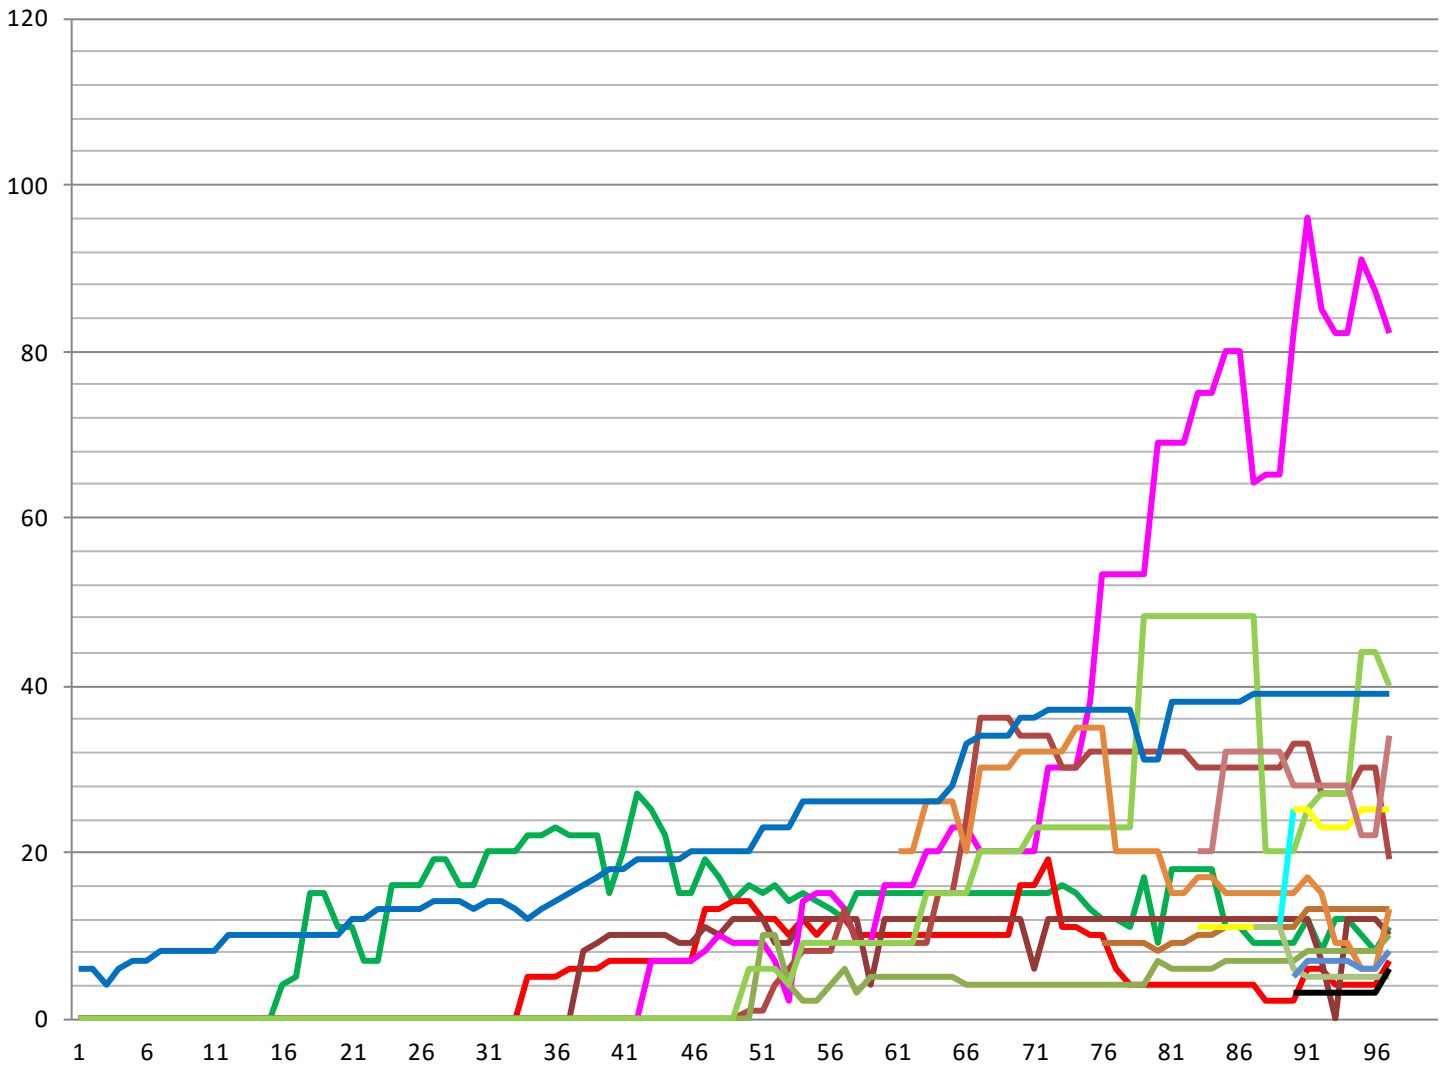

- Reeves Grading
- Metro Power
- Davis Crane Erectors
- Pyramid Masonry
- Sears Contract
- Gainesville Mechanical
- 1st Choice Glass
- Southern Mechanical
- Rival Construction
- Feltman Brothers
- JME
- Graham Hodge
- Elite Flooring
- Specialty Finishes
- Holder

