

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #110
Douthitt Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 22420
- » Total Man Hours on Project: 1081124
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0



HOLDER CONSTRUCTION COMPANY


Superintendents Weekly Activity Report #110
Douthitt Hills Student Community, Clemson University Project
Joe Jett




CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Hanging ACT Grid @ Building E.
- » Continued Acoustical Tile @ Building G 4th Floor.
- » Continued Punchlist @ Building G.
- » Continued Drywall Finishing @ Building E.
- » Continued Fire Alarm Testing @ Building G.
- » Continued Overhead Inspections @ Bldg. G.
- » Continued Tile in Building E.
- » Continued Trash Walls North of Building E.
- » Continued T & B @ Building G.
- » Removed Sidewalk at HWY 93 South of Bldg E.

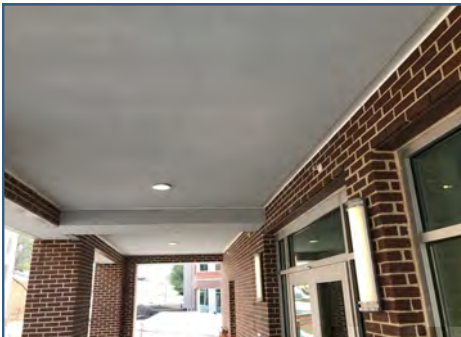

Building G Exterior Lights

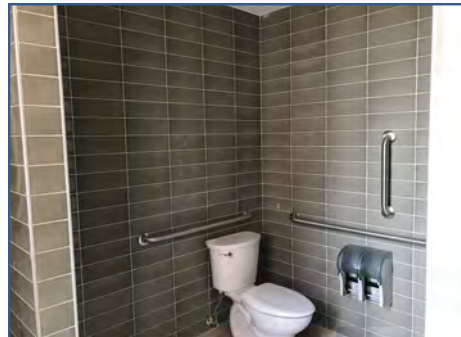

Building E Bathroom Tile




HUB Loading Dock

SITE, HUB, & WEST ZONE

- » Continued Interior Framing and Hanging @ Bldgs. B and C.
- » Continued Brick Masonry @ Bldg. D.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. C.
- » Poured Loading Dock SOG.
- » Continued DEIFS @ Bldgs. B & C.
- » Continued Sunshade Infill @ HUB.
- » Continued Finishing Drywall @ Building A.
- » Began Demo @ Cherry Road Intersection.
- » Install Storm Line Between Bldg D and B.
- » Began Grading Around Cooling Tower.
- » Continued Curb & Gutter N. of Bldg.
- » Set Vaults @ Kite Hill Water Tower



Building E Handrails

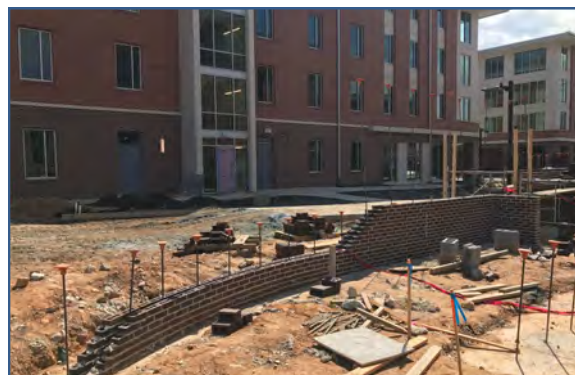

Trash Walls North of Building E

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #110
Douthitt Hills Student Community, Clemson University Project
Joe Jett



NEXT WEEK'S ACTIVITIES

East Zone


- » Continue Finishing Drywall @ Building E.
- » Continue Painting @ Building E.
- » Continue Wall Tile @ Building E.
- » Continue Installing Lights & Devices @ Bldg. E.
- » Continue ACT Grid @ Building E.
- » Begin 1st Floor Lobby Tile @ Building F.
- » Continue Punch List @ Building G 2nd Floor.
- » Continue Acoustical Ceiling Tile @ Building G.
- » Began Carpet @ Building G.
- » Began Punchlist @ Building E.



Building B Finishing



Building D Masonry

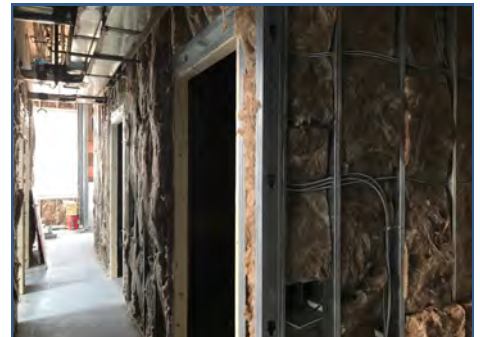

Building C Wall Insulation

SITE, HUB, & WEST ZONE

- » Continue Brick Masonry @ Building D.
- » Continue MEP Rough-In @ Bldgs. A, B, & HUB.
- » Continue Hanging Drywall @ Bldg. B.
- » Continue Framing Walls @ Building C & D.
- » Continue Painting Walls @ Building A.
- » Continue Cherry Rd Intersection Roadwork.
- » Continue Loading Dock @ HUB.
- » Continue DEIFS @ Bldgs. B & C.
- » Continue Glass Installation @ Building D.
- » Continue Masonry Walls N. of Bldg. E.
- » Continue Door Hardware @ Building A.



Building B Mechanical Room



HUB Interior Buildout

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #110

Douthitt Hills Student Community, Clemson University Project

Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1755	120145
American Deep Foundation	Auger Cast Piles	0	0	6166
Accessories Unlimited	Bathroom Accessories	2	80	595
Baker Roofing	Sheathing and Shingles	2	100	7394
Brightview Landscape Development	Hardscape & Landscape	8	320	7500
Cabinets By Design	Millwork	5	200	1160
Carolina Fire Protection	Sprinklers	10	500	27995
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	4	200	5370
Feltman Brothers	West - Masonry	25	1250	28335
Gainesville Mechanical	Ductwork	2	100	63469
Gill Plumbing	Plumbing	44	2200	45280
Graham Hodge	Glass	4	160	6210
Gregory Electric	Aboveground Electric	10	500	23500
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	18	900	19152
Johnson Controls	Building Controls	11	550	9685
IBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	40	1600	55482
King Asphalt	Asphalt	0	0	4285
Kone	Elevators	4	200	4063
Labor Finders	Labor Force	13	520	47108
Metro Power	Underground Electrical	9	360	24387
Nations Roofing	Roofing	8	320	9875
Old North State Masonry	East - Masonry	0	0	28859
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	0	0	85610

Superintendents Weekly Activity Report #110
Douthitt Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE

[illegible]

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #110

Douthit Hills Student Community, Clemson University Project

Joe Jett




WEATHER


CURRENT WEEK

12


Snow



Actual: 46° | 36°


 MM in

Average: 65° | 40°


 0.12 in

13


Rain



Actual: 45° | 34°


 0.08 in

Average: 65° | 39°


 0.38 in

14


Rain



Actual: 54° | 35°


 0.06 in

Average: 64° | 38°


 0.20 in

15


Clear



Actual: 44° | 28°


 0.00 in

Average: 65° | 37°


 0.09 in

16


Clear



Actual: 57° | 26°


 0.00 in

Average: 64° | 40°


 0.14 in

17


Partly Cloudy



Actual: 63° | 33°


 0.00 in

Average: 63° | 37°


 0.30 in

18


Rain



Forecast: 73° | 42°

 0.0 in

Average: 62° | 37°

 0.15 in

Rain Days This Week = 0


Rain Days To Date = 65

SAFETY REVIEW LOG

Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

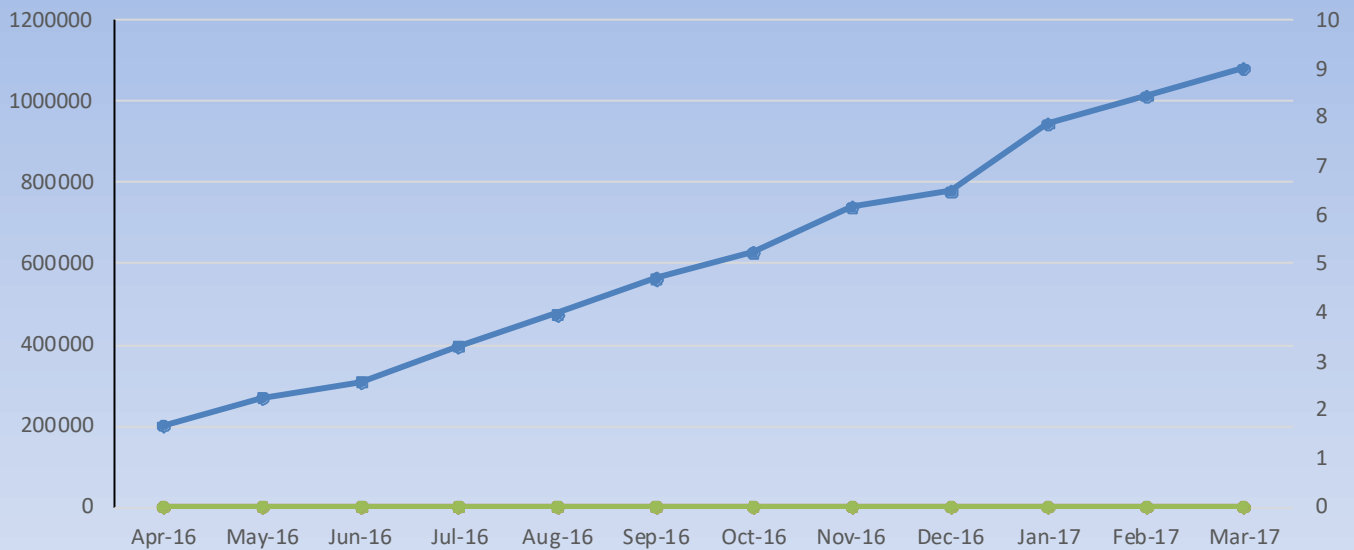

	Apr-16	May-16	Jun-16	Jul-16	Aug-16	Sep-16	Oct-16	Nov-16	Dec-16	Jan-17	Feb-17	Mar-17
— Cumulative Man-Hours	201384	268272	307534	395795	475812	563897	627462	738504	776399	941838	1012338	1081124
— RCR	0	0	0	0	0	0	0	0	0	0	0	0
— DART R	0	0	0	0	0	0	0	0	0	0	0	0





MANPOWER CHART

Douthit Hills Workforce

