

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #5
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 866
- » Total Man Hours on Project: 4188
- » Crafts On Project This Week: 3
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued steam line removal east of water tower
- » Completed water tower removal and haul off
- » Mobilization of foundation removal equipment



Continue Water Tower Demo



Mobilization of Foundation Removal Equipment

- » Began Removal of telephone poles
- » Began installation of jobsite signage

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #5


Douthit Hills Student Community, Clemson University Project

Joe Jett



NEXT WEEK'S ACTIVITIES

- » Mobilization of equipment for foundation removal
- » Begin removal water tower concrete foundation

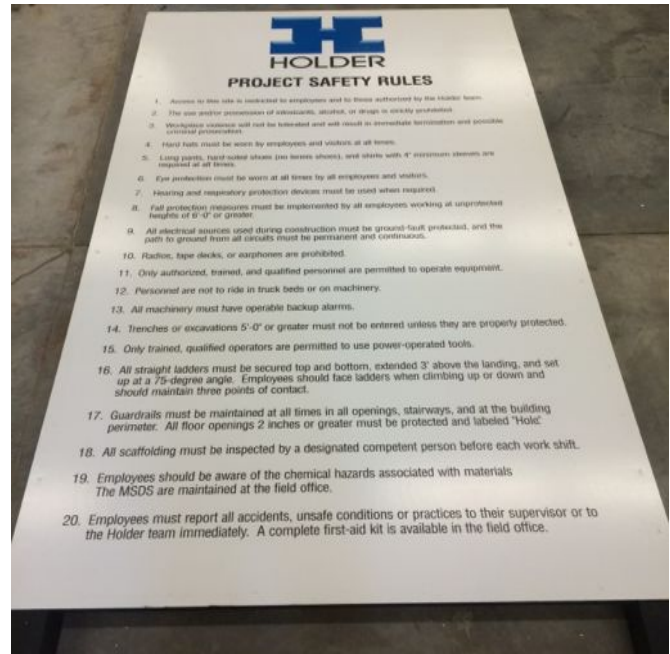

Began Installation of Jobsite Safety Signage



Water Tower Riser Demo

- » Continue removal of steam line east of water tower
- » Begin removal of steam line SE of water tower

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #5
Douthit Hills Student Community, Clemson University Project
Joe Jett



WEATHER


CURRENT WEEK

25	26	27	28	29	30	31
Actual: 57 34 0.00 Average: 51 30 0.30	Actual: 54 35 0.00 Average: 54 30 0.21	Actual: 51 33 0.00 Average: 52 28 0.15	Actual: 52 30 0.00 Average: 52 29 0.06	Actual: 55 30 0.00 Average: 54 30 0.03	Actual: 50 39 0.00 Average: 55 30 0.07	Forecast: 50 36 Average: 55 29 0.11

Rain Days This Week = 0

Rain Days To Date = 3

SAFETY REVIEW LOG

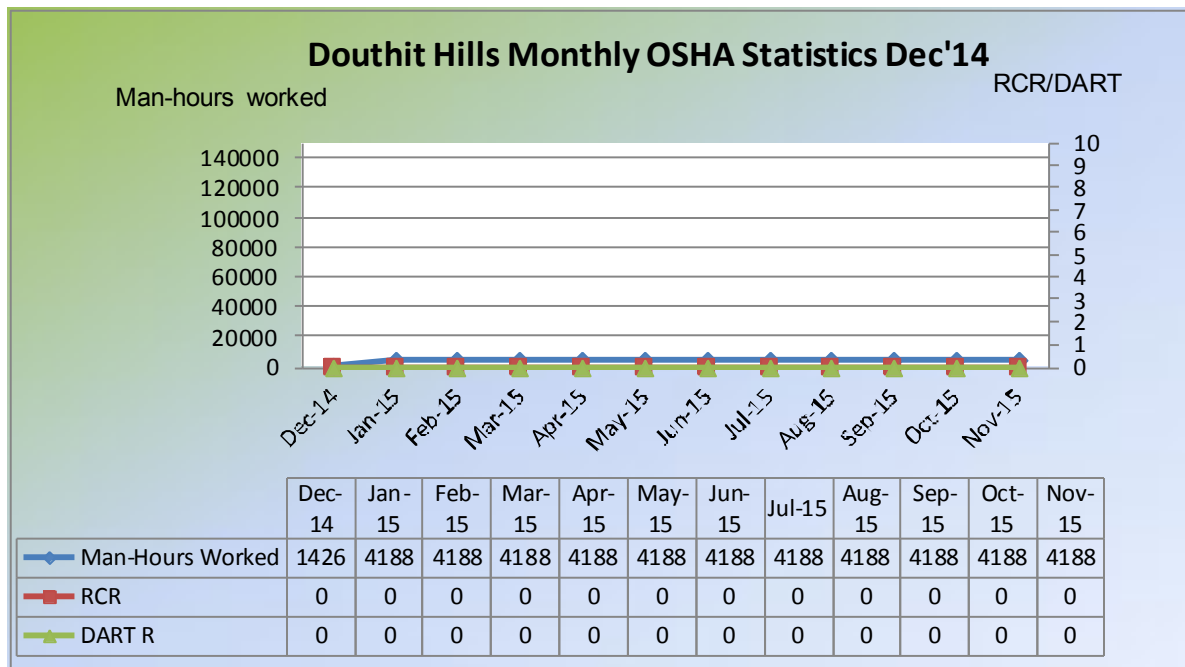

Superintendents Weekly Activity Report #5
Douthitt Hills Student Community, Clemson University Project
Joe Jett



REPORTS



BLE — Soils & Erosion Control Inspections





MANPOWER CHART

