

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #7
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 526
- » Total Man Hours on Project: 5330
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued steam line removal east of water tower
- » Began installation of speed bump signage
- » Began installation of speed bumps on Daniel and Martin street



Speed Bump Signage



Steam Line Removal



NEXT WEEK'S ACTIVITIES

- » Continue removal of steam line
- » Continue installation of speed bumps on Daniel and Martin St.



Began Speed Bump Installation
Signage



Completed Steam Line Removal SE of
Tower

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #7
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Actual Rain	Average High/Low	Average Rain
8	Scattered Clouds	70° 43°	0.00 in	54° 29°	0.13 in
9	Tstorm	59° 52°	1.07 in	53° 26°	0.02 in
10	Partly Cloudy	62° 42°	0.00 in	52° 28°	0.09 in
11	Fog	60° 32°	0.00 in	54° 30°	0.14 in
12	Clear	55° 28°	0.00 in	56° 30°	0.12 in
13	Clear	Forecast: 44° 29°	0.0 in	Average: 55° 31°	0.21 in
14	Clear	Forecast: 58° 24°	0.0 in	Average: 54° 31°	0.22 in

Rain Days This Week = 1

Rain Days To Date = 5

SAFETY REVIEW LOG

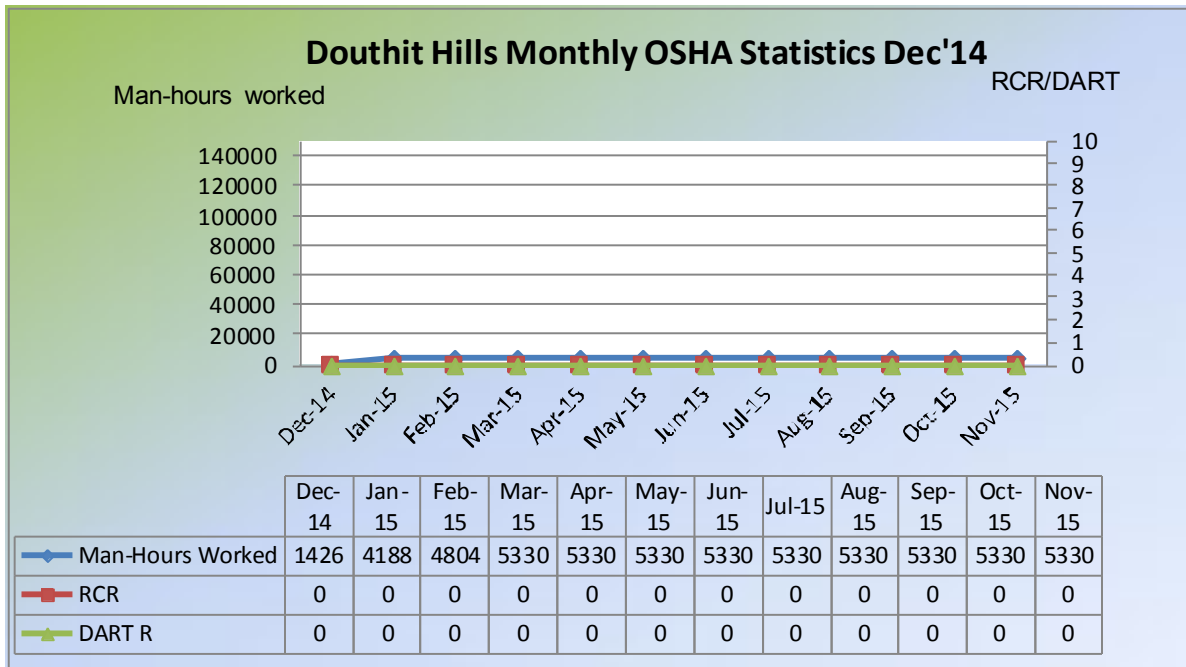

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #7
Douthitt Hills Student Community, Clemson University Project
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	6	260	1640
CNC Fence	Site Fence	0	0	480
Hutch-N-Son	Early Site Work	0	0	600
JBR Construction	Steam Line Removal	5	150	1050
Labor Finders	Labor Force	2	116	810
R.E. Mclean Tank	Tank Demo	0	0	660
D.H. Griffin	Tank Foundation Removal	0	0	90
TOTAL		13	526	5330

REPORTS



INSPECTIONS/TESTING

- DHEC Erosion Control Inspection
- S&ME Steam line Inspections
- BLE — Soils & Erosion Control Inspections





MANPOWER CHART

