



SAFETY

- » Total Man Hours Worked This Week: 1149
- » Total Man Hours on Project: 11570
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued installation of orange tree save on tree protection fence
- » Completed grading and stone at trailer compound
- » Continued mobilization of grading equipment
- » Commenced removal of overhead power lines and poles



Holder Trailer Compound

- » Located and marked existing sanitary sewer lines
- » Commenced installation of silt fence at detention pond area



Located Existing Sewer Line



NEXT WEEK'S ACTIVITIES

- » Continue installation of orange tree save on tree protection fence
- » Continue removal of overhead power lines and poles
- » Continue mobilization of site contractor
- » Continue installation of jobsite erosion control



Installation of Silt fence at Detention Pond



OHP Demolition work

- » Commence installation of electrical duct bank for trailer compound
- » Commence installation of temporary wheel wash at gate #1

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #11
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

26	Scattered Clouds	27	Partly Cloudy	28	Clear	29	Rain	30	Rain	1	Scattered Clouds	2	Clear
Actual: 82° 57°	Actual: 73° 54°	Actual: 72° 50°	Actual: 66° 55°	Actual: 78° 52°	Forecast: 72° 51°	Forecast: 79° 57°	0.00 in	0.00 in	0.00 in	0.0 in	0.0 in	0.0 in	0.0 in
Average: 74° 48°	Average: 74° 49°	Average: 75° 49°	Average: 75° 49°	Average: 75° 51°	Average: 77° 52°	Average: 77° 52°	0.20 in	0.06 in	0.18 in	0.18 in	0.18 in	0.11 in	0.11 in

Rain Days This Week = 0

Rain Days To Date = 11

SAFETY REVIEW LOG

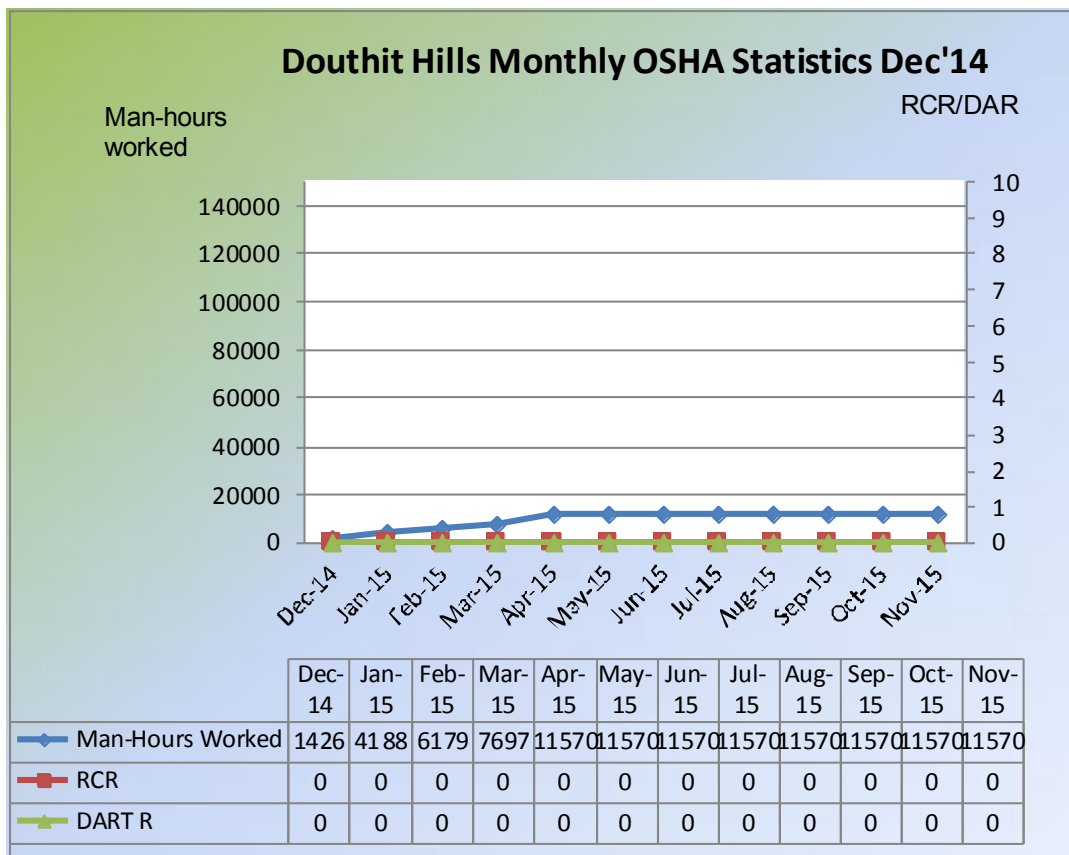



TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	10	550	5361
CNC Fence	Site Fence	0	0	675
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Labor Finders	Labor Force	2	96	1198
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	15	475	475
Hutch-N-Son	Early Site Work	2	20	1045
Tree South	Arborist	2	8	26
TOTAL		31	1149	11570

REPORTS



INSPECTIONS/TESTING

- DHEC Erosion Control Inspection
- S&ME Steam line Inspections
- BLE — Soils & Erosion Control Inspections





MANPOWER CHART

