

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #17
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 2577
- » Total Man Hours on Project: 23057
- » Crafts On Project This Week: 9
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Completed installation of orange tree save on new tree protection fence
- » Continued mobilization and installation of office trailers
- » Continued silt fence and erosion control installation
- » Continued deck build-out for trailer compound
- » Continued cutting grass in tree save areas
- » Commenced installation of head walls and storm pipe at pond location



Mobilized Office Trailers at Compound



Grading and Storm Drain Install at Pond Location

- » Continued grading at pond location
- » Continued hauling off tree mulch from project site
- » Continued hardscape demo on project site
- » Continued water and sewer tie-in at trailer compound
- » Continued electrical hook up at trailer compound
- » Completed clearing and grubbing on project site



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control
- » Continue mobilization of storm water piping
- » Continue hauling off tree mulch
- » Continue mobilization of office trailers
- » Continue temporary power hook up for trailer compound
- » Continue deck build out for trailer compound
- » Continue water and sewer hook up at trailer compound



Continued Deck Build-Out for Trailer Compound



Clearing and Grubbing East

- » Continue grading and storm pipe install at pond location
- » Continue hardscape demo on project site

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #17
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

7	Scattered Clouds	8	Tstorm	9	Tstorm	10	Fog	11	Chance of a Thunderstorm	12	Partly Cloudy	13	Clear
Actual: 89° 71°	Actual: 87° 69°	Actual: 88° 69°	Forecast: 84° 70°	Forecast: 87° 70°	Forecast: 88° 70°	Forecast: 93° 71°	0.00 in	0.22 in	0.58 in	0.0 in	0.11 in	0.0 in	0.0 in
Average: 84° 61°	Average: 84° 61°	Average: 85° 62°	Average: 84° 62°	Average: 85° 61°	Average: 85° 62°	Average: 86° 62°	0.07 in	0.25 in	0.09 in	0.19 in	0.06 in	0.08 in	0.08 in

Rain Days This Week = 2

Rain Days To Date = 15

SAFETY REVIEW LOG

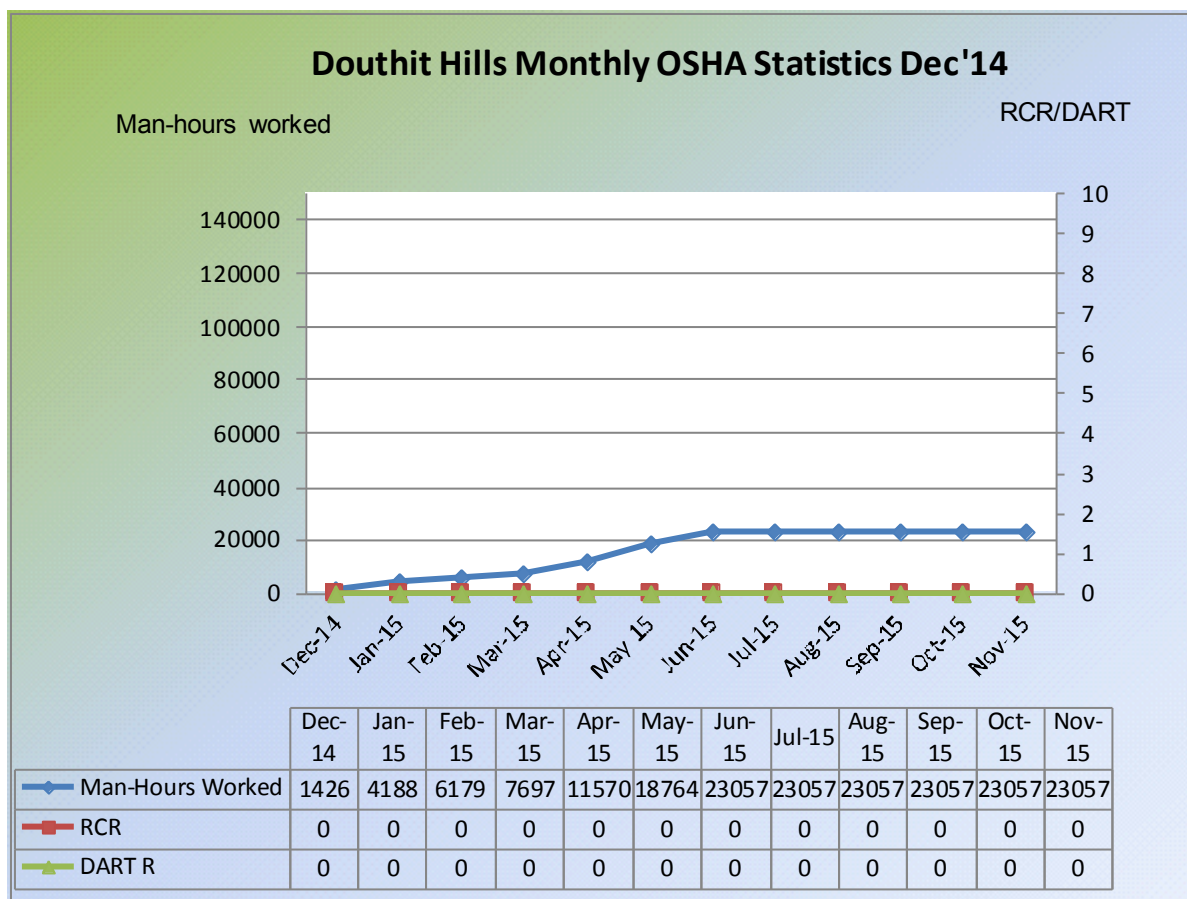



TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	13	620	9378
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	728
Cowart Tree Mulch	Tree Removal	2	100	500
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	2	12	1337
Labor Finders	Labor Force	5	260	1985
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	16	960	4610
RJ Coogan	Deck Installers	3	135	200
Silt Fence Installation	Site Erosion Control	5	50	353
Southern Mechanical Inc.	Electrical/Plumbing	6	240	580
Tree South	Arborist	5	200	316
TOTAL		57	2577	23057

REPORT



DHEC Erosion Control Inspection
BLE — Soils & Erosion Control Inspections





MANPOWER CHART

