

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #23
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 1820
- » Total Man Hours on Project: 36401
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation
- » Continued cutting grass in tree save areas
- » Completed set up of office furniture into trailers
- » Continued demo of warehouse building
- » Continued cut and fill for Building F and G
- » Commenced cut for sewer line #2 install back of Clemson House



Grass at pond Area



Sewer Line #2 install

- » Continued hardscape demo on project site
- » Continued sewer line #2 install
- » Continue storm line #4A install



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control
- » Continue mobilization of storm water piping
- » Continue install of sewer line #2 Back of Clemson House
- » Continue storm line #4A install
- » Continue cut and fill building F and G
- » Continue cut and fill building E



Storm Line #4A install



Cut for Sewer Line #2 install Back of Clemson House

- » Continue hardscape demo on project site
- » Continue demo of warehouse slab on grade
- » Continue cutting grass on site
- » Extend L.O.D. @ East End of Site

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #23
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

19	Scattered Clouds	20	Tstorm	21	Tstorm	22	Clear	23	Scattered Clouds	24	Rain	25	Partly Cloudy
Actual: 95° 73° 0.00 in	Actual: 96° 75° 0.00 in	Actual: 95° 73° 0.18 in	Actual: 93° 73° 0.00 in	Actual: 91° 75° 0.00 in	Actual: 90° 75° 0.01 in	Forecast: 90° 73° 0.0 in							
Average: 90° 67° - in	Average: 91° 68° - in	Average: 91° 68° - in	Average: 91° 68° - in	Average: 90° 68° - in	Average: 89° 67° - in	Average: 89° 68° - in							

Rain Days This Week = 2

Rain Days To Date = 20

SAFETY REVIEW LOG

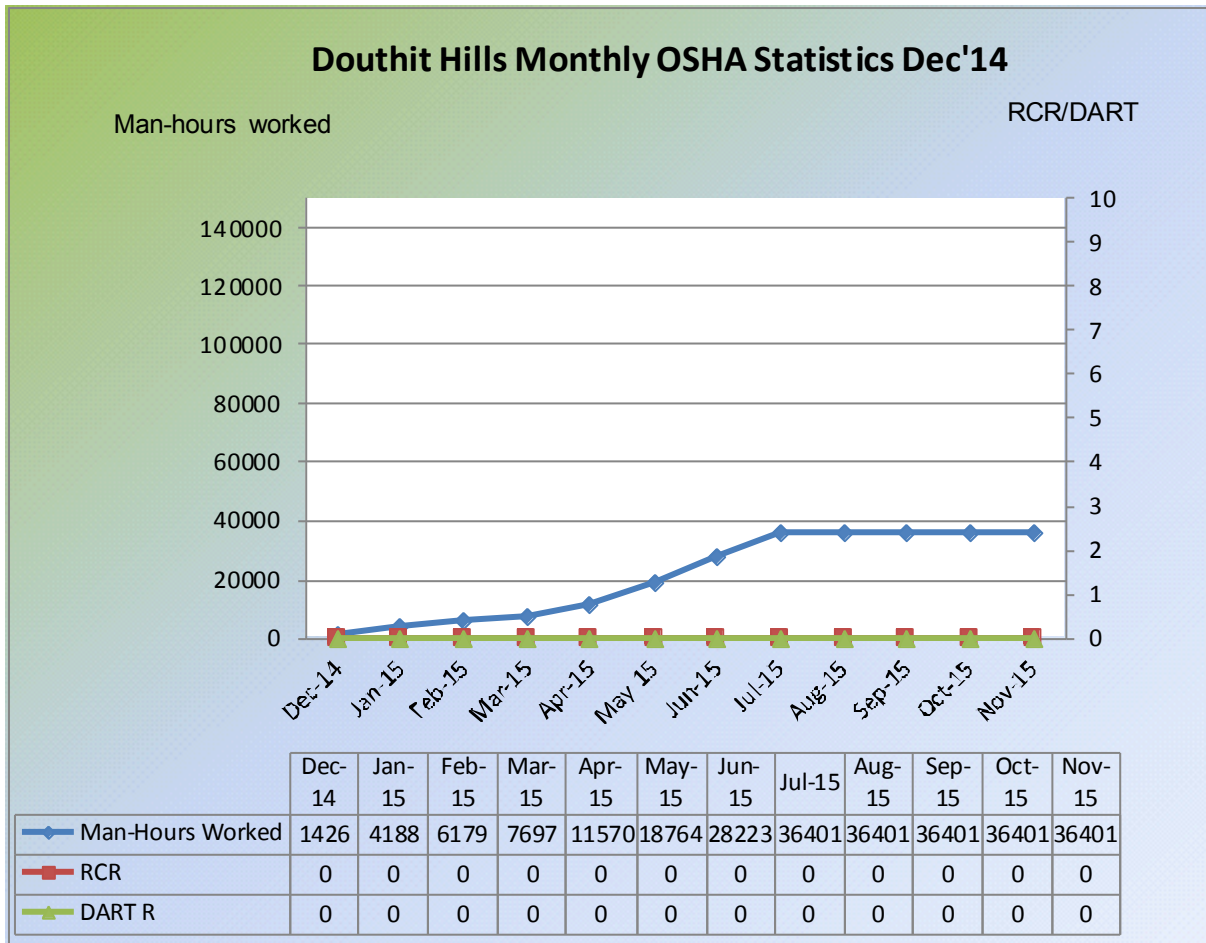

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #23
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	13	650	13298
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	240
Labor Finders	Labor Force	5	210	3633
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	16	960	10160
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	0	0	522
TOTAL		34	1820	36401

REPORT



INSPECTIONS/TESTING

DHEC Erosion Control Inspection





MANPOWER CHART

