

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #26
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 1593
- » Total Man Hours on Project: 41732
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation.
- » Continued cutting grass in tree save areas.
- » Continued preparations for Clemson house student move in.



Starting line up!!!



Newman Rd. entrance

- » Continued hardscape demo on project site
- » Continued sewer line #2 install between structures #1 and #14.
- » Continue storm line #4A install between structures #160 and #163.
- » Installed storm line #5A from structures #803 to #819



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control.
- » Continue mobilization of storm water piping.
- » Continue storm line 5A.
- » Commence mobilization of chiller pipe.
- » Commence tree removal and grading of Daniel Square.



Pond



Pecan Grove

- » Continue hardscape demo on project site.
- » Continue cutting grass on site.
- » Commence mobilization of underground electrical utilities.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #26
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	13	585	15153
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	240
Labor Finders	Labor Force	5	208	4299
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	20	800	12960
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	0	0	532
TOTAL		38	1593	41732

REPORT



INSPECTIONS/TESTING

DHEC Erosion Control Inspection



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #26
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

9 Clear Forecast: 94° 73° 0.0 in Average: 88° 68° 0.04 in	10 Chance of a Thunderstorm Forecast: 93° 73° 0.53 in Average: 89° 67° 0.09 in	11 Chance of a Thunderstorm Forecast: 93° 72° 0.11 in Average: 88° 67° 0.21 in	12 Clear Forecast: 93° 71° 0.0 in Average: 86° 67° 0.16 in	13 Clear Forecast: 92° 70° 0.0 in Average: 86° 66° 0.18 in	14 Partly Cloudy Forecast: 92° 70° 0.06 in Average: 86° 66° 0.11 in	15 Record: 100° 57° 1.73 in Average: 87° 66° 0.10 in
--	---	---	---	---	--	---

Rain Days This Week = 0

Rain Days To Date = 22

SAFETY REVIEW LOG

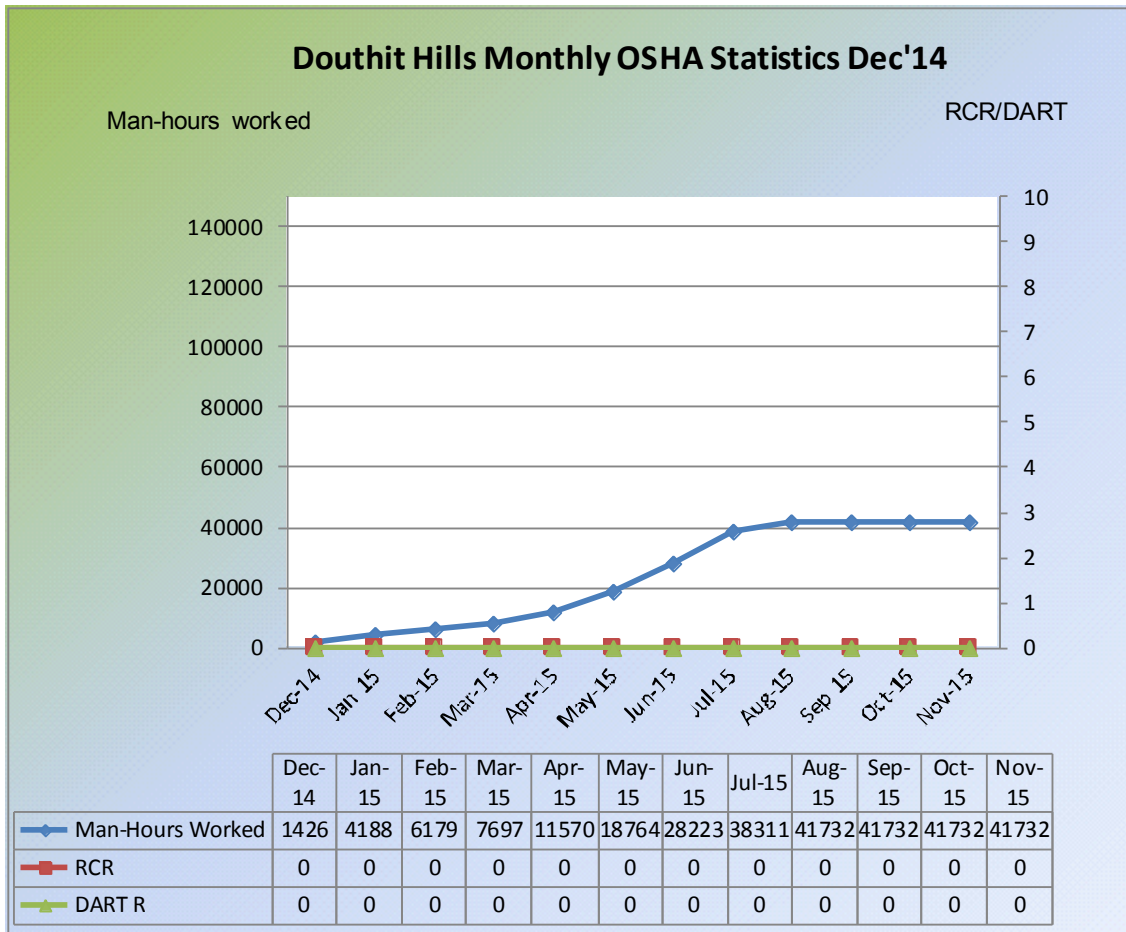

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #26
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

