

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #24
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 1910
- » Total Man Hours on Project: 38311
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation
- » Continued cutting grass in tree save areas
- » Continued Grading East Parking Lot
- » Started Grading East Entrance



Grass at pond Area



Overall Project Site

- » Continued hardscape demo on project site
- » Continued sewer line #2 install
- » Continue storm line #4A install



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control
- » Continue mobilization of storm water piping
- » Continue install of sewer line #2 to re-route Clemson House
- » Continue storm line #4A install East Spine



East Area View



Storm Line #4A install

- » Continue hardscape demo on project site
- » Continue cutting grass on site
- » Continue grading @East Parking
- » Continue grading @ East Entrance

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #24
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

26 Scattered Clouds Actual: 93° 73° 0.00 in Average: 88° 68° 0.18 in	27 Rain Actual: 96° 75° 0.09 in Average: 89° 68° 0.08 in	28 Tstorm Actual: 93° 75° 0.00 in Average: 90° 68° 0.19 in	29 Tstorm Actual: 96° 75° 0.00 in Average: 89° 68° 0.20 in	30 Scattered Clouds Actual: 98° 75° 0.00 in Average: 89° 67° 0.23 in	31 Partly Cloudy Forecast: 94° 71° 0.0 in Average: 88° 66° 0.16 in	1 Clear Forecast: 93° 69° 0.0 in Average: - - 0.11 in
---	---	---	---	---	---	--

Rain Days This Week = 1

Rain Days To Date = 21

SAFETY REVIEW LOG

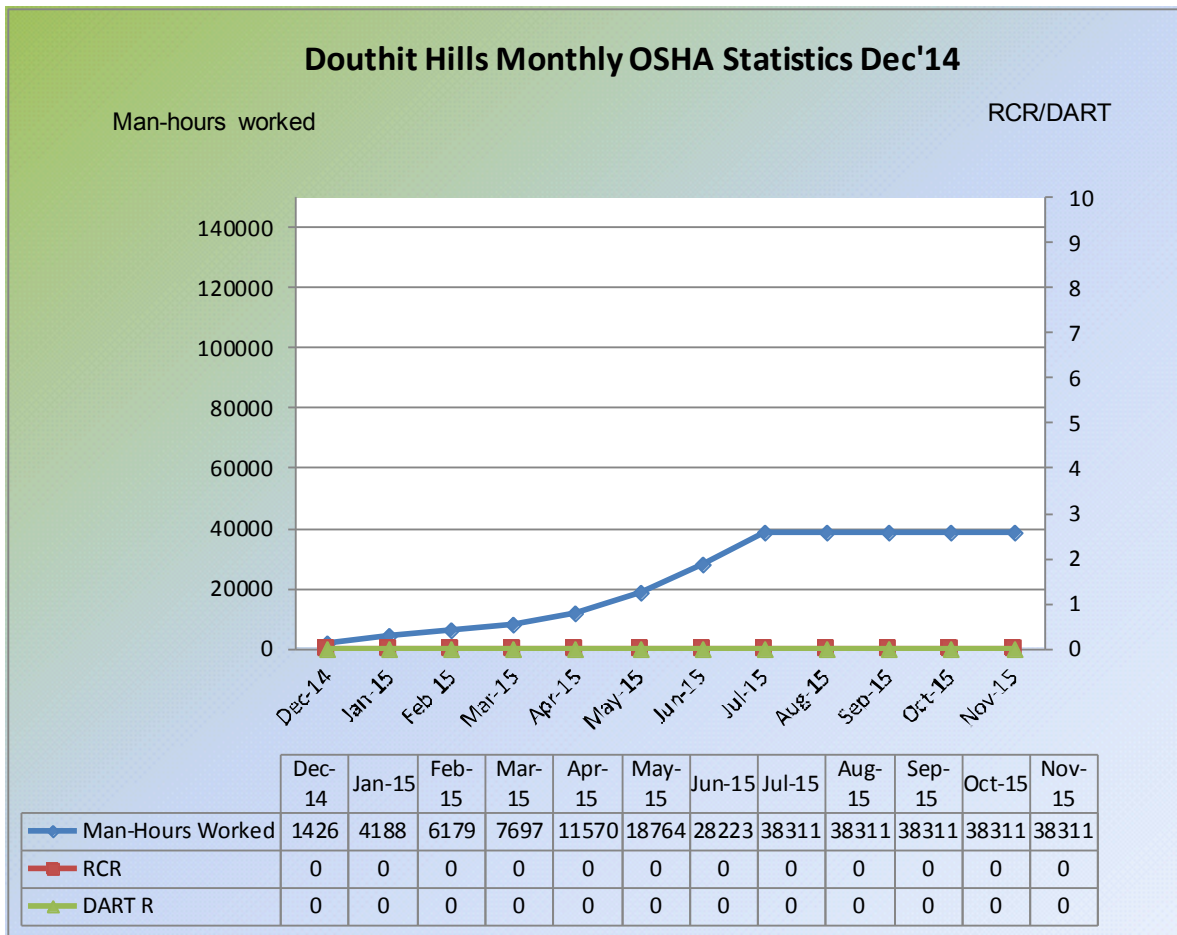

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #24
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	14	650	13948
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	240
Labor Finders	Labor Force	5	250	3883
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	20	1000	11160
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	1	10	532
TOTAL		40	1910	38311

REPORT



INSPECTIONS/TESTING

DHEC Erosion Control Inspection



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #24
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

