

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #27
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 1993
- » Total Man Hours on Project: 43725
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation.
- » Continued cutting grass in tree save areas.
- » Continued installation on sewer line #1



Clearing New Daniel Square entrance



Pecan Grove

- » Commenced electrical underground installation east of Newman rd. entrance.
- » Commenced Tree removal at new Daniel square entrance.
- » Commenced Chill water pipe installation at Building G pad.



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control.
- » Continue installation of storm water piping.
- » Continue storm line 5A.
- » Continue installation of chiller pipe.
- » Commence tree removal and grading of Daniel Square.



Starting Underground Electrical Conduit



Back filled gate one for construction entrance.

- » Continue hardscape demo on project site.
- » Continue cutting grass on site.
- » Continue installation of underground electrical utilities.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #27
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	13	585	15738
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	240
Labor Finders	Labor Force	5	208	4507
Metro Power	Underground Electrical	4	120	120
Ostein	Chill Water pipe	5	160	160
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	20	800	13760
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	0	0	532
Valley Farm Construction	Tree removal/Grading	3	120	120
TOTAL		50	1993	43725

REPORT



INSPECTIONS/TESTING

DHEC Erosion Control Inspection

August 23, 2015

Page | 4



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #27

Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


CURRENT WEEK

16	Clear	17	Rain	18	Tstorm	19	Tstorm	20	Rain	21	Clear	22	Chance of a Thunderstorm
Actual: 90° 70° 0.00 in	Actual: 87° 71° 0.63 in	Actual: 84° 71° 0.52 in	Actual: 88° 73° 0.51 in	Actual: 89° 73° 0.00 in	Forecast: 87° 72° 0.03 in	Forecast: 86° 71° 0.16 in							
Average: - - - in	Average: - - - in	Average: - - - in	Average: - - - in	Average: - - - in	Average: - - - in	Average: - - - in							

Rain Days This Week = 2

Rain Days To Date = 24

SAFETY REVIEW LOG

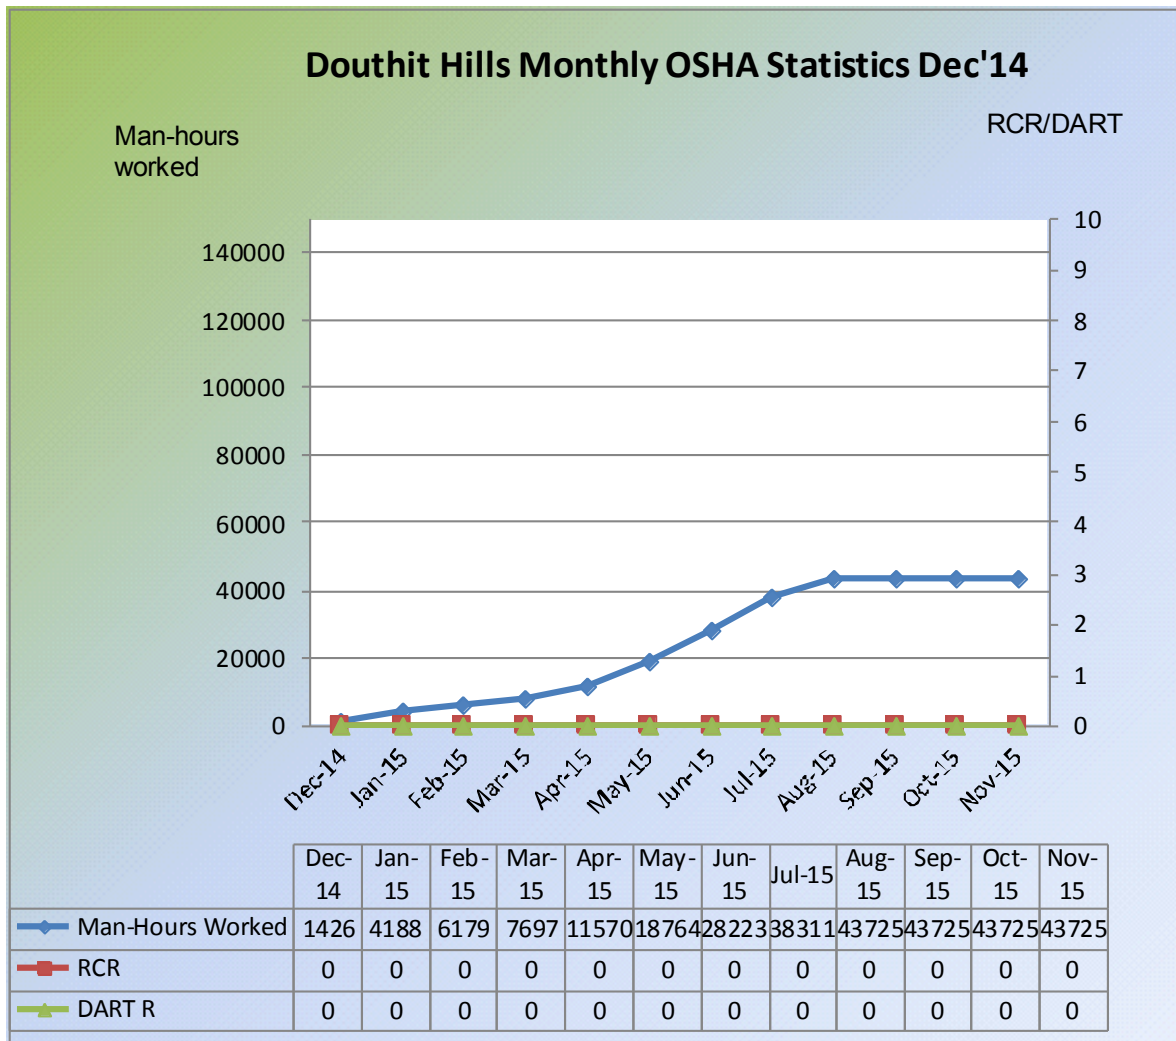

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #27
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

