

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #25
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 1828
- » Total Man Hours on Project: 40139
- » Crafts On Project This Week: 2
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation at Daniel square.
- » Continued cutting grass in tree save areas.
- » Commenced grading for Newman drive entrance.



Grading for Newman Rd. entrance.



Installed structure #16 on sewer line #2.

- » Continued on office compound improvements
- » Continued sewer line #2 install
- » Continued storm line #4A install



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control
- » Continue mobilization of storm water piping
- » Continue install of sewer line #2 Back of Clemson House
- » Continue storm line #4A install



Storm drain inlet protection.



Installing sewer line between structure #16 and #15.

- » Continue hardscape demo on project site
- » Continue cutting grass on site

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #25
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

2	Clear	3	Clear	4	Clear	5	Clear	6	Chance of a Thunderstorm	7	Partly Cloudy	8	Clear
Actual: 95° 69° 0.00 in		Actual: 98° 72° 0.00 in		Actual: 100° 73° 0.00 in		Forecast: 96° 73° 0.07 in		Forecast: 89° 71° 0.56 in		Forecast: 92° 71° 0.06 in		Forecast: 92° 72° 0.0 in	
Average: - - - in		Average: - - - in		Average: - - - in		Average: - - - in		Average: - - 0.15 in		Average: - - 0.32 in		Average: - - 0.26 in	

Rain Days This Week = 1

Rain Days To Date = 22

SAFETY REVIEW LOG

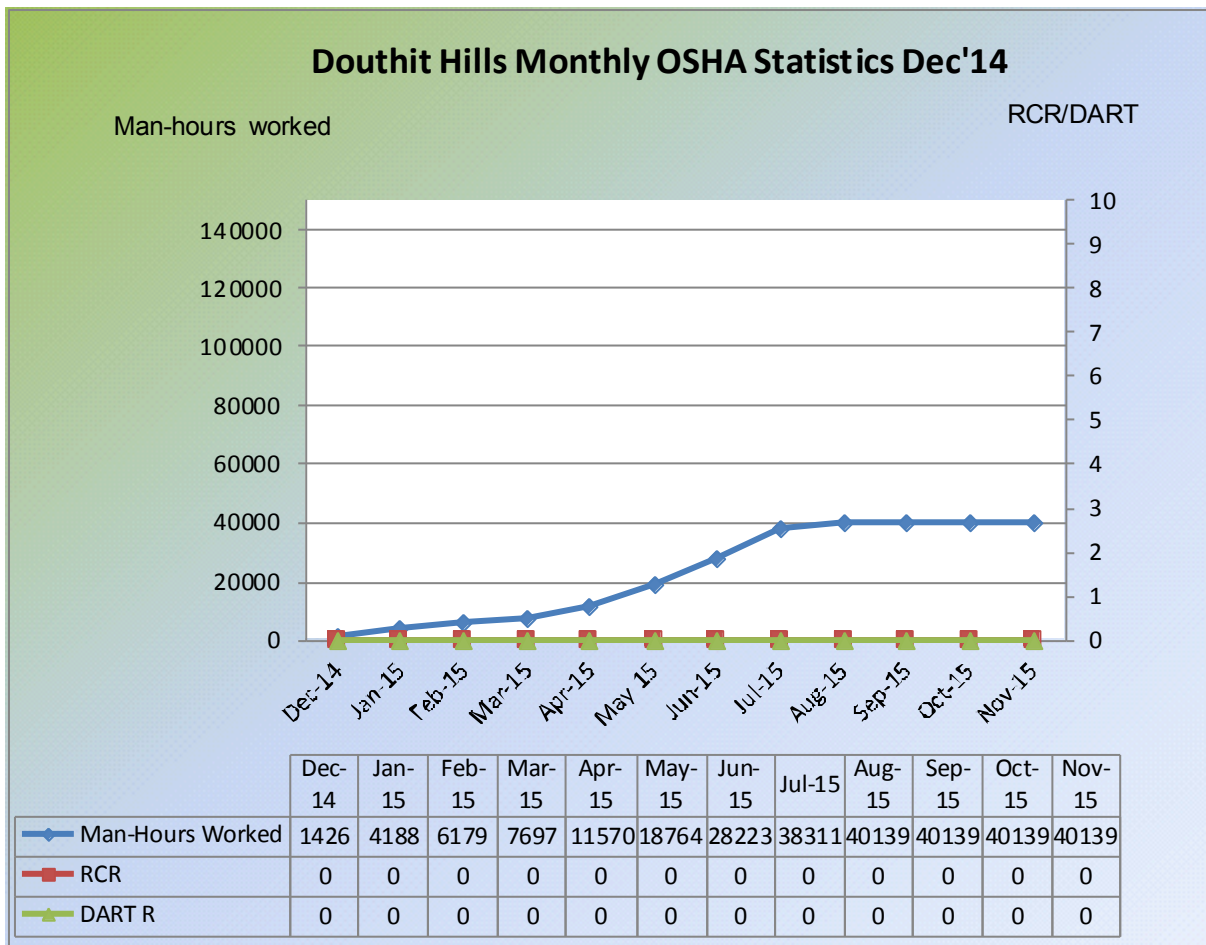

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #25
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

