

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #30  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 2166
- » Total Man Hours on Project: 51,070
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation as needed.
- » Continued cutting grass in tree save areas.
- » Continued electrical underground installation North of the East parking lot.
- » Continued installation of storm lines 3, 4B & 5B.



Underground Electrical Conduit near Building G pad.



Additional erosion control added at Daniel Square entrance

- » Commenced spreading top soil on Pecan Grove.
- » Commenced underground electrical near building G pad.
- » Commenced layout of building G.





## NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control as needed.
- » Continue installation of storm line 4B and 3 near Gate 1.
- » Continue spreading top soil at Pecan Grove.
- » Continue installation of Storm Line 5A near Newman Rd. intersection.
- » Continue installation of underground electrical utilities near building G pad.



Installation of jobsite erosion control near trailer compound.



Spreading of top soil on Pecan Grove.

- » Continue cutting grass on site.
- » Continue installation of utilities for the wheel wash at construction Gate 1 .
- » Commence spreading top soil at new Daniel Square entrance.
- » Commence rough grading of Newman temporary Road over Storm Line 5A

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #30  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	15	675	17628
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	748
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	608
Labor Finders	Labor Force	5	200	5107
Metro Power	Underground Electrical	6	203	788
Ostein	Chill Water pipe	0	0	480
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	22	1056	16928
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	2	32	588
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>50</b>	<b>2166</b>	<b>51070</b>

## REPORT



### INSPECTIONS/TESTING

DHEC Erosion Control Inspection



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #30  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER


### CURRENT WEEK

6 Partly Cloudy	7 Partly Cloudy	8 Rain	9 Tstorm	10 Tstorm	11 Fog	12 Partly Cloudy
Actual: 89°   72° 0.00 in	Actual: 88°   70° 0.01 in	Actual: 88°   72° 0.89 in	Actual: 79°   73° 2.07 in	Actual: 88°   72° 0.00 in	Forecast: 84°   67° 0.12 in	Forecast: 80°   57° 0.0 in
Average: 84°   63° 0.10 in	Average: 84°   63° 0.12 in	Average: 84°   63° 0.27 in	Average: 85°   62° 0.07 in	Average: 84°   62° 0.05 in	Average: 83°   60° 0.12 in	Average: 84°   61° 0.11 in

Rain Days This Week = 1

Rain Days To Date = 23

### SAFETY REVIEW LOG

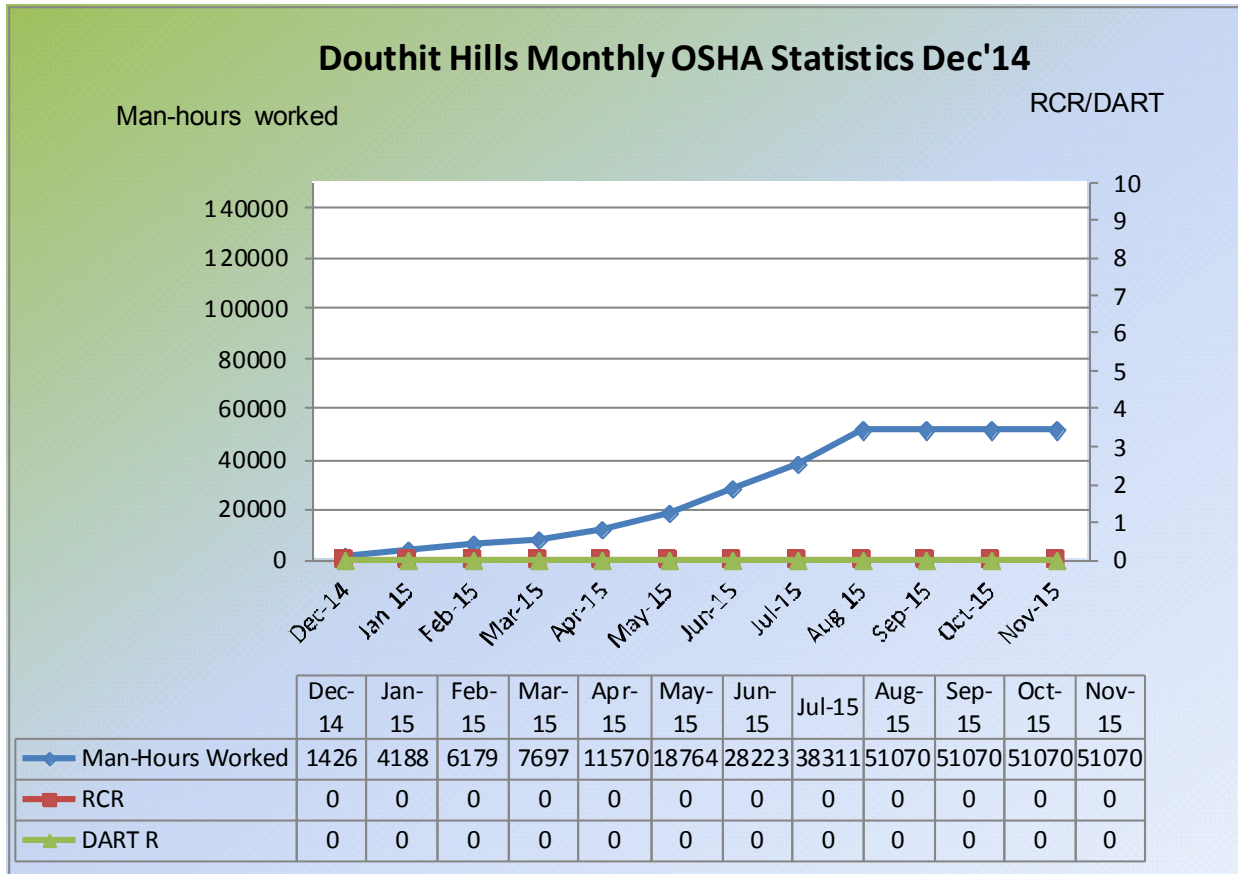

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #30  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

