

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #32
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 2337
- » Total Man Hours on Project: 55,734
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Installed North berms.
- » Paved construction entrance at Gate 1.
- » Installed domestic water from the existing line at Highway 93 to hydrant #1.
- » Performed and passed all bacteria and hydro static testing for Domestic water installed.
- » Completed installation of Storm Line 3 and 4B near Gate 1 and the East zone.
- » Seeded, hayed and stabilized the Daniel Sq. entrance.
- » Commenced duct bank install for the Gate 1 truck wash.
- » Commenced rough grading for Southern portion of the HUB.



Asphalt paving at construction Gate 1.



Installed two berms along the North side of the site.

- » Continued installation of crane roads for Building F and G.
- » Continued excavation for the Eastern portion of building G and the basement.
- » Continued electrical underground installation North of the East lot from manhole #11 to #12.
- » Continued underground electrical from building G to manhole #10.
- » Continued silt fence and erosion control installation as needed.
- » Continued cutting grass in tree save areas.



NEXT WEEK'S ACTIVITIES

- » Complete installation truck wash temporary power.
- » Commence install of traffic lights and camera for construction Gate 1.
- » Commence excavation for Building G footings and elevator pit area.
- » Commence pouring elevator slab for Building G.
- » Commence rough grading for East lot.
- » Clean out mud from the bottom of the detention pond.



Continued installation of East zone crane and access roads.



Installation of underground electrical North of East parking lot.

- » Continue installation of storm line 5B.
- » Continue installation of East zone crane and access roads for Building E.
- » Continue installation of underground electrical utilities near building G pad.
- » Continue installation of underground electrical from manhole #12 to #13.
- » Continue cutting grass on site.
- » Continue installation of jobsite erosion control as needed.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #32
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	17	765	19113
American Deep Foundation	Auger cast piles	0	0	280
CNC Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	682
Labor Finders	Labor Force	6	220	5527
Metro Power	Underground Electrical	6	240	1233
Osteen	Chill Water pipe	0	0	480
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	22	1056	19040
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	603
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	2	56	700
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		53	2337	55734



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #32
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Precipitation	Average High/Low	Average Precipitation
20	Scattered Clouds	90° 68°	0.00 in	82° 61°	0.07 in
21	Partly Cloudy	82° 69°	0.00 in	82° 61°	0.11 in
22	Partly Cloudy	79° 68°	0.00 in	82° 58°	0.23 in
23	Scattered Clouds	81° 66°	0.00 in	80° 57°	0.13 in
24	Rain	75° 61°	0.33 in	80° 56°	0.07 in
25	Rain	Forecast: 67° 63°	0.37 in	Average: 78° 56°	0.20 in
26	Chance of Rain	Forecast: 70° 64°	0.03 in	Average: 78° 57°	0.16 in

Rain Days This Week = 2

Rain Days To Date = 25

SAFETY REVIEW LOG

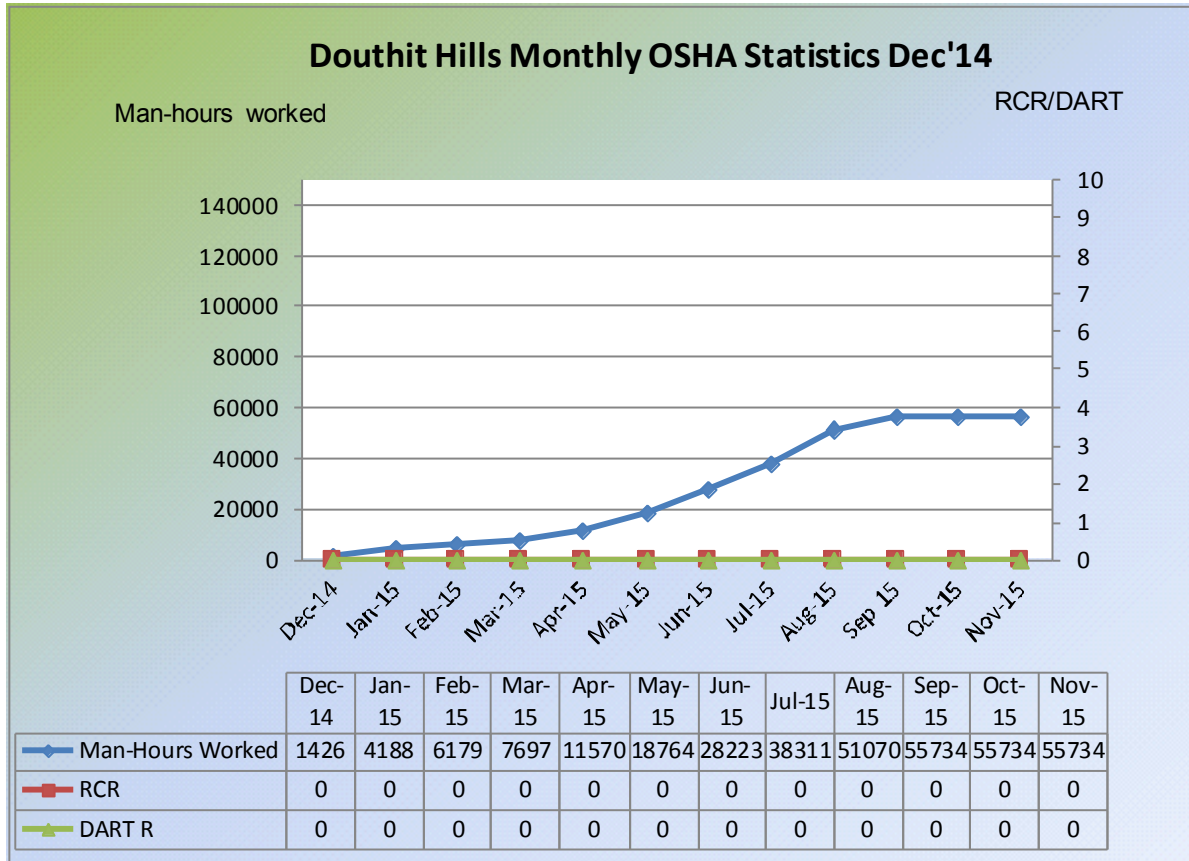

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #32
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

