

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #29
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 2873
- » Total Man Hours on Project: 48904
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued silt fence and erosion control installation as needed.
- » Continued cutting grass in tree save areas.
- » Continued electrical underground installation North of the East parking lot.
- » Completed the installation of chilled water pipe at East Zone
- » Continued and complete all of the vacuum testing on Sanitary Sewer line 2..
- » Continue rough grading of Newman temporary Road.



The starting line up.



Asphalt Paving and striping at new Daniel Square entrance

- » Commenced asphalt paving at the new Daniel square entrance.
- » Commenced final grading of Pecan Grove.
- » Commenced installation of storm line 5B & 3.



NEXT WEEK'S ACTIVITIES

- » Continue installation of jobsite erosion control.
- » Continue installation of storm line 5B, 4B and 3.
- » Continue final grading of Pecan Grove and then seed & hay once complete
- » Continue rough grading of Newman temporary Rd.



Continue Underground Electrical Conduit



Rough Grading for Newman temporary Rd.

- » Continue cutting grass on site.
- » Continue installation of construction Gate 1 utilities.
- » Continue installation of underground electrical utilities.
- » Commence final grading at Daniel Square entrance.


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #29
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK



Rain Days This Week = 0

Rain Days To Date = 22

SAFETY REVIEW LOG

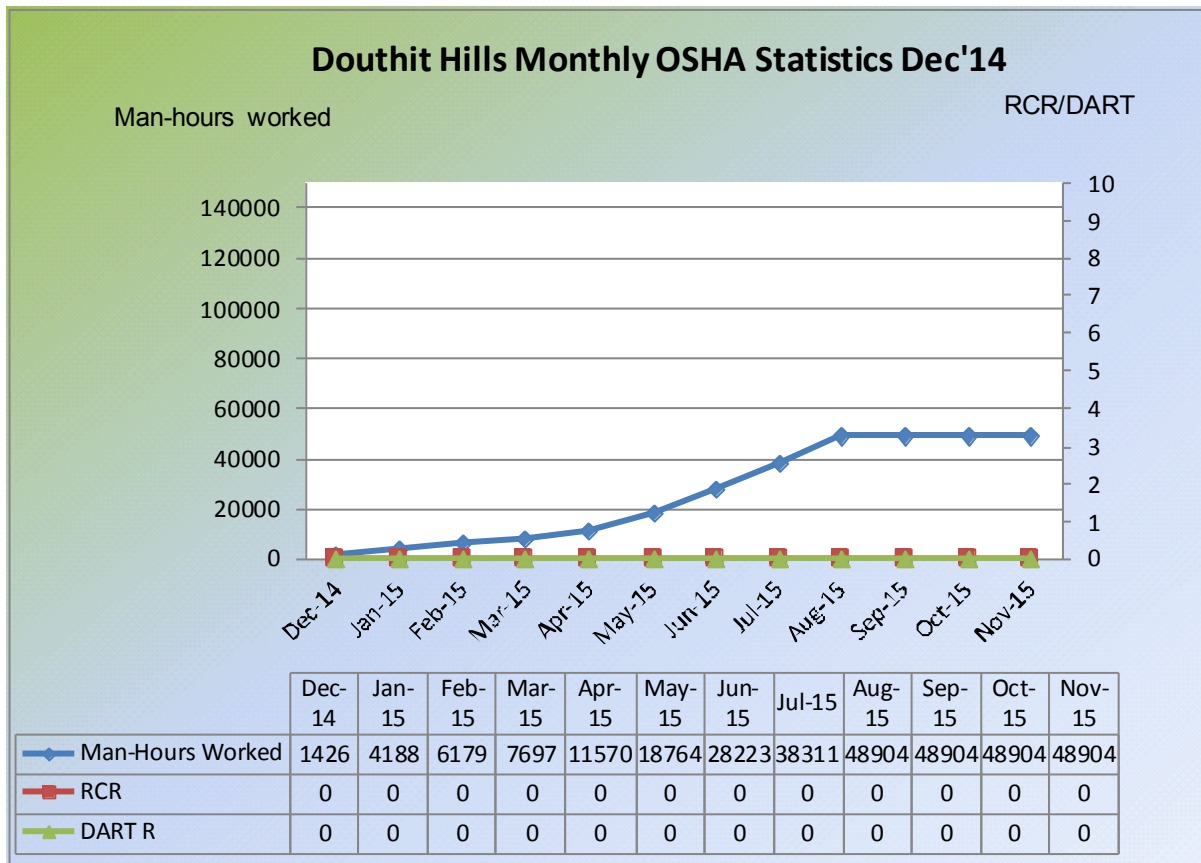

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #29
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

