

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #36  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 3895
- » Total Man Hours on Project: 67312
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

- » Completed grading Hub Building Pad.
- » Completed installation of Storm Line 2.
- » Completed Sanitary Sewer Line 2.
- » Completed Storm Line 6A.



Newman Road preparation and grading.



Continued forming basement walls of Building G.

- » Continued grading at West Zone.
- » Poured footings at level 1 Building G.
- » Poured walls at basement of Building G.
- » Continued silt fence and erosion control installation as needed.
- » Continued cutting grass in tree save areas.





## NEXT WEEK'S ACTIVITIES

- » Continue grading East lot.
- » Continue base and pour curb & gutter at Newman road and east lot.
- » Continue water line installation at North Lot.
- » Commence chill water installation at west zone.
- » Continue installation of East zone access roads for Building E.



Excavation of West Zone.



Completed Building G basement south wall.

- » Continue waterproofing of Building G walls and footings.
- » Continue excavating, forming and pouring footings at Building G west side.
- » Continue installation of underground electrical from manhole #11 to #9.
- » Continue cutting grass on site.
- » Continue installation of jobsite erosion control as needed.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #36  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	19	855	22443
American Deep Foundation	Auger cast piles	0	0	280
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	682
Labor Finders	Labor Force	8	360	6719
Metro Power	Underground Electrical	7	406	2323
Osteen	Chill Water pipe	5	50	550
Precision	Concrete	20	960	2210
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	25	1200	22630
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	4	32	635
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	2	32	764
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>90</b>	<b>3895</b>	<b>67312</b>



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #36  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER


### CURRENT WEEK

Day	Weather	Actual High/Low	Actual Precip	Average High/Low	Average Precip
18	Clear	64°   43°	0.00 in	72°   47°	0.14 in
19	Clear	64°   41°	0.00 in	72°   46°	0.28 in
20	Fog	68°   42°	0.00 in	71°   45°	0.04 in
21	Fog	73°   44°	0.00 in	70°   45°	0.08 in
22	Clear	81°   48°	0.00 in	71°   45°	0.19 in
23	Clear	Forecast: 81°   55°	Forecast: 0.0 in	Average: 70°   45°	0.14 in
24	Overcast	Forecast: 75°   58°	Forecast: 0.0 in	Average: 69°   46°	0.06 in

Rain Days This Week = 0

Rain Days To Date = 29

## SAFETY REVIEW LOG

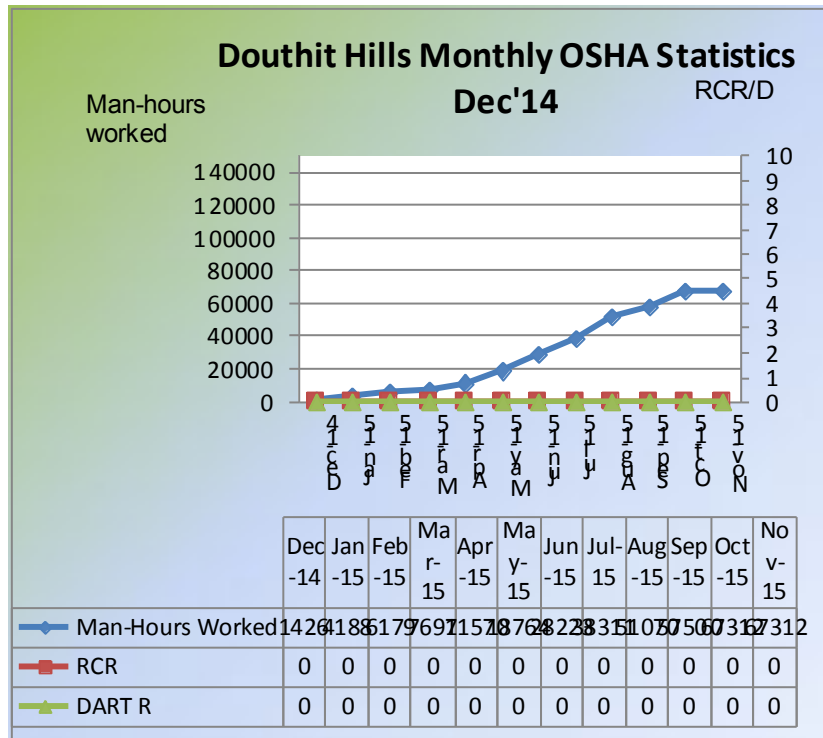

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #36  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

