

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #40
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: **3275**
- » Total Man Hours on Project: **78376**
- » Crafts On Project This Week: 8
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Continued grading at East Lot
- » Continued base for curb & gutter at East Lot.
- » Continued Precast Installation at Building G
- » Installed aggregate base at North and East Lots and the temporary road.
- » Continued installation of underground detention system at North West Lot.
- » Continued deep foundations at HUB Building.



Precast panels at Building G



Footings at Building F

- » Continued water proofing of Building G walls and footings.
- » Excavated, formed, poured and backfilled footings at Building G west side.
- » Continued installation of underground electrical from Manhole 9 to Manhole 8..
- » Began Building F continuous footings.
- » Opened Daniel Square North Entry.



NEXT WEEK'S ACTIVITIES

- » Complete paving the Phase 2 Public Access road from Hwy 93 to Bradley Street.
- » Continue Manholes 9 to 8.
- » Continue underground detention at North West Lot.
- » Continue precast at Building G.
- » Continue base and Curb & Gutter @ East Lot.
- » Begin grout and continue welding of Pre-Cast @ Building G.



Paving East Lot



East Lot preparation for paving

- » Continue deep foundations at the HUB Building
- » Continued Grading at West Zone.
- » Continue waterproofing and backfill at Building G.
- » Complete footings at Building G and continue Building F.
- » Continue on elevator pit at Building F.
- » Install MH5 E & C.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #40
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	20	800	25483
American Deep Foundation	Auger cast piles	8	360	1120
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Crane Erection	10	490	1108
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	17	417	1259
Labor Finders	Labor Force	9	405	7737
Metro Power	Underground Electrical	7	395	3610
Osteen	Chill Water pipe	0	0	550
Precision	Concrete	13	50	3572
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	15	767	24277
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	0	0	635
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	1	8	829
Upstate Curb	Curb and Gutter			120
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		100	3275	78376



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #40
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

15	Clear		16	Fog		17	Rain		18	Rain		19	Rain		20	Clear		21	Partly Cloudy	
Actual: 60° 37°		Actual: 64° 35°		Actual: 66° 53°		Actual: 66° 51°		Actual: 75° 57°		Forecast: 68° 42°		Forecast: 58° 41°		Forecast: 68° 42°		Forecast: 58° 41°		Forecast: 58° 41°		
0.00 in		0.00 in		0.00 in		0.89 in		0.76 in		0.0 in		0.0 in		0.0 in		0.0 in		0.0 in		
Average: 60° 36°		Average: 63° 37°		Average: 63° 38°		Average: 63° 39°		Average: 63° 39°		Average: 62° 40°		Average: 62° 40°		Average: 61° 38°		Average: 61° 38°		Average: 61° 38°		
0.16 in		0.07 in		0.10 in		0.19 in		0.07 in		0.12 in		0.12 in		0.11 in		0.11 in		0.11 in		

Rain Days This Week = 1

Rain Days To Date = 35

SAFETY REVIEW LOG

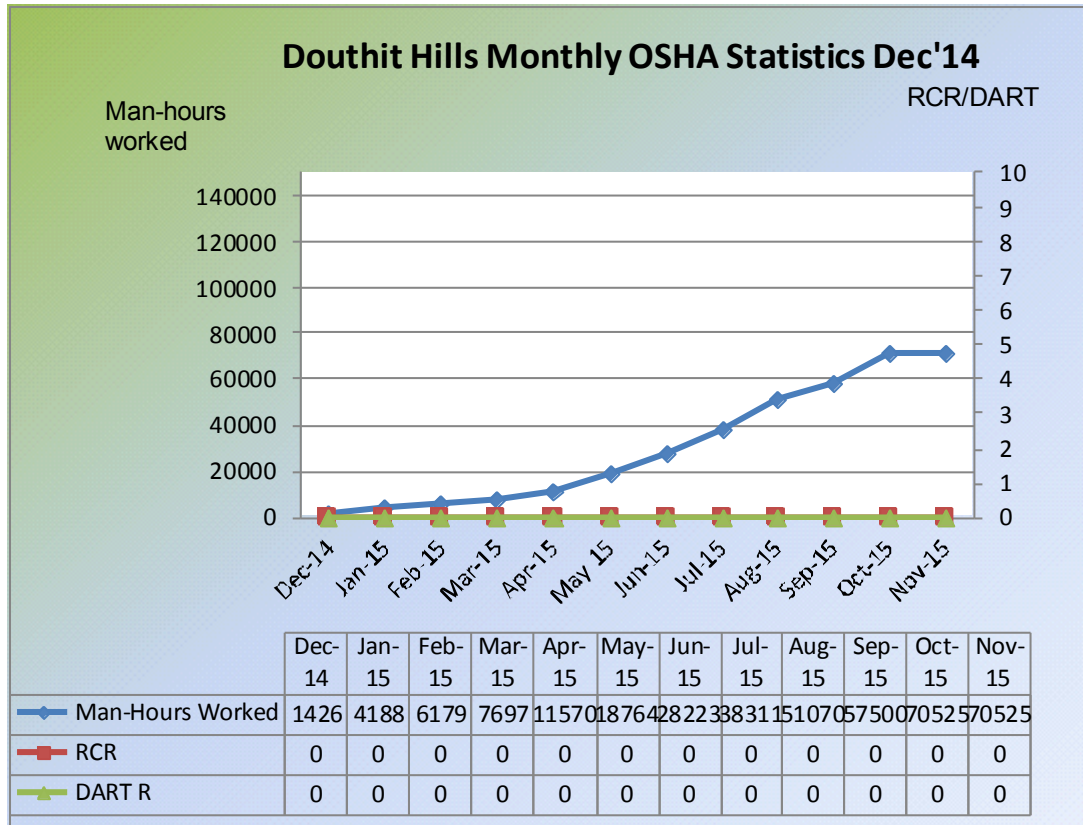

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #40
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

