

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #41
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 3810
- » Total Man Hours on Project: 83933
- » Crafts On Project This Week: 4
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Began Tree Removal @ Kite Hill
- » Completed Storm 4A @ Bldg F
- » Opened Phase 2 Access Rd and Captured Daniel Dr/Martin St
- » Installed Fence @ Phase 2 Rd and removed fence @ Daniel/Martin Streets
- » Installed Duct bank From MH8 to MH9 & Set MH7E&C



Hydro seeding at Newman Road



Footings and Stem Walls at Building F

- » Began Underground Lighting Circuit @ Newman Road
- » Poured Footings/Stem Walls @ Bldg G
- » Continued Pre-Cast Install @ Sequence 2 of Bldg G
- » Installed Deep Foundations @ Hub Bldg- Area 1



NEXT WEEK'S ACTIVITIES

- » Grade Top of Pond
- » Complete Tree Removal @ Kite Hill
- » Continue Underground Detention System @ North West Lot
- » Continue Grading @ West Zone
- » Complete Daniel/Martin Demolitions
- » Continue Deep Foundations @ HUB Bldg Area 2



Striping At Newman Road



Northeast Parking Lot

- » Install Duct Bank From MH5E&C to Bldg C
- » Continue Underground Lighting Circuit @ Newman Road
- » Continue Curb & Gutter @ East Lot
- » Continue Pre-Cast Sequence 2 @ Bldg G
- » Start Trusses @ Bldg G
- » Continue Footings & Retaining Wall @ Bldg F

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #41
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	20	800	27083
American Deep Foundation	Auger cast piles	9	432	1552
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Crane Erection	10	480	1868
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	2	5	1147
Labor Finders	Labor Force	9	405	8430
Metro Power	Underground Electrical	13	413	4022
Osteen	Chill Water pipe	0	0	550
Precision	Concrete	14	672	4724
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	14	546	24823
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Silt Fence Installation	Site Erosion Control	4	32	667
Southern Mechanical Inc.	Electrical/Plumbing	0	0	1140
Tree South	Arborist	2	25	871
Upstate Curb	Curb and Gutter	0	0	120
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		97	3810	83933



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #41
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRE

30	Rain		1	Rain		2	Rain		3	Clear		4	Fog		5	Clear			
Actual: 62° 53°	Actual: 55° 51°	Actual: 62° 48°	Actual: 53° 41°	Forecast: 55° 38°	Forecast: 59° 37°	0.19 in	0.42 in	0.53 in	0.00 in	0.0 in	0.0 in	0.18 in	0.0 in	0.0 in	0.16 in	0.12 in	0.21 in	0.07 in	0.22 in
Average: 58° 34°	Average: 57° 34°	Average: 57° 34°	Average: 56° 35°	Average: 57° 33°	Average: 57° 32°														

Rain Days This Week = 0

Rain Days To Date = 34

SAFETY REVIEW LOG

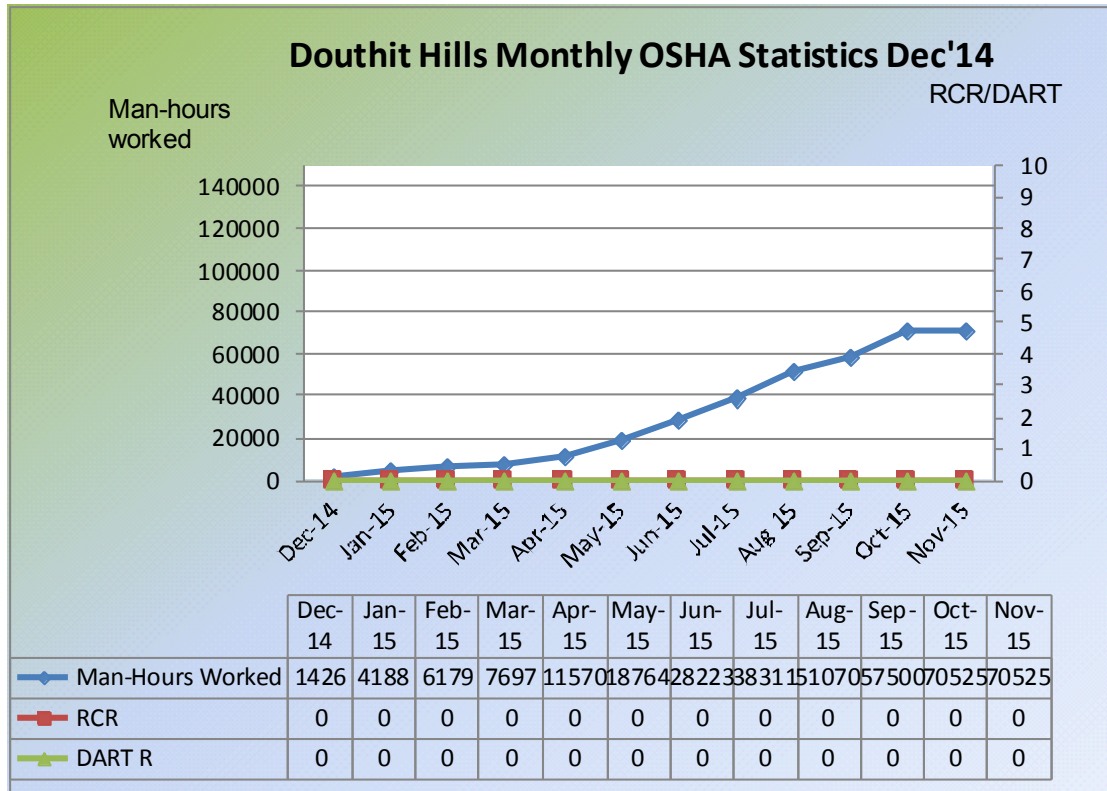

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #41
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

