



## SAFETY

- » Total Man Hours Worked This Week: 5779
- » Total Man Hours on Project: 111795
- » Crafts On Project This Week: 7
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### EAST ZONE

- » Formed & Poured Basement Walls @ Bldg. E.
- » Continued Footings/Stem Walls at Building E.
- » Continued Pad Prep @ Bldg. E.
- » Continued Waterproofing @ Bldg. E.
- » Continued Truss & Decking @ Bldg. G.
- » Framed Interior Walls @ Bldg. G.
- » Continued Pre-Cast (3rd Floor Walls/4th Floor Metrodeck) @ Bldg. F.



Completed Curb and Gutter @ East Lot



Building E Basement Walls

### SITE & WEST ZONE

- » Continued Mass Grading at West Zone.
- » Continued Chilled Water Pipe @ HUB Utility Yard & Tie-In to East Zone.
- » Continued Auger Cast Piles @ Bldg. B Basement.
- » Installed Hand Hole and Duct Bank South of Bldg. C.
- » Continued Domestic Water Installation @ East Zone Toward HUB Utility Yard.
- » Installed Forced Main Lift Station & Valve Box @ HUB Utility Yard.
- » Continued Grading @ East Lot.
- » Completed Curb & Gutter @ East Lot.





## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Continue Footings/Stemwalls @ Bldg E.
- » Continue Basement Walls @ Bldg. E.
- » Continue Interior Wall Framing @ Bldg. G.
- » Continue Pre-Cast at Building F.
- » Continue Truss/Decking @ Bldg. G.
- » Continue Waterproofing @ Bldg. E.
- » Continue Attic Duct Installation @ Bldg. G.
- » Begin Plumbing Underground Rough-In @ Bldg. G.



Precast Erection at Building F



MH6E and MH6C Tie in

### SITE & WEST ZONE

- » Continue Underground Utilities @ HUB Utility Yard.
- » Install Soil Cement @ East Parking Lot to Support Paving Activity.
- » Continue Duct Bank and Manhole Installation South of Bldg.'s A & C.
- » Continue Chilled Water Tie-In from East Zone to HUB.
- » Begin Storm Drain Line 8 @ West Zone Spine.
- » Remove Trees @ Daniel Drive Bank to Support Installation of Slope Drain 10-B.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #49  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	20	800	31803
American Deep Foundation	Auger cast piles	9	540	3598
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	720	4338
D.H. Griffin	Tank Foundation Removal	0	0	90
JBR Construction	Steam Line Removal	0	0	2040
Hutch-N-Son	Early Site Work	0	0	1337
King Asphalt	Asphalt	0	0	1147
Labor Finders	Labor Force	16	601	12151
Metro Power	Underground Electrical	14	450	6659
Osteen	Chill Water pipe	4	192	790
Precision	Concrete	22	1144	10248
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	14	812	29313
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	9	450	1650
Silt Fence Installation	Site Erosion Control	0	0	671
Southern Mechanical Inc.	Mechanical	0	0	1140
Tree South	Arborist	1	20	991
Upstate Curb	Curb and Gutter	5	50	360
Valley Farm Construction	Tree removal/Grading	0	0	395
Gainesville Mechanical	Plumbing	0	0	0
<b>TOTAL</b>		<b>126</b>	<b>5779</b>	<b>111795</b>



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #49  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER

### CURRENT WEEK



Rain Days This Week = 0


Rain Days To Date = 39

### SAFETY REVIEW LOG

#### Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

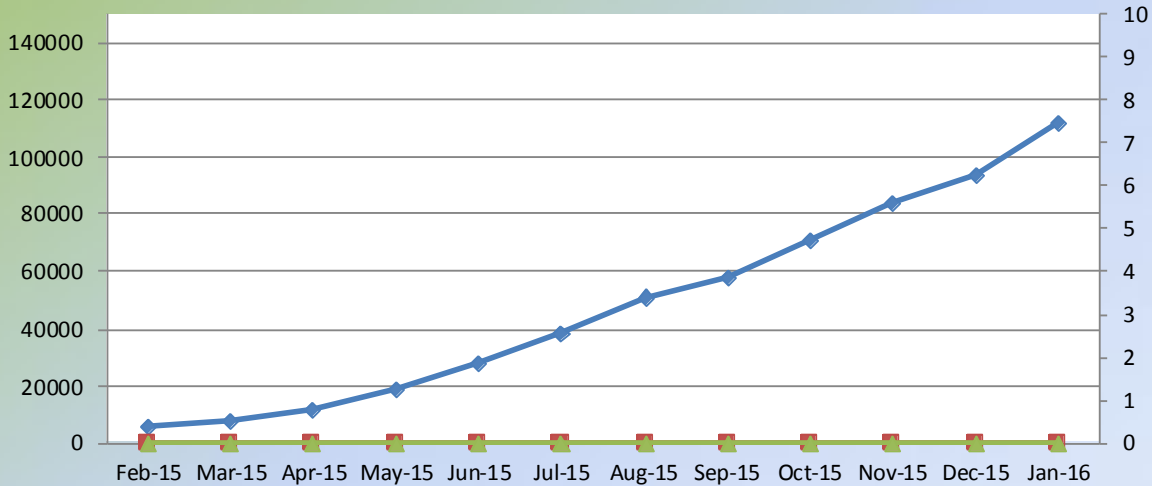

	Feb-15	Mar-15	Apr-15	May-15	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16
Man-Hours Worked	6179	7697	11570	18764	28223	38311	51070	57500	70525	83828	93233	11177
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #49  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

