

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #51  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 6254
- » Total Man Hours on Project: 123052
- » Crafts On Project This Week: 7
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### EAST ZONE.

- » Continued interior wall layout/installation @ Building G.
- » Continued Grout/Caulk of precast @ Building F.
- » Continued Waterproofing @ Building E.
- » Continue Backfill @ Building E.
- » Continued Plumbing Rough-In @ Building G.
- » Continue Window Frame Installation @ Building G.



Window Installation @ Building G



Plumbing Rough-In @ Building G

### SITE & WEST ZONE

- » Completed Domestic Water Installation @ HUB Utility Yard
- » Installed Grease Interceptors @ HUB Utility Yard.
- » Installed base @ East Parking Lot.
- » Completed Auger Cast Piles @ Building B.
- » Continued Storm Line 8 @ West Spine.
- » Continued Ductbank Installation @ West Zone.



## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Continue Precast Erection @ Building E.
- » Continue Backfill @ Building E.
- » Continue Window Frame Installation @ Building G.
- » Begin Prep for 4th floor Topping Slab @ Building F.
- » Begin Roof Trusses @ Building F.
- » Continue Exterior Soffit @ Bldg. G.
- » Begin Ice & Water Shield @ Bldg. G.
- » Continue Brick Relief Angle @ Bldg. G.



HUB Building Pad Prep



Grease Interceptors @ HUB Utility Yard

### SITE & WEST ZONE

- » Begin chipping Pile Caps @ HUB.
- » Begin Footings and Foundation @ HUB.
- » Begin Paving @ East Parking Lot.
- » Continue Storm Line 8 @ West Spine
- » Begin Ductbank Installation @ HUB Utility Yard.
- » Set Manholes 4 E&C.
- » Continue Domestic Water @ HUB Utility Yard.
- » Continue Wire Pull @ Parking Lot Lights.
- » Continue Racking Manholes.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #51  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	23	800	33880
American Deep Foundation	Auger cast piles	6	96	4054
Baker Roofing	Sheathing and Shingles	7	280	280
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	576	5418
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	1	20	40
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	10	480	480
JBR Construction	Early Site Work	0	0	2049
King Asphalt	Asphalt	4	160	1547
Labor Finders	Labor Force	14	600	13406
Metro Power	Underground Electrical	12	502	7659
Osteen	Chill Water pipe	4	192	1142
Precision	Concrete	22	1150	12366
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	15	780	30765
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	9	360	2370
Silt Fence Installation	Site Erosion Control	4	18	689
Southern Mechanical Inc.	Electrical/Plumbing	6	240	480
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>149</b>	<b>6254</b>	<b>123052</b>



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #51  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER

### CURRENT WEEK

7	Clear	8	Partly Cloudy	9	Mostly Cloudy	10	Clear	11	Clear	12	Partly Cloudy	13	Clear
Actual: 57°   35° 0.00 in		Actual: 53°   37° 0.00 in		Actual: 39°   28° 0.00 in		Actual: 36°   24° 0.00 in		Actual: 54°   27° 0.00 in		Forecast: 50°   27° 0.0 in		Forecast: 45°   25° 0.0 in	
Average: 53°   29° 0.18 in		Average: 54°   29° 0.13 in		Average: 53°   26° 0.02 in		Average: 52°   28° 0.09 in		Average: 54°   30° 0.14 in		Average: 56°   30° 0.12 in		Average: 55°   31° 0.21 in	

Rain Days This Week = 0


Rain Days To Date = 40

### SAFETY REVIEW LOG

#### Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

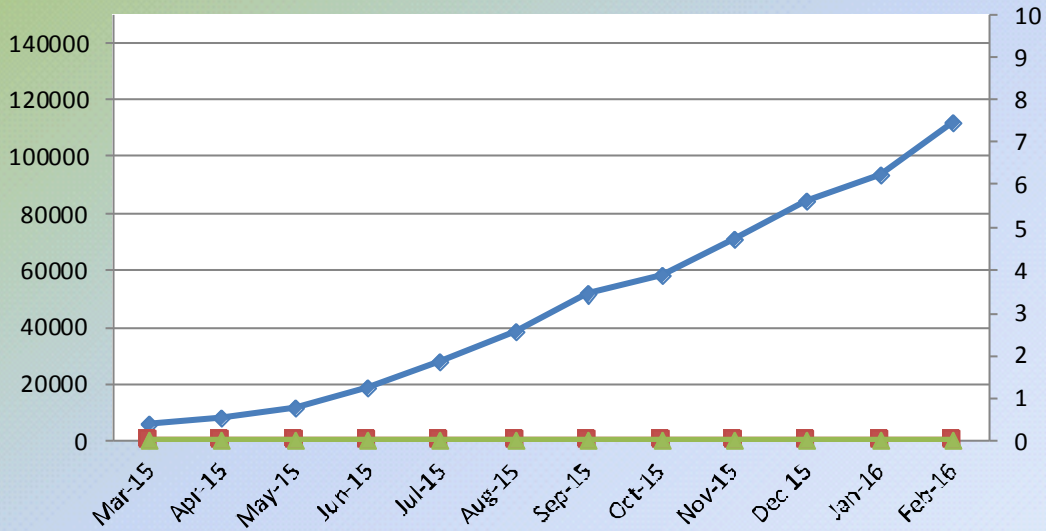

	Mar-15	Apr-15	May-15	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16
Man-Hours Worked	6179	7697	11570	18764	28223	38311	50979	57409	70434	83737	93142	111684
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #51  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

