



SAFETY

- » Total Man Hours Worked This Week: 5484
- » Total Man Hours on Project: 135019
- » Crafts On Project This Week: 11
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

EAST ZONE

- » Continued Installing Attic Duct @ Building G.
- » Continued Precast Erection @ Building E.
- » Continued Foundations for Building E Sequence 2.
- » Completed 4th floor Topping Slab @ Building F
- » Backfilled Interior @ Building F.
- » Prep for SOG @ Building G.
- » Installed HM Door Frames @ Building G.



Bldg. G Door Frames



Bldg. E Precast



Bldg. F Topping Slab

SITE, HUB, & WEST ZONE

- » Continued Chilled Water Pipe installation @ West Zone
- » Continued Chipping Pile Caps @ HUB.
- » Continued Footings and Foundation @ HUB.
- » Completed Storm Line 8 @ West Spine
- » Completed Communication Ductbank Installation @ HUB Utility Yard.
- » Began Forming Walls and Columns @ HUB.
- » Completed Chilled Water Tie—In from HUB to Cooling Tower.



Erosion Control @ Newman Road



Foundation Reinforcing @ HUB



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Installing Attic Duct @ Building G.
- » Begin Roof Trusses @ Building F.
- » Tie - In Sanitary Lie @ Building G.
- » Begin Sequence 2 Precast @ Building E.
- » Continue Framing Interior Walls @ Building G 3rd Floor.
- » Continue Decking and Ice & Water Shield @ Bldg. G.



HUB Wall Formation



East Parking Lot Striping

SITE, HUB, & WEST ZONE

- » Begin Crane Roads @ West Zone.
- » Continue Forming Walls and Columns @ HUB.
- » Install Ductbank form MH4 E&C to MH6 E&C.
- » Continue Grade Beams @ HUB.
- » Install Storm Line 9 South of Bldg. A.
- » Install Ductbank form Existing Manhole to MH 10.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #53
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	23	920	35840
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	12	192	752
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	9	360	5778
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	7	336	536
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	160	1040
JBR Construction	Early Site Work	0	0	2049
King Asphalt	Asphalt	4	40	1977
Labor Finders	Labor Force	15	636	14642
Metro Power	Underground Electrical	10	236	8430
Osteen	Chill Water pipe	4	160	1494
Precision	Concrete	40	1600	15466
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	14	644	32177
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	2	40	2630
Silt Fence Installation	Site Erosion Control	0	0	849
Southern Mechanical Inc.	Electrical/Plumbing	4	160	640
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		148	5484	135019



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #53

Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


CURRENT WEEK

21	Rain		22	Tstorm		23	Rain		24	Tstorm		25	Partly Cloudy		26	Clear		27	Clear	
Actual: 69° 54°		Actual: 68° 53°		Actual: 52° 48°		Actual: 70° 44°		Forecast: 52° 35°		Forecast: 57° 32°		Forecast: 59° 36°								
0.03 in		0.41 in		0.62 in		0.44 in		0.0 in		0.0 in		0.0 in								
Average: 58° 34°		Average: 59° 35°		Average: 57° 34°		Average: 58° 34°		Average: 59° 34°		Average: 59° 32°		Average: 58° 32°								
0.06 in		0.20 in		0.26 in		0.12 in		0.08 in		0.15 in		0.18 in								

Rain Days This Week = 2

Rain Days To Date = 43

SAFETY REVIEW LOG

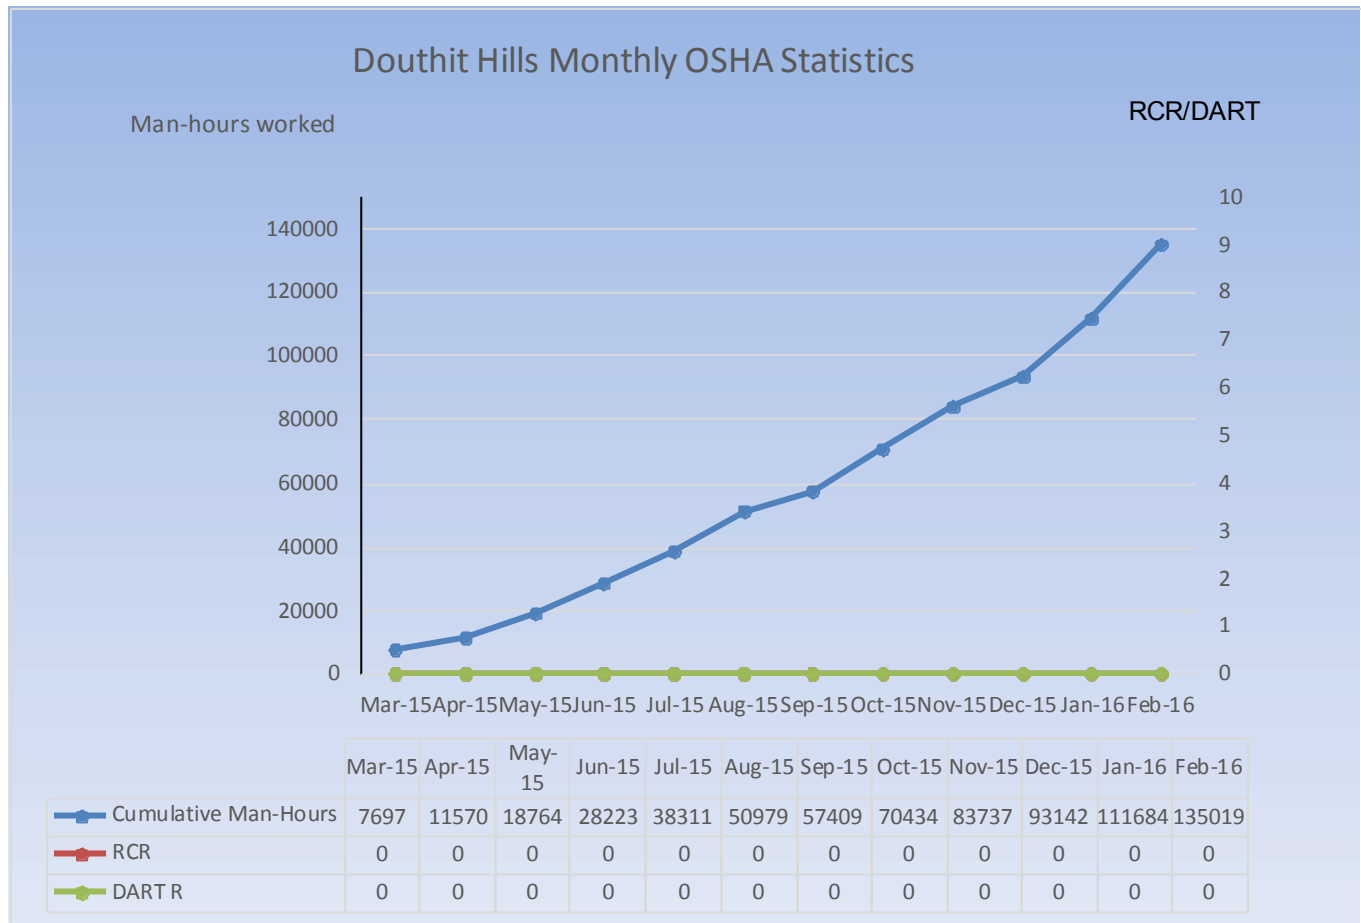



MANPOWER CHART

