

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #55  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 6700
- » Total Man Hours on Project: 148121
- » Crafts On Project This Week: 11
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### EAST ZONE

- » Continued Framing Interior Walls @ Building G 2nd Floor.
- » Continued Precast Erection @ Building E.
- » Poured SOG @ Building G.
- » Installed 3rd Floor Windows @ Bldg. F.
- » Continued Trusses @ Building F.
- » Continued Sanitary Aboveground @ Building G, Floors 2-4.
- » Continued Brick Relief @ Building F.
- » Layout Interior walls @ Bldg. F.



Bldg. G Slab on Grade



Bldg. E Precast Sequence 1



Bldg. F Electrical Tie In

### SITE, HUB, & WEST ZONE

- » Completed Crane Roads @ West Zone.
- » Continued Forming Walls and Columns @ HUB.
- » Continued Grade Beams @ HUB.
- » Tied-In Sanitary to Bldg. F.
- » Continued Chilled Water @ West Zone.
- » Continued Storm Line 9 South of Building A.
- » Received Rebar for Footings and Mobilized @ Building A.
- » Installed Ductbank from MH4 E&C to MH5 E&C



West Zone Crane Roads



HUB Walls





## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Complete Roof Trusses @ BLDG. F.
- » Continue Sequence 2 Precast @ BLDG. E.
- » Continue Caulking Exterior and Interior @ BLDG. G.
- » Install Duct @ BLDG. G 3rd Floor.
- » Coring and Layout of Bathrooms @ BLDG.F 3rd Floor.
- » Prep Topping Slabs @ BLDG. E Sequence One.
- » Continue Sanitary Aboveground @ Building F.
- » Complete Stairwell Window Frames @ Bldg. G.



Aboveground Plumbing @ Building G



Drop Inlets @ Storm Line 9

### SITE, HUB, & WEST ZONE

- » Continue Forming Walls and Columns @ HUB.
- » Continue Grade Beams @ HUB.
- » Rack Manholes
- » Complete Storm Line 9.
- » Begin Medium Voltage Cable
- » Begin foundations @ Building A.
- » Continue Racking Manholes.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #55  
Douthitt Hills Student Community, Clemson University Project  
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man	Total Man Hrs.
Holder Construction Company	General Contractor	25	1000	37760
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	0	0	1112
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	6954
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	8	320	1176
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	2	80	1120
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	4	180	180
King Asphalt	Asphalt	0	0	1992
Labor Finders	Labor Force	15	615	15872
Metro Power	Underground Electrical	10	396	9222
Osteen	Chill Water pipe	4	192	1866
Precision	Concrete	35	1680	18946
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	14	672	33584
Rival Construction Inc.	Concrete	1	25	25
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	15	580	3210
Silt Fence Installation	Site Erosion Control	0	0	884
Southern Mechanical Inc.	Electrical/Plumbing	9	360	1450
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>154</b>	<b>6700</b>	<b>148121</b>



# HOLDER CONSTRUCTION COMPANY

## Superintendents Weekly Activity Report #55

### Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


#### CURRENT WEEK

6	Clear		7	Clear		8	Clear		9	Partly Cloudy		10	Partly Cloudy		11	Partly Cloudy		12	Mostly Cloudy	
Actual: <b>64°</b>   <b>44°</b>			Actual: <b>66°</b>   <b>41°</b>			Actual: <b>73°</b>   <b>46°</b>			Actual: <b>75°</b>   <b>52°</b>			Forecast: <b>78°</b>   <b>61°</b>			Forecast: <b>82°</b>   <b>62°</b>			Forecast: <b>78°</b>   <b>60°</b>		
0.00 in			0.00 in			0.00 in			0.00 in			0.0 in			0.0 in			0.06 in		
Average: <b>62°</b>   <b>37°</b>			Average: <b>62°</b>   <b>36°</b>			Average: <b>62°</b>   <b>35°</b>			Average: <b>62°</b>   <b>35°</b>			Average: <b>63°</b>   <b>38°</b>			Average: <b>63°</b>   <b>37°</b>			Average: <b>65°</b>   <b>40°</b>		
0.16 in			0.12 in			0.13 in			0.11 in			0.15 in			0.08 in			0.12 in		

Rain Days This Week = 0

Rain Days To Date = 43

#### SAFETY REVIEW LOG

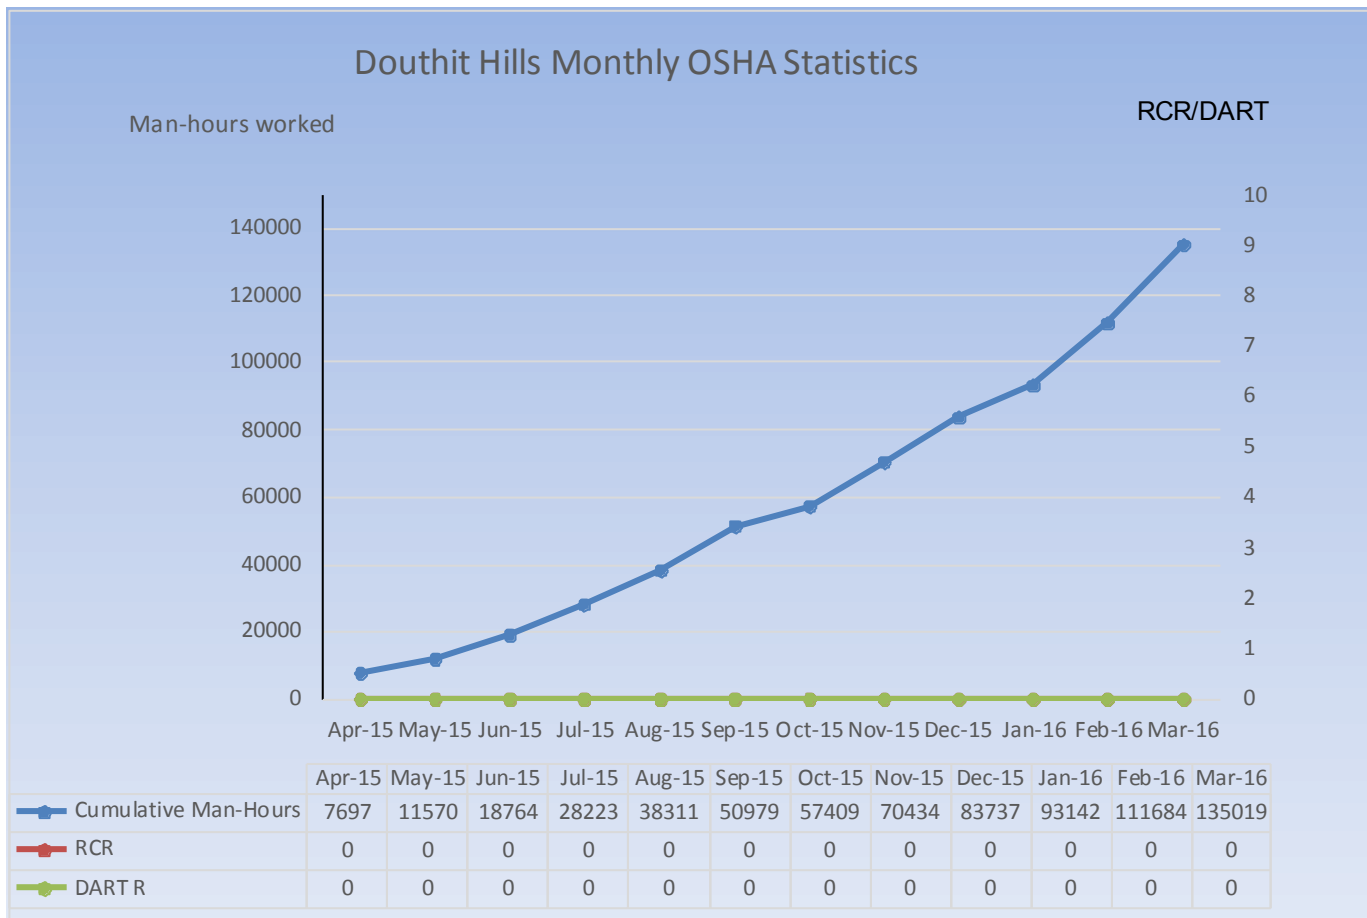



## MANPOWER CHART

### Douthit Hills Workforce

