

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #56
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY


- » Total Man Hours Worked This Week: 6655
- » Total Man Hours on Project: 152944
- » Crafts On Project This Week: 11
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

- » Completed Roof Trusses @ Building F.
- » Continued Sequence 2 Precast @ Building E.
- » Continued Caulking Exterior and Interior of All Floors @ Building G.
- » Coring and Layout of Bathrooms @ Building F 3rd Floor.
- » Poured Topping Slab @ Building E Sequence 1.
- » Completed Stairwell Window Frames @ Building G.
- » Continued Sanitary Aboveground @ Building F.

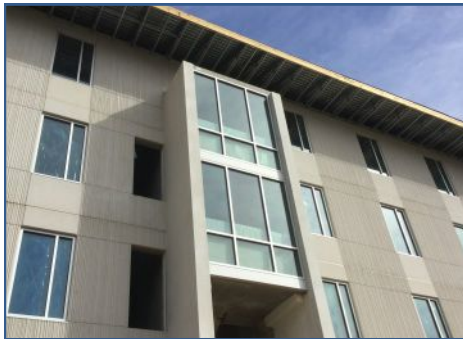

Bldg. G Stairwell Storefront



Bldg. E Precast Sequence 2



Bldg. F Electrical Stub Ups

SITE, HUB, & WEST ZONE

- » Continued Forming Walls and Columns @ HUB.
- » Continued Grade Beams @ HUB.
- » Continued Racking Manholes
- » Continued Storm Line 9.
- » Began Foundations @ Building A.
- » Began Foundations @ The HUB Loading Dock.
- » Began Freight Elevator Shear Wall.
- » Installed Chiller and Lighting Duct Banks @ HUB Utility Yard



HUB Walls



Ductbank North of the HUB



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Framing Interior Walls @ Building G 1st and 2nd Floor.
- » Prep and Pour SOG @ Building F
- » Continue Roof Decking @ Building F.
- » Continue Window Install @ Building F.
- » Continue Precast @ Building E Sequence 2.
- » Continue Brick Angle Relief @ Building E.



Building A Foundations



Backfill @ Building B.

SITE, HUB, & WEST ZONE

- » Begin Tie in from MH4E&C to MH3E&C.
- » Begin Chilled Water Flush & Test.
- » Complete Storm Line 9.
- » Continue Foundations @ Building A.
- » Begin Ductbank from MH3 to Building D.
- » Complete Forced Main Tie-in.
- » Complete Temporary Electric to Bldg's. E & F.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #56
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man	Total Man Hrs.
Holder Construction Company	General Contractor	26	1000	38760
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	7	56	1168
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	576	7530
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	8	320	1176
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	48	1168
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	8	408	516
King Asphalt	Asphalt	0	0	1992
Labor Finders	Labor Force	11	440	16312
Metro Power	Underground Electrical	11	376	9598
Osteen	Chill Water pipe	4	140	2006
Precision	Concrete	30	1440	18946
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	13	598	34182
Rival Construction Inc.	Concrete	9	243	268
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	15	600	3810
Silt Fence Installation	Site Erosion Control	0	0	884
Southern Mechanical Inc.	Electrical/Plumbing	9	410	1860
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
TOTAL		167	6655	152944



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #56
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

13	Rain		14	Rain		15	Clear		16	Clear		17	Clear		18	Mostly Cloudy		19	Chance of Rain	
Actual: 78° 64°	Actual: 75° 53°	Actual: 82° 55°	Actual: 86° 61°	Forecast: 80° 51°	Forecast: 70° 51°	Forecast: 59° 47°														
0.46 in	0.24 in	0.00 in	0.00 in	0.0 in	0.03 in	0.11 in														
Average: 65° 39°	Average: 64° 38°	Average: 65° 37°	Average: 64° 40°	Average: 63° 37°	Average: 62° 37°	Average: 64° 40°														
0.38 in	0.20 in	0.09 in	0.14 in	0.30 in	0.15 in	0.18 in														

Rain Days This Week = 0

Rain Days To Date = 43

SAFETY REVIEW LOG

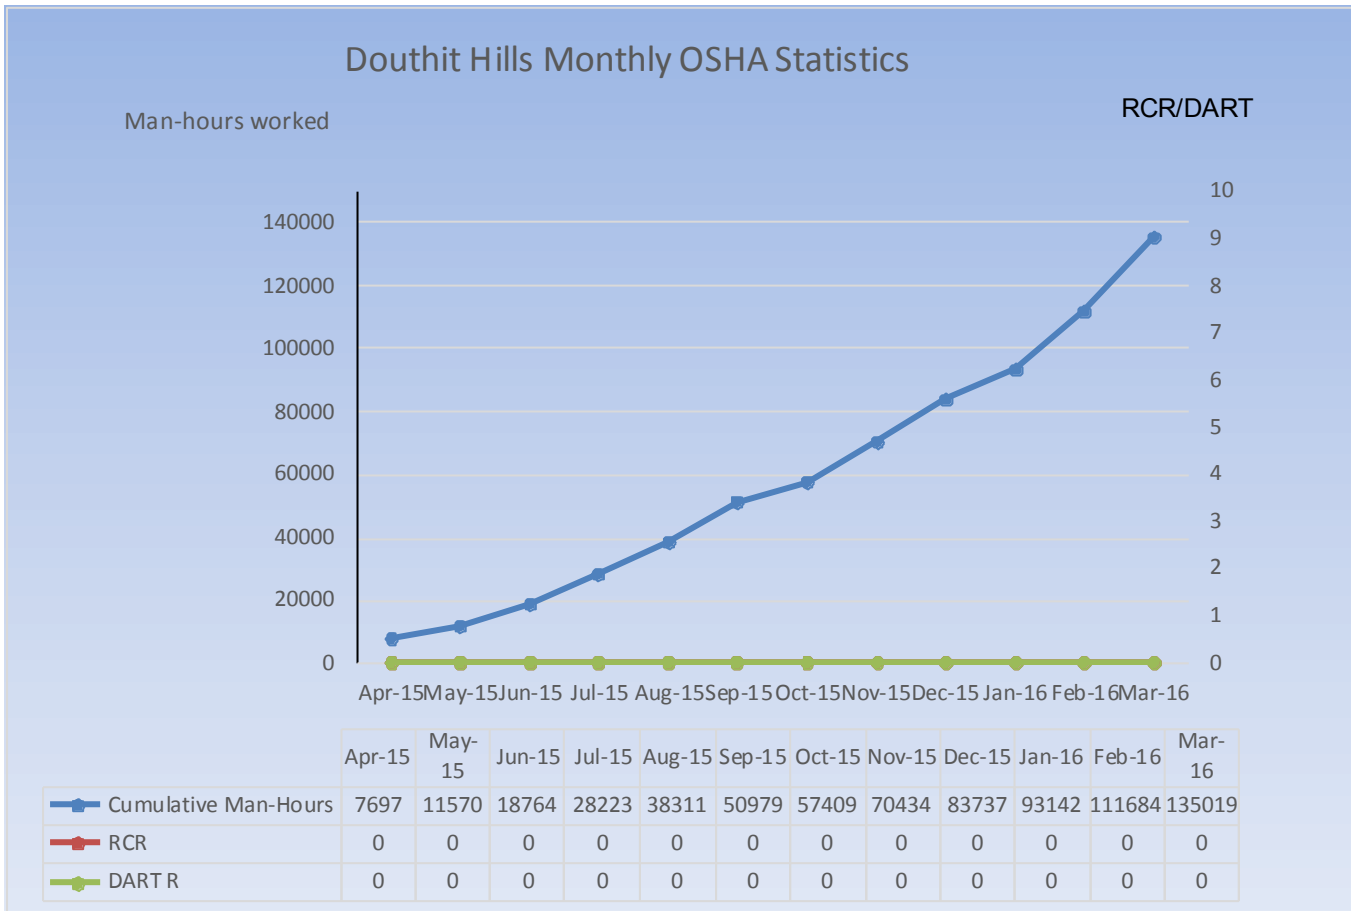

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #56
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

