

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #59  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 7056
- » Total Man Hours on Project: 159999
- » Crafts On Project This Week: 11
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

- » Began Shingles on Building G.
- » Continued Sequence 2 Precast @ Building E.
- » Continued Caulking Exterior and Interior Of All Floors @ Building G.
- » Poured SOG @ Building F.
- » Continued Window Frame Installation @ Building F.
- » Began Electrical Underground @ Building E Sequence 1.
- » Continued Sanitary Aboveground @ Building F.



Bldg. G Hanger Duct



Bldg. E Electrical Stub Ups



Bldg. F SOG

## SITE, HUB, & WEST ZONE

- » Continued Forming Walls and Columns @ HUB.
- » Began Waterproofing @ HUB.
- » Continued Racking Manholes
- » Completed Storm Line 9.
- » Continued Foundations @ Building A.
- » Continued Access Roads @ Building B.
- » Began CIP Walls @ Building A.
- » Began Below-grade Waterproofing @ Building A.



Waterproofing @ HUB Walls



Columns and CIP Walls @ HUB



## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Continue Framing Interior Walls @ Building G 1st and 2nd Floor.
- » Continue Roof Decking @ Building F.
- » Continue Window Install @ Building F 2nd Floor.
- » Complete Precast @ Building E Sequence 2.
- » Continue Brick Relief Angle @ Building E.
- » Continue Shingles @ Building G.
- » Pour Topping Slab @ Building E 2nd Floor.



Building A Wall Forms



Access Road @ Building B

### SITE, HUB, & WEST ZONE

- » Begin Pulling Medium Voltage Cable.
- » Continue Storm Line 6.
- » Continue Foundations @ Building A.
- » Continue Freight Elevator Shear Wall.
- » Continue CIP Walls @ Building A.
- » Begin Foundations @ Building B.
- » Begin Backfill @ HUB.
- » Begin Storm Line 10B South.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #59  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	26	1040	39800
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	7	288	1456
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	8130
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	13	559	1735
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	270	1438
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	8	344	860
King Asphalt	Asphalt	0	0	1992
Labor Finders	Labor Force	10	541	16853
Metro Power	Underground Electrical	12	413	10010
Osteen	Chill Water pipe	0	0	2006
Precision	Concrete	27	1134	20080
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	12	548	34730
Rival Construction Inc.	Concrete	9	405	673
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	13	524	4334
Silt Fence Installation	Site Erosion Control	0	0	884
Southern Mechanical Inc.	Electrical/Plumbing	9	390	2250
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>164</b>	<b>7056</b>	<b>159999</b>



# HOLDER CONSTRUCTION COMPANY

## Superintendents Weekly Activity Report #59

### Douthit Hills Student Community, Clemson University Project

Joe Jett




## WEATHER

### CURRENT WEEK

20	Mostly Cloudy	21	Scattered Clouds	22	Clear	23	Clear	24	Partly Cloudy	25	Partly Cloudy	26	Partly Cloudy
Actual: 57°   45°	Actual: 61°   39°	Actual: 69°   37°	Actual: 73°   46°	Actual: 75°   55°	Forecast: 78°   52°	Forecast: 74°   56°							
0.01 in	0.00 in	0.00 in	0.00 in	0.00 in	0.0 in	0.01 in							
Average: -   -	Average: -   -	Average: -   -	Average: -   -	Average: -   -	Average: -   -	Average: -   -							
- in	- in	- in	- in	- in	- in	- in							

Rain Days This Week = 0      Rain Days To Date = 43

### SAFETY REVIEW LOG

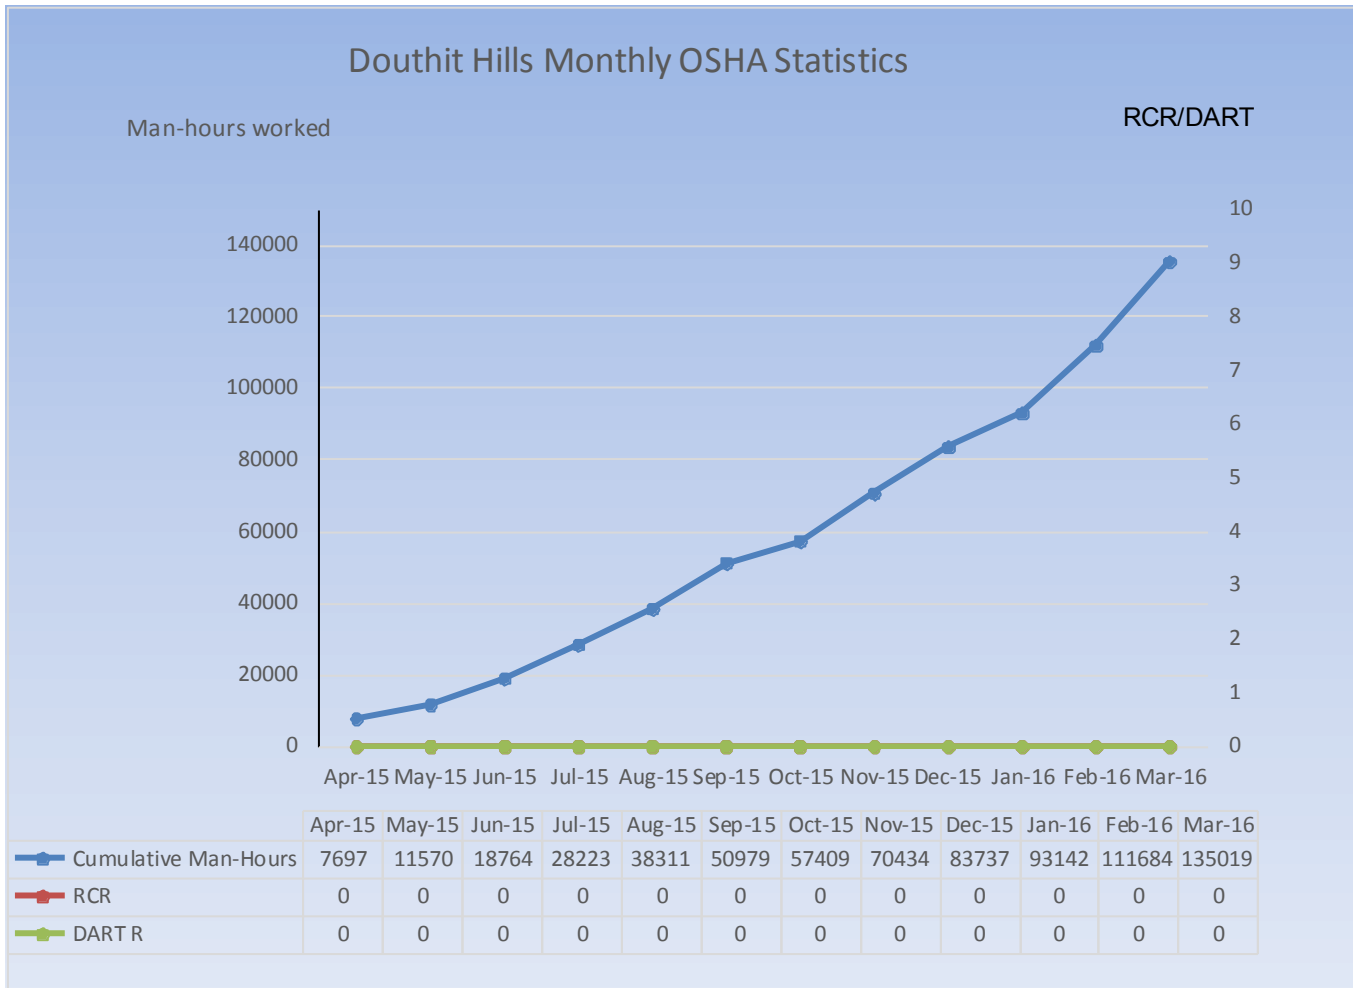

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #59  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

