

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #54  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 7061
- » Total Man Hours on Project: 141421
- » Crafts On Project This Week: 11
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### EAST ZONE

- » Continued Installing Attic Duct @ Building G.
- » Continued Precast Erection @ Building E.
- » Completed Topping Slabs @ Building F.
- » Continued Trusses @ Building F.
- » Continued Framing Interior Walls @ Building G.
- » Prepped for SOG @ Building G.
- » Continued Decking and Ice & Water Shield @ Building G.
- » Continued Brick Relief Angle @ Bldg. F.
- » Began Metal Decking @ Bldg. F Roof.
- » Continued Utility Tie-In At Bldg's G & F.



Bldg. G Slab on Grade Prep



Bldg. E Precast Sequence 2



Bldg. F Trusses

### SITE, HUB, & WEST ZONE

- » Continued Crane Road @ West Zone.
- » Continued Forming Walls and Columns @ HUB.
- » Continued Grade Beams @ HUB.
- » Completed Ductbank From Existing MH to MH10.
- » Completed Ductbank From MH4 E&C to MH6 E&C @ HUB Utility Yard.
- » Began Storm Line 9 South of Building A.
- » Continued Chilled Water Installation @ West



Building F 2nd Floor Topping Slab



HUB Walls



## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Pour SOG @ Building G.
- » Continue Roof Trusses @ Building F.
- » Continue Sequence 2 Precast @ Building E.
- » Continue Framing Interior Walls @ Building G 3rd Floor.
- » Continue Brick Relief @ Building F.
- » Continue Sanitary Aboveground @ Building G, Floors 2-4.
- » Continue Topping Slab Prep @ Bldg. F, Floors 2-4.



HUB Walls and Grade Beams



Crane Roads at West Zone

### SITE, HUB, & WEST ZONE

- » Continue Crane Roads @ West Zone
- » Continue Forming Walls and Columns @ HUB.
- » Continue Grade Beams @ HUB.
- » Rack Manholes
- » Continue Chilled Water @ West Zone
- » Mobilize & Begin Footings & Foundations @ Bldg. A.
- » Continue Storm Line 9 @ West Zone.
- » Install Ductbank From MH4 E&C to MH5 E&C.
- » Begin Ductbank From MH4 E&C to MH3 E&C.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #54  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man	Total Man Hrs.
Holder Construction Company	General Contractor	23	920	36760
American Deep Foundation	Auger cast piles	0	0	4292
Baker Roofing	Sheathing and Shingles	9	360	1112
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	576	6354
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Plumbing	8	320	856
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	2	80	1040
JBR Construction	Early Site Work	0	0	2049
King Asphalt	Asphalt	2	14	1992
Labor Finders	Labor Force	15	615	15257
Metro Power	Underground Electrical	9	396	8826
Osteen	Chill Water pipe	4	180	1674
Precision	Concrete	40	1800	17266
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Grading	Site Grading & Utilities	15	735	32912
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	14	580	2630
Silt Fence Installation	Site Erosion Control	5	35	884
Southern Mechanical Inc.	Electrical/Plumbing	9	450	1090
Tree South	Arborist	0	0	1171
Upstate Curb	Curb and Gutter	0	0	360
Valley Farm Construction	Tree removal/Grading	0	0	395
<b>TOTAL</b>		<b>167</b>	<b>7061</b>	<b>141421</b>



# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #54  
 Douthit Hills Student Community, Clemson University Project  
 Joe Jett



## WEATHER


### CURRENT WEEK

Day	Weather	Actual High/Low	Actual Precip	Forecast High/Low	Forecast Precip	Average High/Low	Average Precip
28	Clear	69°   39°	0.00 in	69°   41°	0.35 in	58°   32°	0.28 in
29	Clear	75°   51°	0.00 in	59°   37°	0.0 in	58°   32°	0.00 in
1	Scattered Clouds	69°   41°	0.35 in	59°   37°	0.0 in	59°   34°	0.16 in
2	Clear	59°   37°	0.0 in	62°   37°	0.20 in	61°   36°	0.12 in
3	Rain	58°   42°	0.24 in	63°   37°	0.0 in	62°   37°	0.25 in
4	Partly Cloudy	63°   37°	0.0 in	63°   40°	0.0 in	63°   37°	0.15 in
5	Clear	63°   40°	0.0 in	63°   40°	0.15 in	63°   40°	0.15 in

Rain Days This Week = 0

Rain Days To Date = 43

### SAFETY REVIEW LOG

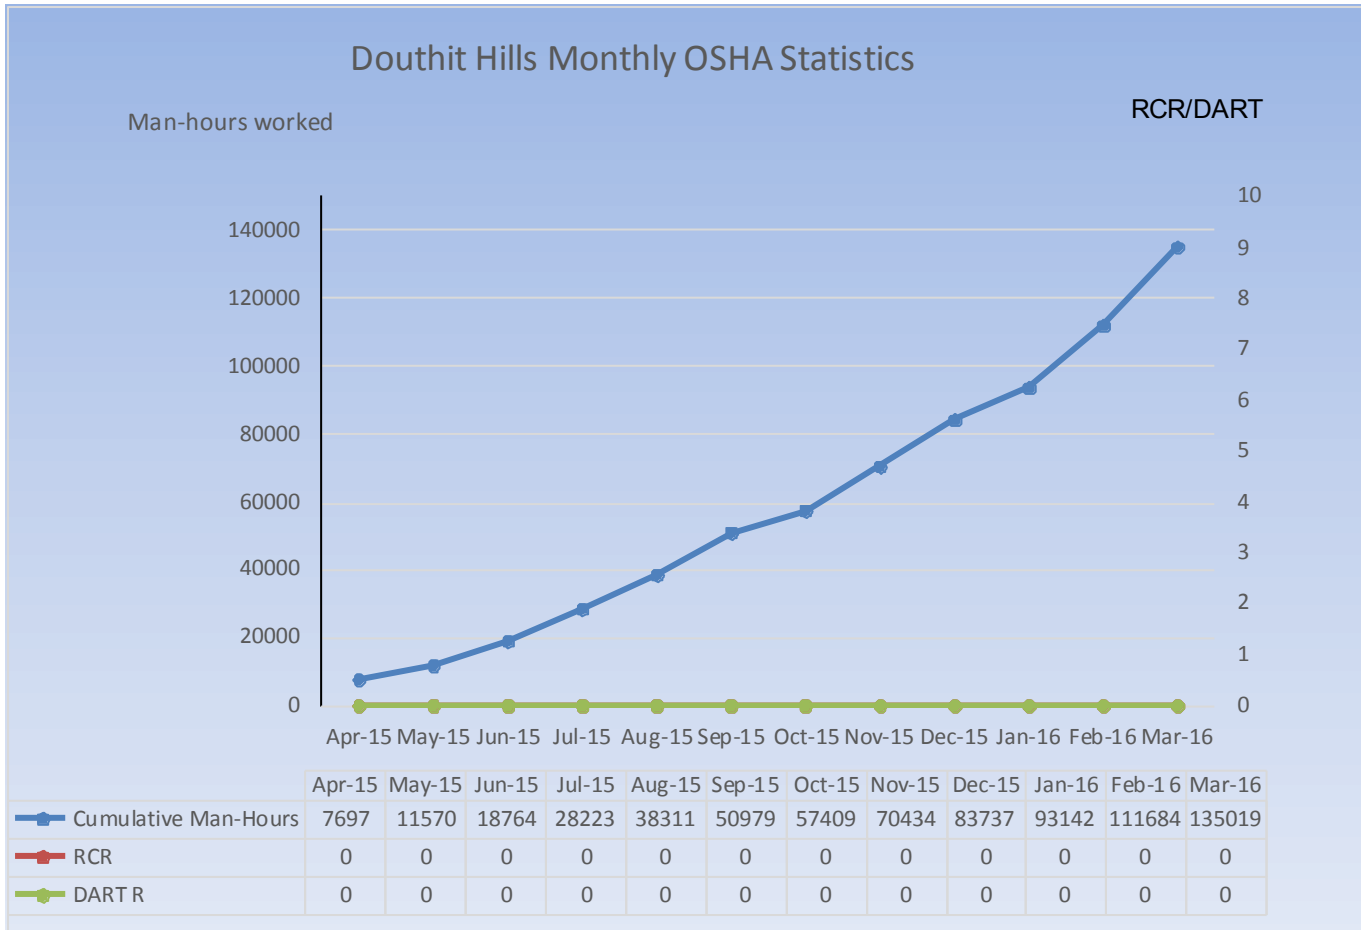

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #54  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

### Douthit Hills Workforce

