

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #65
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 12571
- » Total Man Hours on Project: 213355
- » Crafts On Project This Week: 15
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

East Zone


- » Continued Domestic Water Rough-In @ Building G Bathrooms.
- » Continued Window Frame Installation @ Building E.
- » Continued Brick Masonry @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Installing Fascia @ Building G.
- » Poured Building E Sequence 1 Slab On Grade.
- » Continued Electrical Rough-In @ Building G.
- » Continued Sprinklers @ Building G .
- » Continued Temporary Power Wiring @ Building E.



Bldg. G Chilled Water

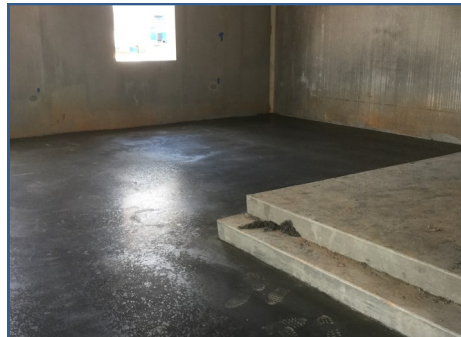

Bldg. E Mech. Room Slab

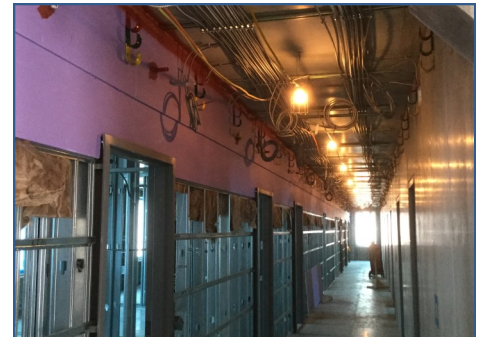

Bldg. F Overhead Rough-In

SITE, HUB, & WEST ZONE

- » Poured Elevated Deck 1B and 1C @ HUB.
- » Continued Auger Cast Piles @ Building B.
- » Poured Elevated Shear Wall @HUB.
- » Completed Storm Line 10 South.
- » Continued CIP Walls @ Building B.
- » Continued Precast @ Building A.
- » Continued Foundations @ Building B.
- » Completed Access Road For Building C.
- » Continue Excavation For Underground Detention System.



CIP Walls @ HUB



Elevated Slab 1B @ HUB



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Overhead Rough-In @ Building G.
- » Continue Brick @ Building G.
- » Continue Stair Rails @ Building F.
- » Continue Temporary Power Wiring @ Building E.
- » Continue Brick Angle @ Building E.
- » Pour SOG Building E Sequence 2.
- » Continue Glazing @ Building E.



Building A Precast



Building B CIP Walls

SITE, HUB, & WEST ZONE

- » Continue Backfill @ Building B.
- » Continue Precast @ Building A.
- » Continue CIP Walls @ Building B.
- » Continue Auger Cast Piles @ Building B.
- » Pour Elevated Deck 2A @ HUB.
- » Continue Forming HUB Elevated Deck 2B and 2C.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #65
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	28	1120	46120
American Deep Foundation	Auger cast piles	9	243	5310
Baker Roofing	Sheathing and Shingles	6	256	3248
Carolina Fire Protection	Sprinklers	5	250	750
C&C Fence	Site Fence	0	0	764
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	576	9390
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	15	840	5292
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	128	2336
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	12	600	3364
King Asphalt	Asphalt	0	0	2264
Labor Finders	Labor Force	11	500	19858
Metro Power	Underground Electrical	10	400	12151
Old North State Masonry	Masonry	22	1000	3560
Osteen	Chill Water pipe	0	0	2066
Precision	Concrete	60	3000	31720
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	750	38670
Rival Construction Inc.	Concrete	26	1248	4881
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	23	1056	7566
Silt Fence Installation	Site Erosion Control	0	0	999
Southern Mechanical Inc.	Electrical/Plumbing	15	580	4700
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	3	24	274
Total		278	12571	213355



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #65

Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Precipitation	Average High/Low	Average Precipitation
1	Tstorm	82° 66°	0.54 in	77° 52°	0.18 in
2	Tstorm	86° 68°	0.00 in	77° 52°	0.11 in
3	Rain	82° 64°	0.11 in	77° 51°	0.20 in
4	Rain	73° 55°	0.00 in	75° 50°	0.20 in
5	Scattered Clouds	Forecast: 66° 50°	0.01 in	Average: 75° 50°	0.13 in
6	Clear	Forecast: 75° 51°	0.0 in	Average: 76° 49°	0.08 in
7	Clear	Forecast: 84° 62°	0.0 in	Average: 77° 51°	0.11 in

Rain Days This Week = 0

Rain Days To Date = 47

SAFETY REVIEW LOG

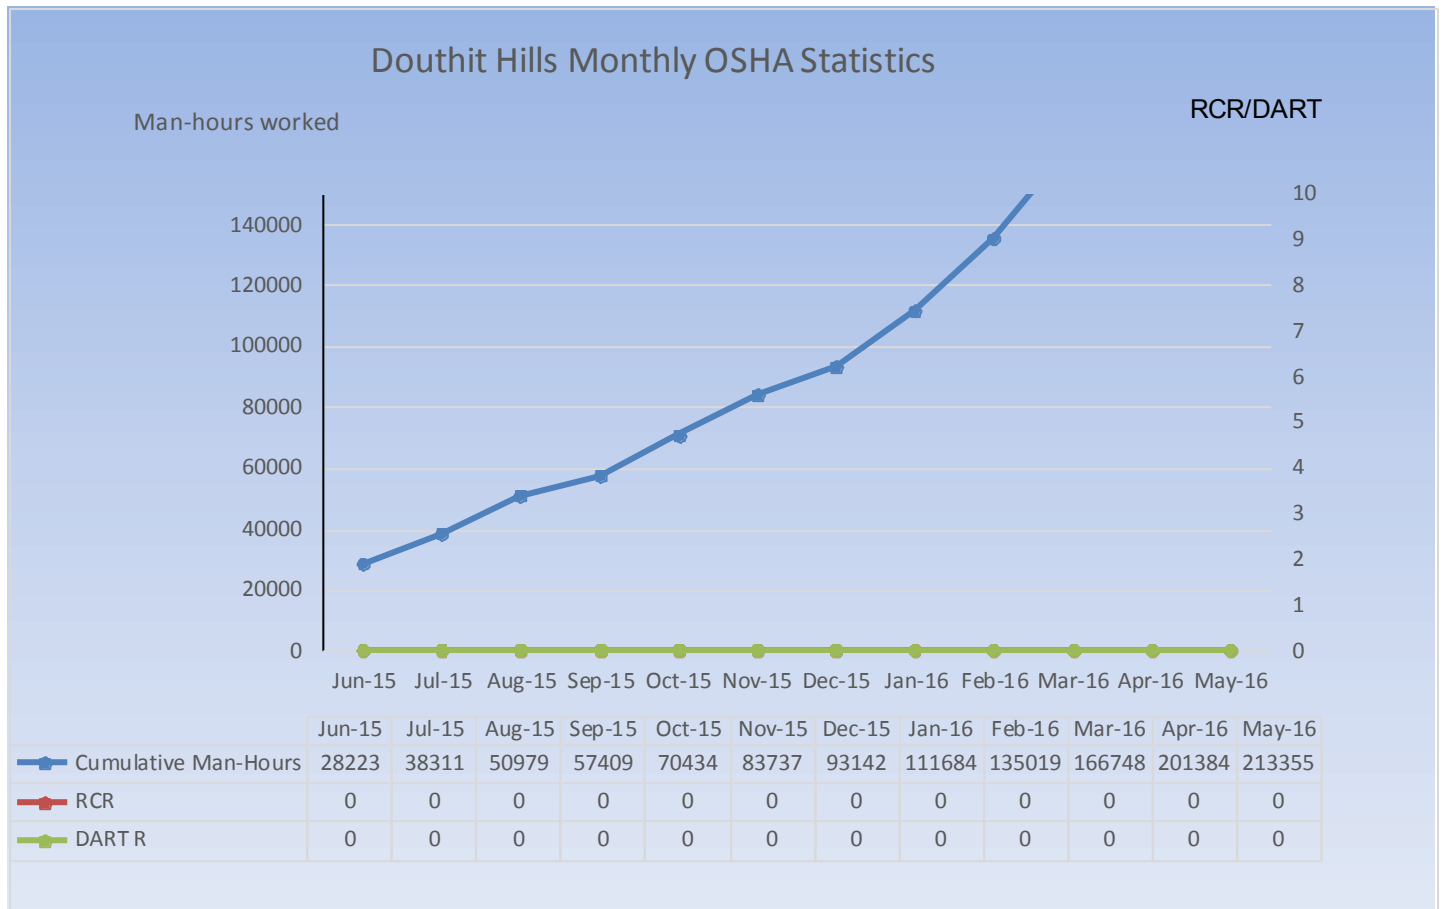

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #65
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

