

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #68
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 13869
- » Total Man Hours on Project: 255010
- » Crafts On Project This Week: 18
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Window Frame Installation @ Building E.
- » Continued Brick Masonry @ Building G.
- » Began Brick @ Building F
- » Began Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Installing Fascia @ Building G.
- » Continued Gutters @ Building G.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Building G .
- » Continued Stair Rails @ Building F.
- » Continued Brick Angle @ Building E.
- » Continued Setting Showers @ Building G.



Bldg. G Brick



Bldg. E Duct



Bldg. F Exterior Doors

SITE, HUB, & WEST ZONE

- » Completed Auger Cast Piles @ Building B.
- » Continued Backfill @ Building B.
- » Continued Stem Walls @ Building B.
- » Continued Precast @ Building A.
- » Continued Forming and Pouring Columns @ HUB.
- » Formed Transformer Pads @ Buildings E, F, & G.
- » Poured Elevated Slab 2A.
- » Continued Backfill @ HUB.



HUB Backfill



HUB Elevated Slab 2A



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building G and Building F.
- » Continue Coring For Plumbing @ Building E.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Gutters @ Buildings G & F.
- » Continue Sprinklers @ Building G.



Building B Backfill



Building B Elevator Pit

SITE, HUB, & WEST ZONE

- » Continue Precast @ Building A.
- » Continue Footings @ Building B.
- » Pour Elevated Deck 2B @ HUB.
- » Continue Forming HUB Elevated Deck 2C.
- » Continue Excavation For Underground Detention System.
- » Pour Transformer Pads @ Buildings E,F, & G.
- » Set Transformers @ Building E and G.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #68
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	33	1320	50080
American Deep Foundation	Auger cast piles	8	256	5926
Baker Roofing	Sheathing and Shingles	6	240	3878
Carolina Fire Protection	Sprinklers	5	300	1650
C&C Fence	Site Fence	3	30	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	480	10350
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	35	1960	10556
Gregory Electric	Aboveground Electric	3	120	240
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	108	2752
Johnson Controls	Building Controls	3	120	240
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	14	602	5382
King Asphalt	Asphalt	13	65	2329
Labor Finders	Labor Force	12	480	21268
Metro Power	Underground Electrical	10	338	13213
Old North State Masonry	Masonry	22	880	5840
Osteen	Chill Water pipe	3	48	2114
Precision	Concrete	55	2200	39120
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	750	40560
Rival Construction Inc.	Concrete	36	1440	8811
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	22	1072	10222
Silt Fence Installation	Site Erosion Control	0	0	999
Southern Mechanical Inc.	Electrical/Plumbing	17	680	6660
Steel Toe	Labor Force	6	240	3200
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #68
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER

CURRENT WEEK

22	Clear		23	Scattered Clouds		24	Clear		25	Clear		26	Tstorm		27	Scattered Clouds		28	Clear	
Actual: 81° 60°		Actual: 82° 57°		Actual: 84° 59°		Actual: 88° 61°		Actual: 89° 66°		Forecast: 84° 64°		Forecast: 87° 66°								
0.00 in		0.00 in		0.00 in		0.00 in		0.00 in		0.0 in		0.01 in								
Average: 80° 57°		Average: 81° 59°		Average: 81° 59°		Average: 81° 59°		Average: 82° 59°		Average: 81° 59°		Average: 81° 59°								
0.08 in		0.25 in		0.14 in		0.06 in		0.07 in		0.12 in		0.14 in								

Rain Days This Week = 0


Rain Days To Date = 50

SAFETY REVIEW LOG

Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

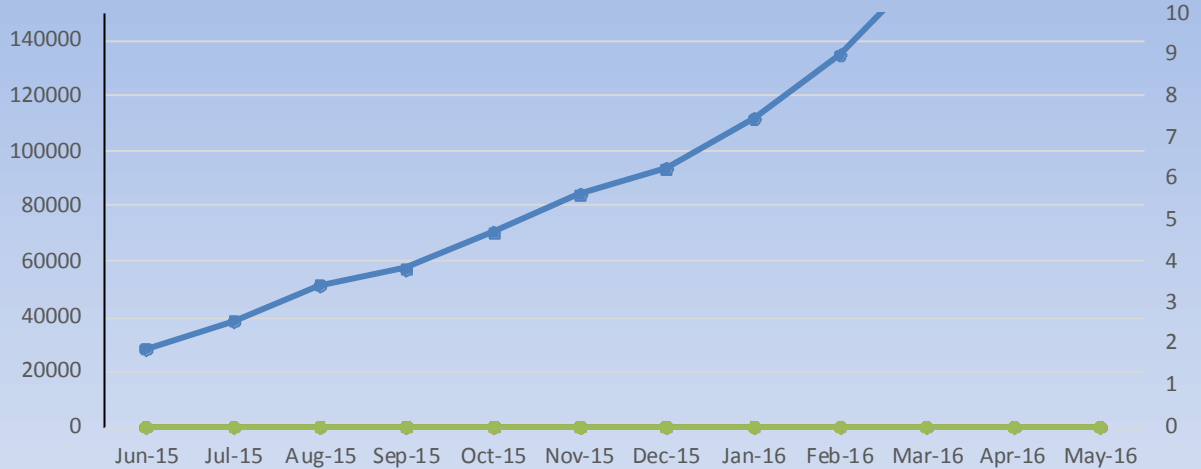

	Jun-15	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16
Cumulative Man-Hours	28223	38311	50979	57409	70434	83737	93142	111684	135019	166748	201384	255010
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART R	0	0	0	0	0	0	0	0	0	0	0	0



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #68
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

