

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #70
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 14178
- » Total Man Hours on Project: 280797
- » Crafts On Project This Week: 17
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Building G & F.
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Installing Fascia @ Building G.
- » Continued Gutters @ Building G.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Building G.
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Building G and F.
- » Began Hanging & Finishing Drywall @ Building G.
- » Continued Layout of 1st, 2nd, & 3rd Floor Walls @ Building E.
- » Continued Coring for Plumbing @ Building E.



Bldg. G Fire Rated Storefront Assembly

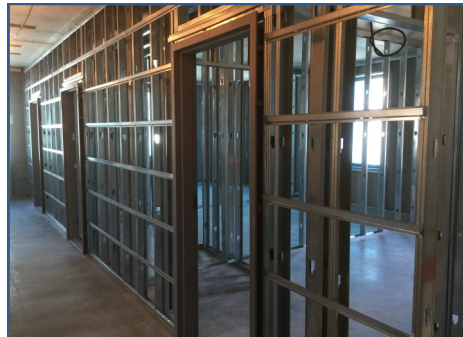

Bldg. E 3rd Floor Framing



Bldg. F Ceiling Install & Overhead Rough-In.

SITE, HUB, & WEST ZONE

- » Continued Backfill @ Building B.
- » Continued Footings @ Building B.
- » Completed Precast @ Building A.
- » Continued Excavation For Building C Foundations.
- » Continued Forming and Pouring Columns @ HUB.
- » Poured Transformer Pads @ Buildings A & C.
- » Poured Elevated Slab 2C.
- » Installed Storm Line 7.
- » Began Cooling Tower Steel Erection.
- » Installed Waterline Behind Clemson House



Building C Footings



HUB Elevated Slab 2C



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building G and Building F.
- » Continue Coring For Plumbing @ Building E.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Gutters @ Buildings G & F.
- » Continue Sprinklers @ Building G.
- » Continue Setting Showers @ Building G and F.



Building A Precast



Building B Waterproofing

SITE, HUB, & WEST ZONE

- » Continue Backfill and Footings @ Building B.
- » Continue Forming HUB Elevated Deck 3A.
- » Continue Excavation For Underground Detention System.
- » Set Transformers @ Building E and G.
- » Continue Excavation for Foundations @ Building C.
- » Continue Sanitary Lines @ HUB.
- » Continue Chiller Tower Erection.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #70
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	36	1400	52840
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	350	4484
Carolina Fire Protection	Sprinklers	6	300	2190
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	480	11310
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	36	1728	12284
Gregory Electric	Aboveground Electric	6	260	500
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	160	3072
Johnson Controls	Building Controls	3	120	480
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	14	602	6572
King Asphalt	Asphalt	0	0	2329
Labor Finders	Labor Force	12	480	22223
Metro Power	Underground Electrical	11	406	13955
Old North State Masonry	Masonry	22	880	7600
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	60	2400	43920
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	16	832	42142
Rival Construction Inc.	Concrete	36	1440	11691
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	20	800	11822
Silt Fence Installation	Site Erosion Control	0	0	1023
Southern Mechanical Inc.	Electrical/Plumbing	23	1150	8490
Steel Toe	Labor Force	6	240	3680
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #70
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	150	1044
Total		335	14178	280797



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #70


Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER

CURRENT WEEK



Rain Days This Week = 0


Rain Days To Date = 50

SAFETY REVIEW LOG

Douthit Hills Monthly OSHA Statistics

Man-hours worked

RCR/DART

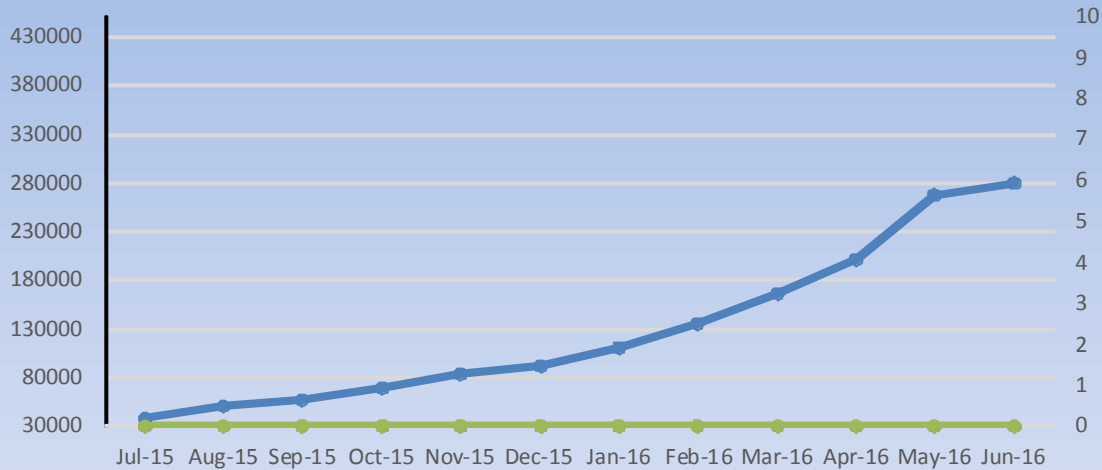

	Jul-15	Aug-15	Sep-15	Oct-15	Nov-15	Dec-15	Jan-16	Feb-16	Mar-16	Apr-16	May-16	Jun-16
Cumulative Man-Hours	38311	50979	57409	70434	83737	93142	11168	13501	16674	20138	26827	28079
RCR	0	0	0	0	0	0	0	0	0	0	0	0
DART	0	0	0	0	0	0	0	0	0	0	0	0



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #70
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

