

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #69
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 13462
- » Total Man Hours on Project: 268272
- » Crafts On Project This Week: 17
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Window Frame Installation @ Building E.
- » Continued Brick Masonry @ Building G.
- » Continued Brick @ Building F
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Installing Fascia @ Building G.
- » Continued Gutters @ Building G.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Building G .
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Building G and F.



Bldg. G Elevator



Bldg. E Duct



Bldg. F Overhead Insulation

SITE, HUB, & WEST ZONE

- » Continued Backfill @ Building B.
- » Continued Stem Walls @ Building B.
- » Continued Precast @ Building A.
- » Began Excavation For Building C Foundations.
- » Continued Forming and Pouring Columns @ HUB.
- » Poured Transformer Pads @ Buildings E, F, & G.
- » Poured Elevated Slab 2B.
- » Continued Backfill @ HUB.
- » Began Removing Access Roads South of Building G.
- » Began Cooling Tower Foundations.



Building C Excavation



HUB Elevated Slab 2B



NEXT WEEK'S ACTIVITIES

EAST ZONE

- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building G and Building F.
- » Continue Coring For Plumbing @ Building E.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Gutters @ Buildings G & F.
- » Continue Sprinklers @ Building G.
- » Continue Setting Showers @ Building G and F.



Building A Precast



Building B Stem Walls

SITE, HUB, & WEST ZONE

- » Continue Precast @ Building A.
- » Continue Backfill and Footings @ Building B.
- » Continue Forming HUB Elevated Deck 2C.
- » Continue Excavation For Underground Detention System.
- » Install Waterline Behind Clemson House.
- » Set Transformers @ Building E and G.

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #69
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	34	1360	51440
American Deep Foundation	Auger Cast Piles	8	240	6166
Baker Roofing	Sheathing and Shingles	8	256	4134
Carolina Fire Protection	Sprinklers	6	240	1890
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	480	10830
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	36	1728	12284
Gregory Electric	Aboveground Electric	3	120	360
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	160	2912
Johnson Controls	Building Controls	3	120	360
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	14	588	5970
King Asphalt	Asphalt	0	0	2329
Labor Finders	Labor Force	12	480	21748
Metro Power	Underground Electrical	10	336	13549
Old North State Masonry	Masonry	22	880	6720
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	60	2400	41520
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	750	41310
Rival Construction Inc.	Concrete	36	1440	10251
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	20	800	11022
Silt Fence Installation	Site Erosion Control	3	24	1023
Southern Mechanical Inc.	Electrical/Plumbing	17	680	7340
Steel Toe	Labor Force	6	240	3440
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #69
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	140	894
Total		333	13462	268472



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #69
 Douthit Hills Student Community, Clemson University Project
 Joe Jett




WEATHER

CURRENT WEEK

29 Partly Cloudy Actual: 75° 69° 0.00 in Average: 80° 59° 0.14 in	30 Tstorm Actual: 89° 64° 0.03 in Average: 81° 59° 0.08 in	31 Tstorm Actual: 90° 66° 0.06 in Average: 82° 60° 0.02 in	1 Tstorm Actual: 91° 70° 0.00 in Average: 84° 60° 0.25 in	2 Scattered Clouds Actual: 89° 69° 0.00 in Average: 84° 59° 0.15 in	3 Scattered Clouds Actual: 93° 70° 0.00 in Average: 84° 61° 0.10 in	4 Scattered Clouds Forecast: 93° 71° 0.28 in Average: 84° 61° 0.17 in
--	---	---	--	--	--	--

Rain Days This Week = 0 Rain Days To Date = 50

SAFETY REVIEW LOG

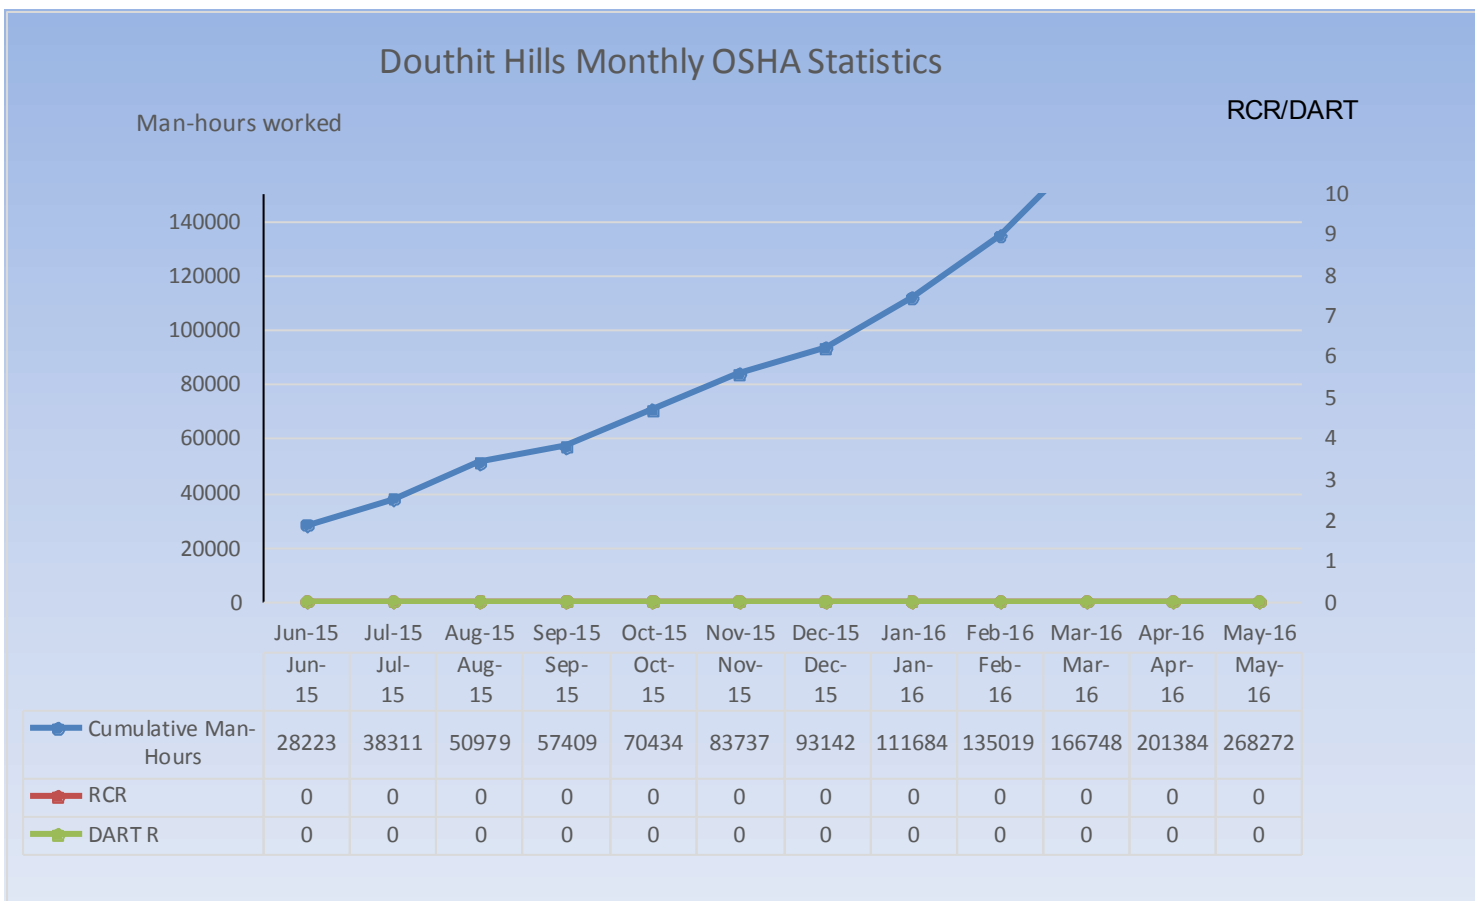

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #69
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

