

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #71  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## SAFETY

- » Total Man Hours Worked This Week: 14230
- » Total Man Hours on Project: 294867
- » Crafts On Project This Week: 17
- » OSHA Recordable Rate: 0





## CURRENT CONSTRUCTION ACTIVITIES

### East Zone

- » Continued Brick @ Buildings G & F.
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Gutters @ Building F.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Buildings G & F.
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Buildings G and F.
- » Continued Hanging & Finishing Drywall @ Building G.
- » Poured Areaway @ Building E.
- » Continue Sanitary Rough-in @ Building E.



Bldg. G EIFS



Bldg. E Areaway Wall



Bldg. F Walls and Framing

### SITE, HUB, & WEST ZONE

- » Continued Footings @ Building B.
- » Began Topping Slab Rough-in @ Building A.
- » Continued Excavation and Pouring Building C Foundations.
- » Continued Forming and Pouring Columns @ HUB.
- » Set Transformers @ Buildings A,C,HUB,F,E, and G.
- » Continued Forming Elevated Slab 3A.
- » Installed Waterline North of Building B & D.
- » Set Cooling Towers 1,2,&3.
- » Continued Underground Electrical @ HUB.



Building E and F Transformers



Cooling Towers





## NEXT WEEK'S ACTIVITIES

### EAST ZONE

- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Buildings G & F.
- » Begin Brick @ Building E.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Gutters @ Buildings F.
- » Continue Sprinklers @ Building G.
- » Continue Setting Showers @ Buildings G and F.



Building A Transformer



Building B Foundations

### SITE, HUB, & WEST ZONE

- » Continue Backfill and Footings @ Building B.
- » Pour HUB Elevated Deck 3A.
- » Continue Excavation For Underground Detention System.
- » Begin Backfill & Foundation Drains @ HUB.
- » Continue Excavation and Pouring Foundations @ Building C.
- » Continue CIP Walls @ Building C.
- » Continue Sanitary Lines @ HUB.
- » Continue Underground Electrical @ HUB.

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #71  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	36	1400	54240
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	350	4834
Carolina Fire Protection	Sprinklers	6	300	2490
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	6	300	11610
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	36	1728	14012
Gregory Electric	Aboveground Electric	6	260	760
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	160	3072
Johnson Controls	Building Controls	3	120	600
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	14	620	7192
King Asphalt	Asphalt	0	0	2329
Labor Finders	Labor Force	12	480	22703
Metro Power	Underground Electrical	16	660	14615
Old North State Masonry	Masonry	22	880	8480
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	60	2400	46320
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	16	832	42974
Rival Construction Inc.	Concrete	34	1500	13191
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	20	800	12622
Silt Fence Installation	Site Erosion Control	0	0	1023
Southern Mechanical Inc.	Electrical/Plumbing	23	1200	9690
Steel Toe	Labor Force	6	240	3920
Tree South	Arborist	0	0	1431
Upstate Curb	Curb and Gutter	0	0	460



Superintendents Weekly Activity Report #71  
Douthitt Hills Student Community, Clemson University Project  
Joe Jett



# HOLDER CONSTRUCTION COMPANY

## Superintendents Weekly Activity Report #71


### Douthit Hills Student Community, Clemson University Project

Joe Jett



## WEATHER


### CURRENT WEEK



Rain Days This Week = 0

Rain Days To Date = 50

### SAFETY REVIEW LOG

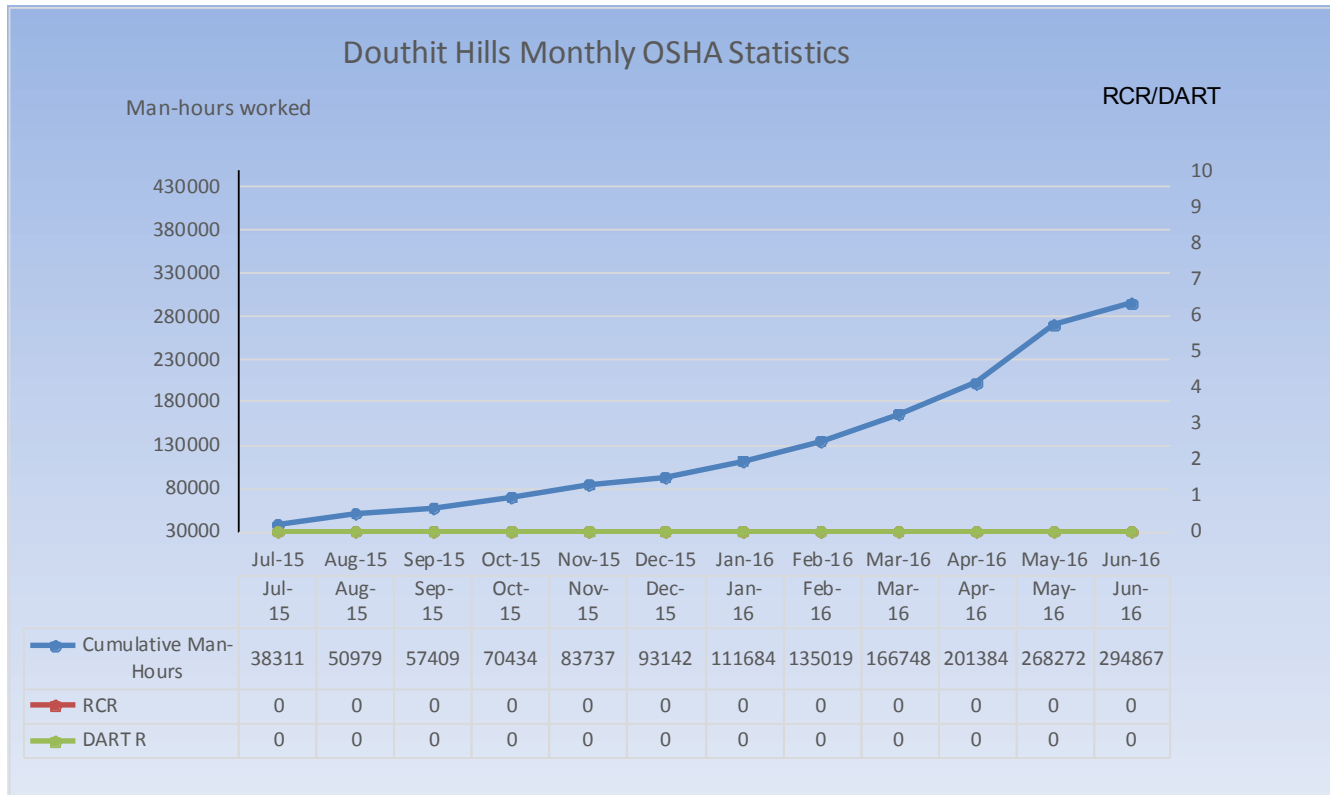

# HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #71  
Douthit Hills Student Community, Clemson University Project  
Joe Jett



## MANPOWER CHART

