

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #74
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 14985
- » Total Man Hours on Project: 342255
- » Crafts On Project This Week: 18
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone


- » Continued Brick @ Building F and E.
- » Continued Cleaning Brick @ Building G.
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Gutters @ Building F.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Building G & F.
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Building G and F.
- » Continued Hanging & Finishing Drywall @ Building G.
- » Continued Sanitary Rough-in @ Building E.
- » Continued Curtain Walls @ Building E.



Bldg. G Elevator Door Framing



Bldg. E Basement SOG

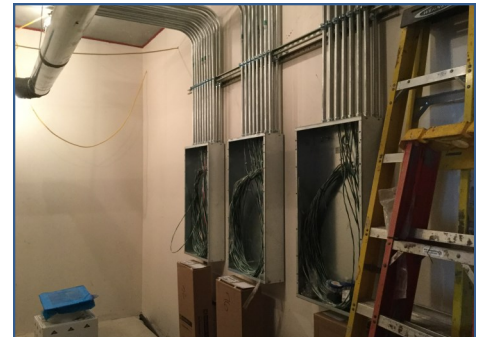

Bldg. F Electrical Panels

SITE, HUB, & WEST ZONE

- » Continued Precast @ Building B.
- » Poured 3rd Floor Topping Slab @ Building A.
- » Poured CIP Walls and Foundations @ Building C.
- » Continued Setting Chambers @ Underground Detention System.
- » Continued Roadwork & Utility Work @ Daniel Square Entrance.
- » Continued Ductbank North of Building B.
- » Continued Pulling Medium Voltage Cable.
- » Poured SOG @ HUB.



HUB Basement SOG




HUB Elevated Level 3



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Setting Showers @ Building G and F.
- » Continue Hanging and Finishing Drywall @ Building G.
- » Continue Setting Showers @ Building G and F.
- » Continue Sanitary Rough-in @ Building E.
- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building E and Building F.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Sprinklers @ Building F.
- » Begin Main Trunk Lines @ Building F.
- » Continue Domestic Water Rough-In @ Building F.

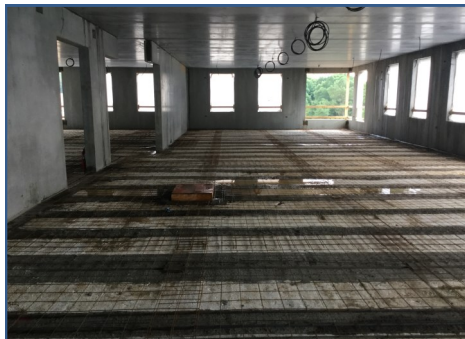

Bldg. A 2nd Floor Slab Prep



Bldg. B Precast



Bldg. C CIP Walls

SITE, HUB, & WEST ZONE

- » Pour HUB Elevated Deck 3C.
- » Continue Setting Chambers @ Underground Detention System.
- » Set Chillers @ HUB.
- » Continue Topping Slab Prep @ Building A.
- » Continue CIP Walls @ Building C.
- » Continue Underground Electrical @ HUB.
- » Continue Roadwork and Utility @ Daniel Square Entrance.
- » Continue Precast @ Building B.



Chambers at Underground Detention



Building B Ductbank to Transformer

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #74
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	37	1665	58865
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	360	5994
Carolina Fire Protection	Sprinklers	7	315	3425
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	540	13350
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	30	1350	18674
Gregory Electric	Aboveground Electric	6	270	1550
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	180	3562
Johnson Controls	Building Controls	3	135	975
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	15	675	8467
King Asphalt	Asphalt	0	0	2329
Kone	Elevators	2	90	503
Labor Finders	Labor Force	11	495	24383
Metro Power	Underground Electrical	11	495	16387
Old North State Masonry	Masonry	23	1035	11499
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	50	2250	53370
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	15	675	45313
Rival Construction Inc.	Concrete	35	1575	19276
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	30	1350	16762
Silt Fence Installation	Site Erosion Control	0	0	1031
Southern Mechanical Inc.	Electrical/Plumbing	23	1035	13125
Steel Toe	Labor Force	5	225	4685
Tree South	Arborist	2	90	1531



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #74
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	180	1484
Total		333	14985	342255



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #74
 Douthit Hills Student Community, Clemson University Project
 Joe Jett




WEATHER

CURRENT WEEK

3 Scattered Clouds Actual: 100° 73° 0.06 in Average: 88° 66° 0.10 in	4 Scattered Clouds Actual: 98° 75° 0.00 in Average: 88° 66° 0.30 in	5 Clear Actual: 97° 78° 0.00 in Average: 88° 66° 0.23 in	6 Tstorm Actual: 97° 75° 0.00 in Average: 88° 66° 0.13 in	7 Tstorm Actual: 96° 73° 0.03 in Average: 87° 66° 0.11 in	8 Clear Forecast: 100° 77° 0.02 in Average: 89° 66° 0.11 in	9 Partly Cloudy Forecast: 98° 74° 0.0 in Average: 90° 66° 0.04 in
---	--	---	--	--	--	--

Rain Days This Week = 1 Rain Days To Date = 52

SAFETY REVIEW LOG

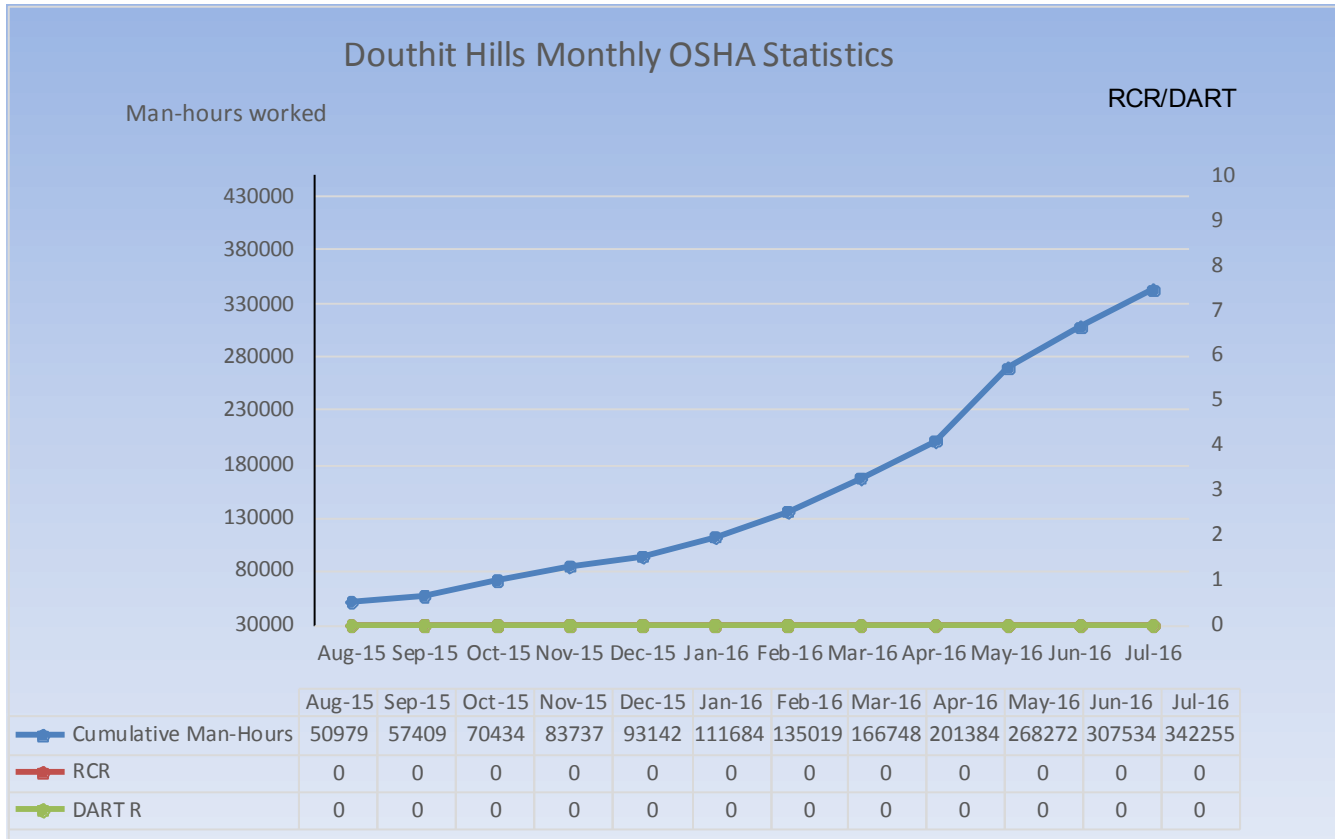

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #74
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

