

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #76
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 17830
- » Total Man Hours on Project 376485
- » Crafts On Project This Week: 21
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Building F and E.
- » Continued Setting IDU Units.
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Installing DEFS @ Soffits.
- » Continued Electrical Rough-In @ Building F.
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Building F.
- » Continued Hanging & Finishing Drywall @ Building G.
- » Continued Sanitary Rough-in @ Building E.
- » Continued Curtain Walls @ Building E.
- » Continued Interior Framing @ Building E.



Bldg. G IDU Units

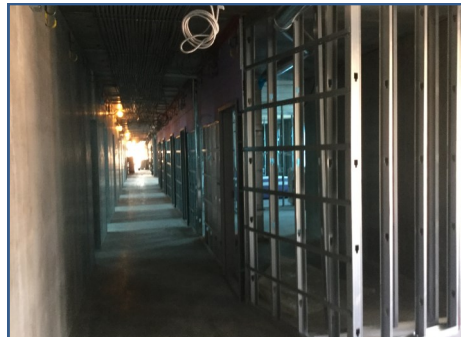

Bldg. E Wall Framing



Bldg. F Mechanical Room

SITE, HUB, & WEST ZONE

- » Poured 1st Floor Topping Slab @ Building A.
- » Poured Foundations @ Building C.
- » Continued Setting Chambers @ Underground Detention System.
- » Continued Roadwork & Utility Work @ Daniel Square Entrance.
- » Continued Final Grading For Sidewalks.
- » Began CMU @ HUB.
- » Poured SOG 3 @ HUB.
- » Graded For Building D Pad.
- » Tied in Foundation Drain @ Building B.



HUB CMU Walls



HUB SOG



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Setting Showers @ Building G and F.
- » Continue Hanging and Finishing Drywall @ Building G.
- » Continue Setting IDU Units @ Building G.
- » Continue Sanitary Rough-in @ Building E.
- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building E and Building F.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Sprinklers @ Building F.
- » Continue Main Trunk Lines @ Building F.
- » Continue Domestic Water Rough-In @ Building F.



Bldg. A Roof Trusses & Decking



Bldg. B Precast



Bldg. C Stem Walls

SITE, HUB, & WEST ZONE

- » Begin Forming Sidewalks.
- » Continue Setting Chambers @ Underground Detention System.
- » Pave Daniel Square Entrance.
- » Continue Roof Decking @ Building A.
- » Continue CMU @ HUB.
- » Begin Building D Foundations.
- » Pour Roof-A @ HUB.
- » Continue Precast @ Building B.
- » Continue Foundations @ Building C.



Chambers at Underground Detention



Trench Drain at Daniel Square Entrance

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #76
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	37	1850	62565
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	400	6794
Carolina Fire Protection	Sprinklers	7	350	4125
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	14550
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	32	1600	21774
Gregory Electric	Aboveground Electric	6	300	2150
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	180	3922
Johnson Controls	Building Controls	3	150	1275
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	17	850	10067
King Asphalt	Asphalt	0	0	2329
Kone	Elevators	2	100	703
Labor Finders	Labor Force	11	550	25483
Metro Power	Underground Electrical	10	400	17287
Old North State Masonry	Masonry	23	1150	13799
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	50	2500	58370
Pyramid Masonry	Masonry	9	270	270
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	12	600	46663
Rival Construction Inc.	Concrete	35	1750	22776
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	53	2650	20912
Silt Fence Installation	Site Erosion Control	0	0	1031
Southern Mechanical Inc.	Electrical/Plumbing	23	1150	15425
Steel Toe	Labor Force	5	250	5185



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #76
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Tree South	Arborist	5	100	1671
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	80	1644
Total		368	17830	376485



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #76

Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Actual Rain	Average High/Low	Average Rain
17	Tstorm	95° 72°	1.09 in	90° 67°	0.03 in
18	Tstorm	96° 73°	0.00 in	90° 67°	0.13 in
19	Scattered Clouds	98° 73°	0.00 in	90° 67°	0.11 in
20	Scattered Clouds	100° 75°	0.00 in	91° 68°	0.09 in
21	Tstorm	93° 75°	0.00 in	91° 68°	0.03 in
22	Clear	Forecast: 95° 73°	0.0 in	Average: 91° 68°	0.18 in
23	Partly Cloudy	Forecast: 98° 74°	0.0 in	Average: 90° 68°	0.17 in

Rain Days This Week = 0

Rain Days To Date = 52

SAFETY REVIEW LOG

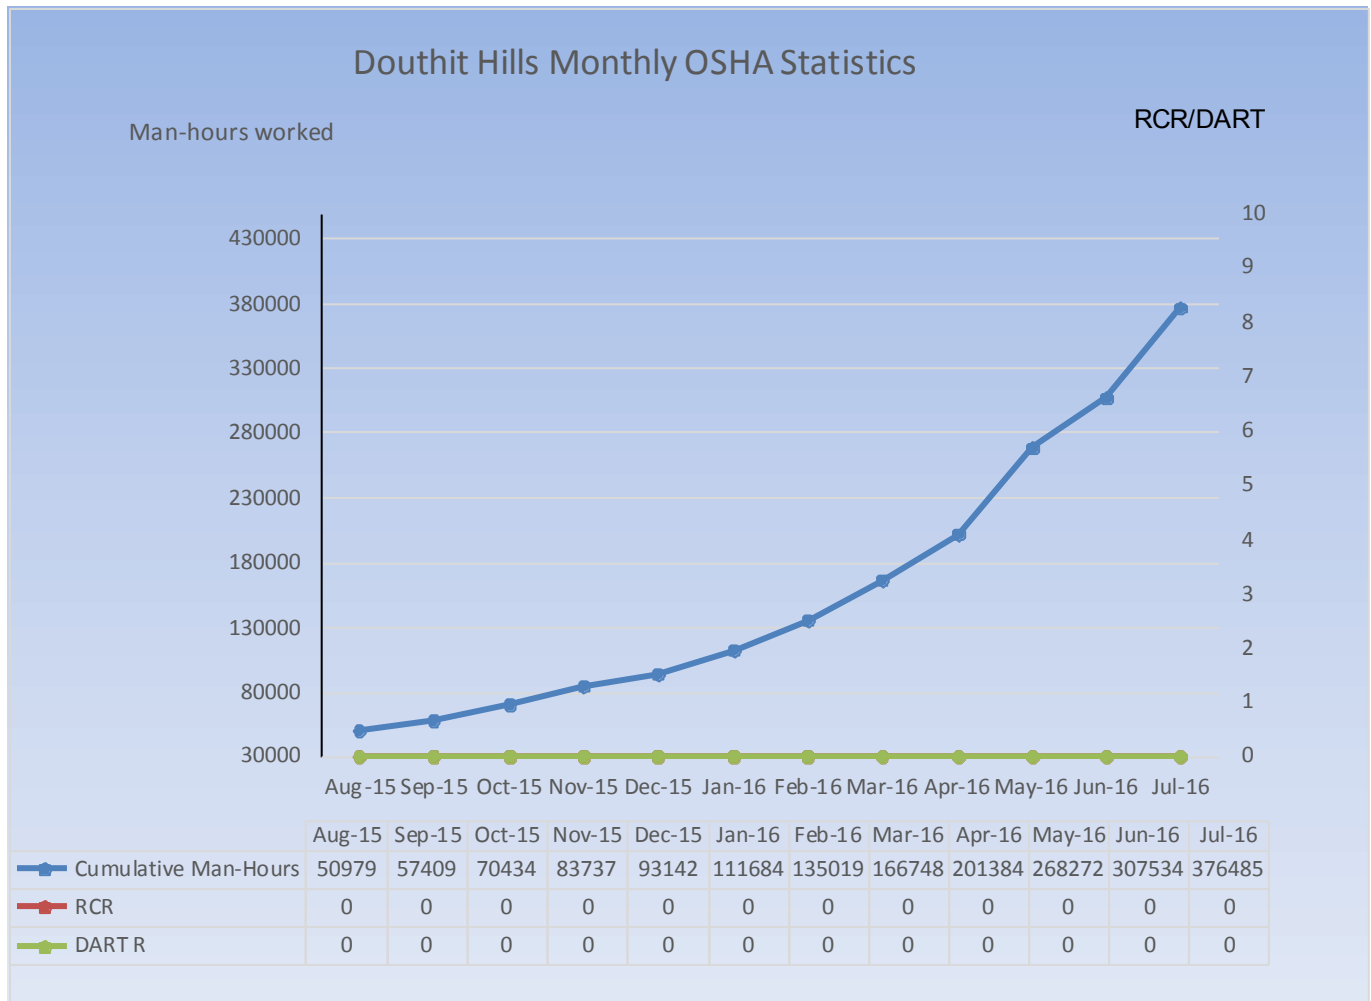

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #76
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

