

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #73
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 16136
- » Total Man Hours on Project: 327270
- » Crafts On Project This Week: 18
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Building F and E.
- » Continued Cleaning Brick @ Building G.
- » Continued Elevators @ Building G.
- » Continued Mechanical Rough-In @ Building F.
- » Continued Gutters @ Building F.
- » Continued Electrical Rough-In @ Building F.
- » Continued Sprinklers @ Building G & F.
- » Continued Roofing @ Building E.
- » Continued Setting Showers @ Building G and F.
- » Continued Hanging & Finishing Drywall @ Building G.
- » Continued Sanitary Rough-in @ Building E.
- » Continued Glazing @ Building E.



Bldg. G Basement Overhead Rough-In



Bldg. E Curtain Wall



Bldg. F 1st Floor Overhead Rough-In

SITE, HUB, & WEST ZONE

- » Continued Precast @ Building B.
- » Poured 4th Floor Topping Slab @ Building A.
- » Continued Pouring Columns and Walls @ HUB.
- » Poured CIP Walls and Foundations @ Building C.
- » Continued Topping Slab Rough-In @ Building A.
- » Continued Underground Electrical @ HUB.
- » Continued Prep for SOG @ HUB.
- » Continued Underground Detention System.
- » Continued Waterline 3.
- » Continued Pulling Medium Voltage Cable.



Cooling Towers



Underground Electrical @ HUB



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Setting Showers @ Building G and F.
- » Continue Hanging and Finishing Drywall @ Building G.
- » Continue Setting Showers @ Building G and F.
- » Continue Sanitary Rough-in @ Building E.
- » Continue Overhead Rough-In @ Buildings G & F.
- » Continue Brick @ Building E and Building F.
- » Continue Glazing @ Building E.
- » Continue Elevators @ Building G.
- » Continue Sprinklers @ Building F.



Bldg. A 4th Floor Slab Rough-In



Bldg. B Precast



Bldg. C CIP Walls

SITE, HUB, & WEST ZONE

- » Pour HUB Elevated Deck 3B.
- » Continue Excavation For Underground Detention System.
- » Tie-In 36" and 24" Chiller Lines to HUB.
- » Continue Topping Slab Prep @ Building A.
- » Continue CIP Walls @ Building C.
- » Continue Underground Electrical @ HUB.
- » Begin Underground Utility Work @ Daniel Square Entrance.
- » Continue Precast @ Building B.



Building A 4th Floor Topping Slab Rough-In



Building B Precast

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #73
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	37	1480	57200
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	8	400	5634
Carolina Fire Protection	Sprinklers	7	320	3110
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	12810
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	30	1440	17324
Gregory Electric	Aboveground Electric	6	260	1280
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	4	150	3382
Johnson Controls	Building Controls	3	120	840
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	15	600	7792
King Asphalt	Asphalt	0	0	2329
Kone	Elevators	2	93	413
Labor Finders	Labor Force	13	600	23888
Metro Power	Underground Electrical	11	497	15892
Old North State Masonry	Masonry	23	1104	10464
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	60	2400	51120
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	16	832	44638
Rival Construction Inc.	Concrete	32	2200	17701
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	30	1440	15412
Silt Fence Installation	Site Erosion Control	0	0	1031
Southern Mechanical Inc.	Electrical/Plumbing	23	1200	12090
Steel Toe	Labor Force	6	270	4460
Tree South	Arborist	2	10	1441

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #73
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Upstate Curb	Curb and Gutter	0	0	460
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	4	120	1304
Total		344	16136	327270




HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #73
 Douthit Hills Student Community, Clemson University Project
 Joe Jett




WEATHER

CURRENT WEEK



SAFETY REVIEW LOG

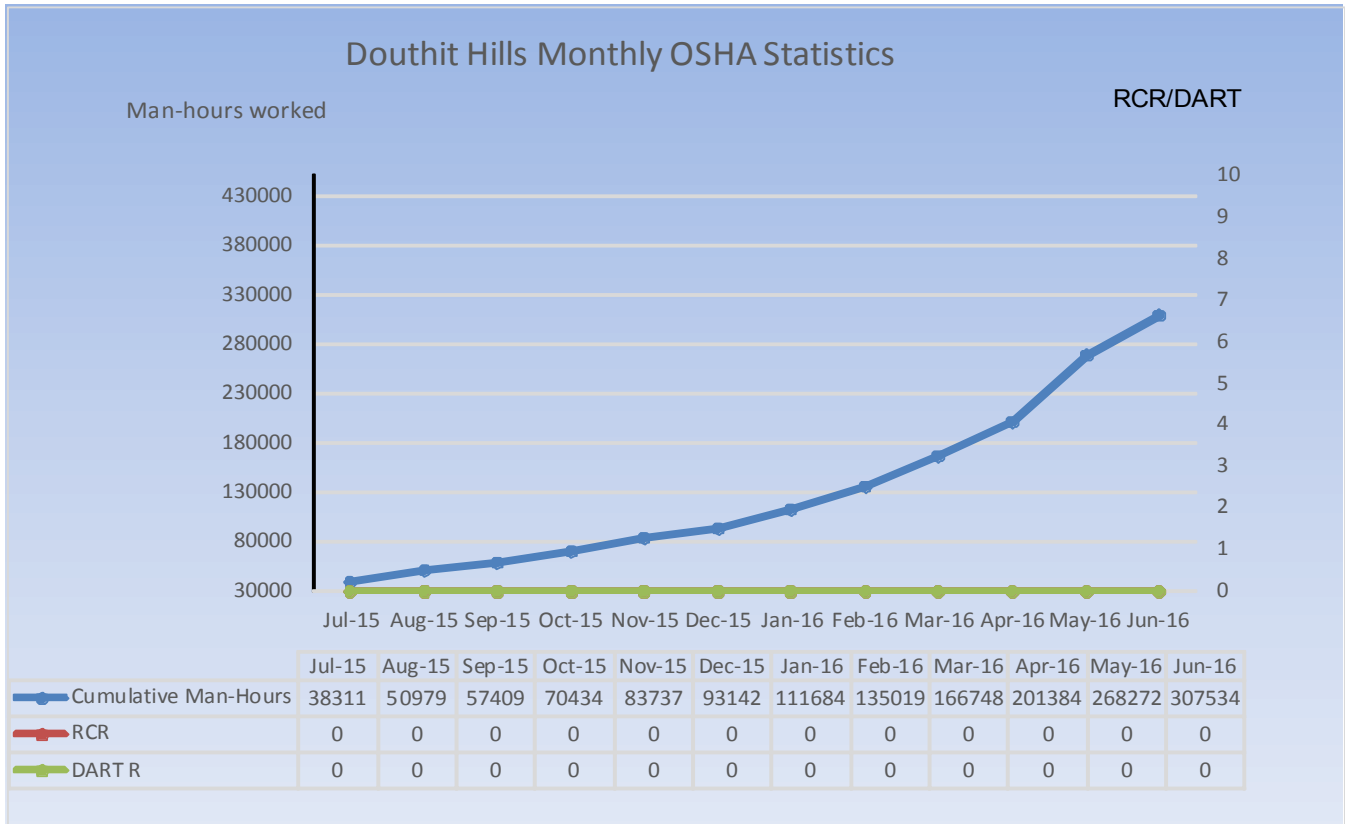

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #73
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

