



SAFETY

- » Total Man Hours Worked This Week: 19744
- » Total Man Hours on Project: 433865
- » Crafts On Project This Week: 20
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Buildings F and E.
- » Continued Setting IDU Units.
- » Continued Elevators @ Building G and F.
- » Continued Mechanical Rough-In @ Buildings F and E.
- » Continued Mechanical Room Conduit @ Building G.
- » Continued Installing DEFS @ Buildings G & F.
- » Continued Electrical Rough-In @ Building E.
- » Continued Setting Showers @ Building F.
- » Continued Hanging & Finishing Drywall @ Buildings G & F.
- » Continued Interior Framing @ Building E.
- » Install Dampers and Flex IDU @ Building G.



Bldg. G Interior Soffit Framing



Bldg. E Overhead Rough In



Bldg. F Columns

SITE, HUB, & WEST ZONE

- » Continued CMU Walls @ HUB.
- » Continued Foundations & CIP Walls @ Building D.
- » Continued Backfill @ Building C.
- » Poured Curb & Gutter @ Martin Street & West Parking Lot.
- » Continued Chiller Piping @ HUB Basement.
- » Continued Roofing @ Building A.
- » Poured Parapet Walls @ HUB.
- » Poured 7th Floor Topping Slab @ Building B.
- » Continued Sequence 2 Precast @ Building B.
- » Continued Interior Framing @ Building A.
- » Continued Windows @ Building A.



Martin Street Curb and Gutter



HUB Stair Forms



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Hanging and Finishing Drywall @ Building F.
- » Begin Elevators @ Building E.
- » Continue Setting IDU Units @ Building G & F.
- » Continue Sanitary Rough-in @ Building E.
- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Brick @ Building E and Building F.
- » Continue Interior Framing @ Building E.
- » Continue Elevators @ Building F & G.
- » Continue Electrical Panels @ Building F.
- » Continue Electrical Rough-In @ Building E.
- » Continue 3rd Floor Communications Room @ Building G.



Bldg. A Shingles



Bldg. B 6th Floor Topping Slab



Bldg. D CIP Walls and Foundations

SITE, HUB, & WEST ZONE

- » Continue Roofing @ Building A.
- » Continue CMU Walls @ HUB.
- » Continue Building D Foundations & CIP Walls.
- » Pour Parapet Walls @ HUB.
- » Continue Sequence 2 Precast @ Building B.
- » Continue Curb and Gutter @ West Parking Lot.
- » Continue Interior Framing @ Building A.
- » Continued Windows @ Building A.
- » Continue Brick Relief Angle @ Building B.
- » Begin Brick Relief Angle @ HUB.
- » Set Jib Crane @ HUB.



Building A Window Frames



Building A Flat Roof System

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #80
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	31	1550	67815
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	0	0	650
Carolina Fire Protection	Sprinklers	14	700	5725
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	16350
D.H. Griffin	Tank Foundation Removal	0	0	90
Gainesville Mechanical	Ductwork	44	2200	28174
Gill Plumbing	Plumbing	7	350	1550
Gregory Electric	Aboveground Electric	11	550	3300
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	7	315	4597
Johnson Controls	Building Controls	3	150	1725
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	20	1000	12767
King Asphalt	Asphalt	0	0	3169
Kone	Elevators	2	100	1003
Labor Finders	Labor Force	13	650	27233
Metro Power	Underground Electrical	4	160	18087
Nations Roofing	Roofing	10	500	500
Old North State Masonry	Masonry	20	1000	17399
Osteen	Chill Water pipe	0	0	2114
Precision	Concrete	54	2700	65070
Pyramid Masonry	Masonry	8	240	1170
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	9	450	48263
Rival Construction Inc.	Concrete	18	900	26276
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	69	3450	29662



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #80
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Silt Fence Installation	Site Erosion Control	0	0	1031
Southern Mechanical Inc.	Electrical/Plumbing	31	1705	19430
Steel Toe	Labor Force	5	250	5935
Tree South	Arborist	0	0	1871
Upstate Curb	Curb and Gutter	7	224	684
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	0	0	1724
Total		399	19744	433609



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #80
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK



Rain Days This Week = 0

Rain Days To Date = 52

SAFETY REVIEW LOG

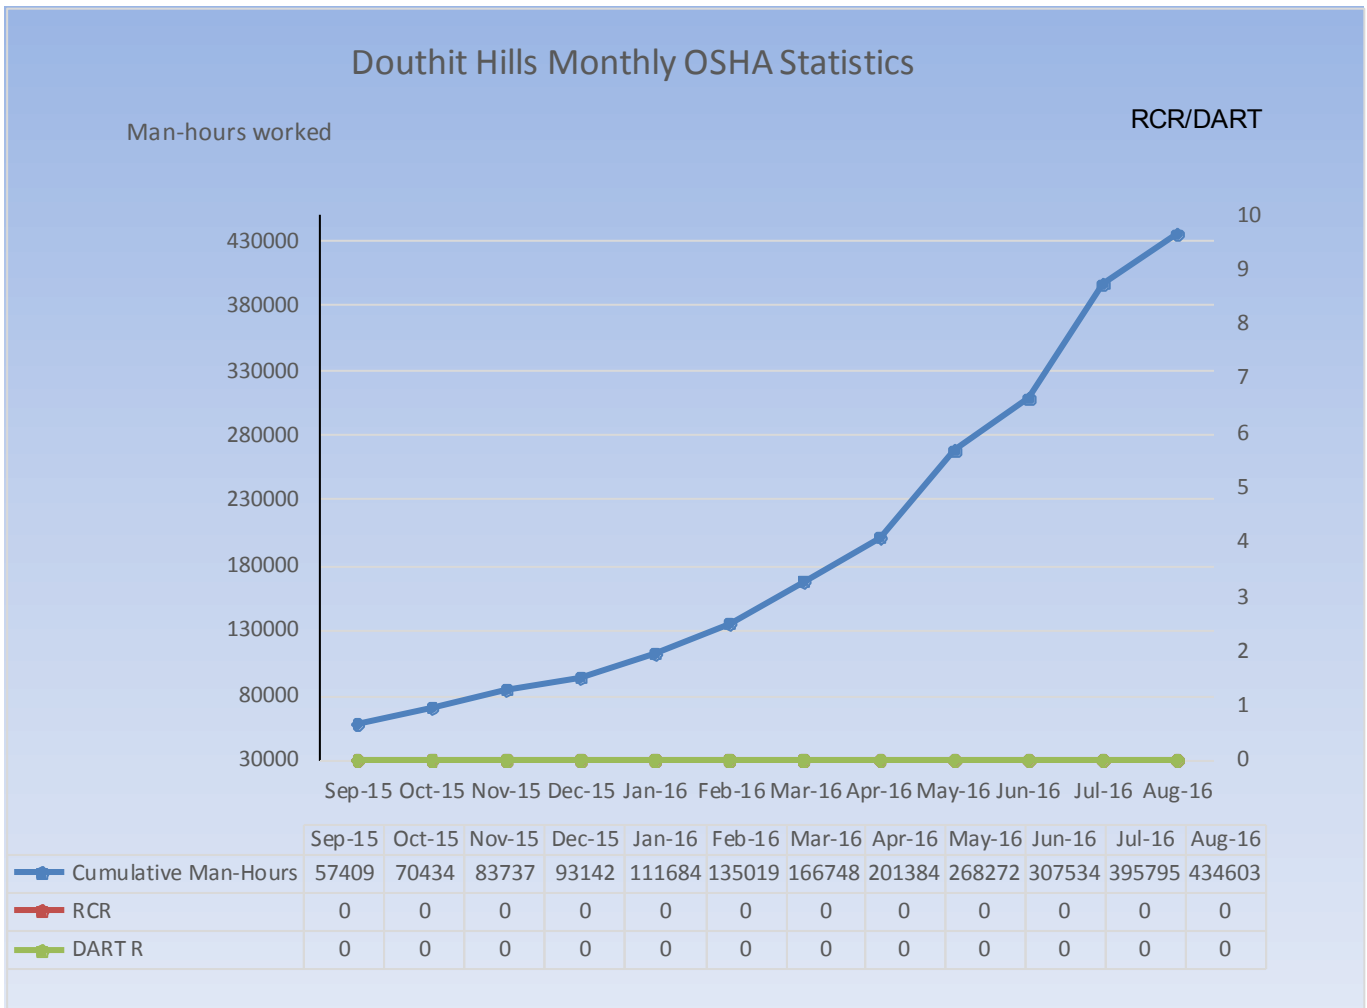

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #80
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

