

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #83
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 21345
- » Total Man Hours on Project: 497557
- » Crafts On Project This Week: 19
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Buildings F and E.
- » Tied In Downspouts @ Building G.
- » Continued Elevators @ Buildings E and F.
- » Continued Mechanical Rough-In @ Buildings F and E.
- » Framed Interior Soffits @ Building G.
- » Continued Installing DEFS @ Buildings E & F.
- » Continued Electrical Rough-In @ Building E.
- » Continued Framing Interior Ceilings @ Building G.
- » Continue Interior Framing @ Building E.
- » Continued Setting Showers @ Building E.
- » Continued Fire Caulking @ Building G.



Bldg. G Interior Soffit Rough In



Bldg. E Overhead Rough-In



Bldg. F Mechanical Room

SITE, HUB, & WEST ZONE

- » Continued CMU Walls @ HUB.
- » Continued CIP Walls @ Building D.
- » Continued Exterior Wall Framing @ HUB.
- » Continued Chiller Piping @ HUB Basement.
- » Continued Final Grading for Sidewalks.
- » Continued Brick Masonry @ Building A.
- » Poured 2nd Floor Topping Slab @ Building B.
- » Completed Precast @ Building B.
- » Began Precast @ Building C.
- » Continued Interior Framing @ Building A.
- » Continued Brick Relief Angle @ HUB.
- » Continued Interior Framing @ HUB.



Final Grading For Sidewalks



HUB CMU Wall



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Hanging Drywall @ Building E.
- » Continue DEFS @ Buildings F & E.
- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Brick @ Buildings E & F.
- » Continue Interior Framing @ Building E.
- » Continue Electrical Rough-In @ Building E.
- » Continue Downspouts @ Building F.
- » Continue Fire Protection @ Building E.
- » Continue Mechanical Rough-in @ Building E.
- » Continue Fire Caulking @ Building G.
- » Continue Hanging IDUs @ Building E



Bldg. A Brick



Bldg. B Completed Precast



Bldg. C Precast

SITE, HUB, & WEST ZONE

- » Continue CMU Walls @ HUB.
- » Continue Brick Relief Angle @ HUB.
- » Continue Brick Masonry @ Building A.
- » Continue Building C Precast.
- » Continue Backfill @ Building D.
- » Pour Topping Slab @ Building B.
- » Continue Interior Framing @ Building A.
- » Continue Brick @ Building A.
- » Continue Exterior Framing @ HUB.
- » Prep For Stone Base @ Martin Street.
- » Continue Exterior Soffit Board @ Building A.



HUB Stair Forms



Building B 1st Floor Slab Prep

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #83
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	38	1900	73165
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	0	0	650
Carolina Fire Protection	Sprinklers	18	900	8425
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	18150
D.H. Griffin	Tank Foundation Removal	0	0	90
Feltman Brothers	West - Masonry	11	550	1000
Gainesville Mechanical	Ductwork	30	1650	34279
Gill Plumbing	Plumbing	13	650	3150
Gregory Electric	Aboveground Electric	12	600	5100
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	270	5407
Johnson Controls	Building Controls	3	150	2175
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	20	1100	16892
King Asphalt	Asphalt	0	0	3169
Kone	Elevators	2	100	1303
Labor Finders	Labor Force	17	935	30038
Metro Power	Underground Electrical	4	160	18567
Nations Roofing	Roofing	0	0	775
Old North State Masonry	East - Masonry	18	990	20589
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	40	2000	71270
Pyramid Masonry	Hub—Masonry	10	300	1950
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	18	900	51213
Rival Construction Inc.	Concrete	17	850	28376
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380






WEATHER

CURRENT WEEK

4	Partly Cloudy	5	Scattered Clouds	6	Clear	7	Scattered Clouds	8	Scattered Clouds	9	Scattered Clouds	10	Clear
Actual: 87° 70° 0.00 in		Actual: 90° 69° 0.00 in		Actual: 95° 69° 0.00 in		Actual: 96° 70° 0.00 in		Actual: 97° 71° 0.00 in		Actual: 97° 72° 0.00 in		Forecast: 95° 72° 0.0 in	
Average: 85° 65° 0.24 in		Average: 84° 64° 0.16 in		Average: 84° 63° 0.10 in		Average: 84° 63° 0.12 in		Average: 84° 63° 0.27 in		Average: 85° 62° 0.07 in		Average: 84° 62° 0.05 in	
Rain Days This Week = <u>0</u>						Rain Days To Date = <u>53</u>							

SAFETY REVIEW LOG

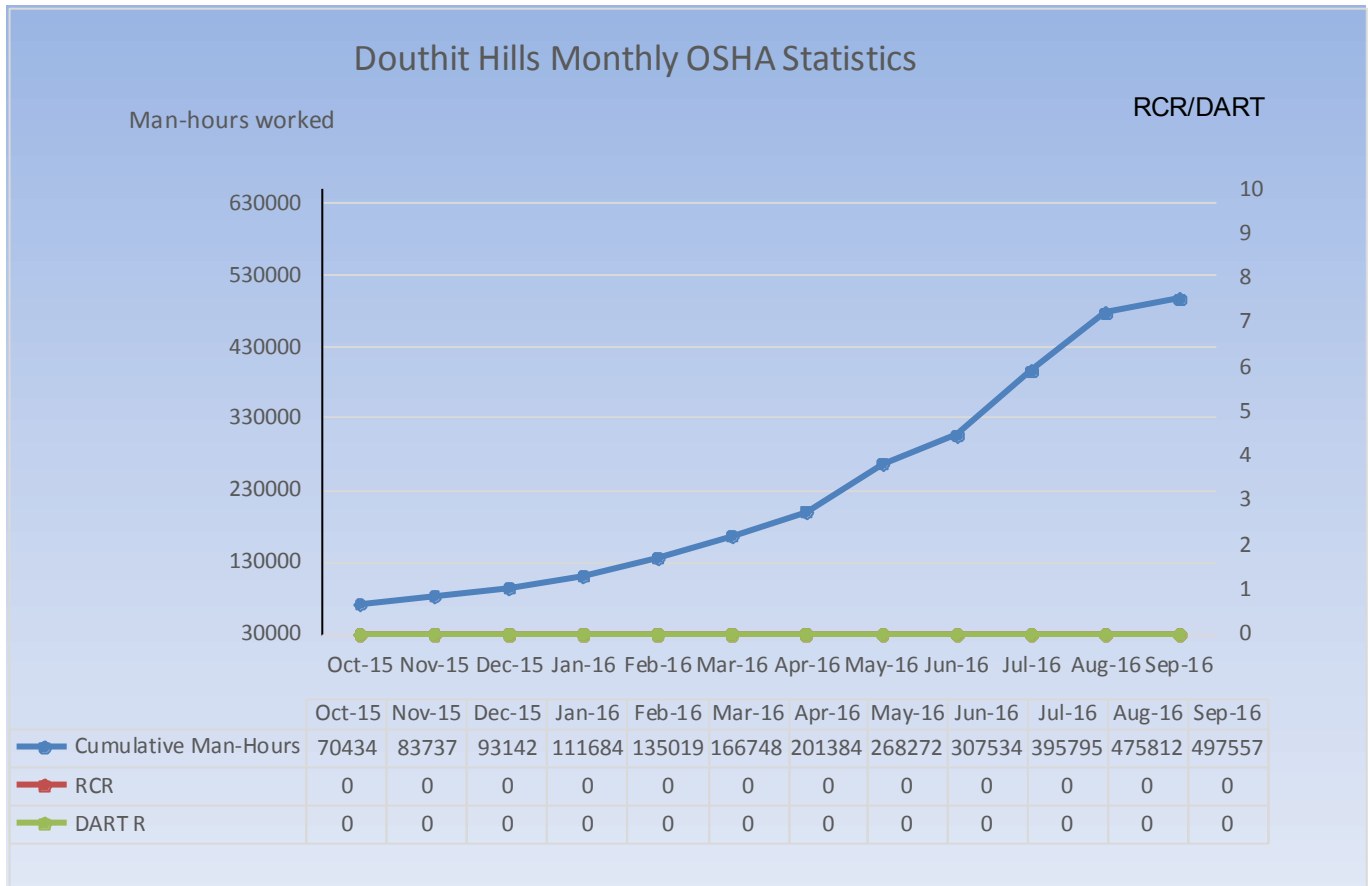

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #83
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

