

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #82
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 20685
- » Total Man Hours on Project: 475812
- » Crafts On Project This Week: 20
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Buildings F and E.
- » Tied In Downspouts @ Building G.
- » Continued Elevators @ Buildings E and F.
- » Continued Mechanical Rough-In @ Building F and E.
- » Framed Interior Soffits @ Building G.
- » Continued Installing DEFS @ Buildings E & F.
- » Continued Electrical Rough-In @ Building E.
- » Continued Framing Interior Ceilings @ Building G.
- » Continued Interior Framing @ Building E.
- » Continued Dampers and Flex IDU @ Building F.
- » Continued Fire Caulking @ Building G.



Bldg. G Downspouts



Bldg. E Switchgear



Bldg. F Overhead Rough-In

SITE, HUB, & WEST ZONE

- » Continued CMU Walls @ HUB.
- » Continued CIP Walls @ Building D.
- » Continued Exterior Wall Framing @ HUB.
- » Continued Chiller Piping @ HUB Basement.
- » Tied in Sanitary Lines @ Buildings A & C.
- » Began Brick Masonry @ Building A.
- » Poured 3rd Floor Topping Slab @ Building B.
- » Set Jib Crane @ HUB.
- » Continued Interior Framing @ Building A.
- » Continued Windows @ Building A.
- » Began Brick Relief Angle @ HUB.
- » Began Interior Framing @ HUB.



HUB Exterior Wall Framing




HUB Stairs



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Hanging and Finishing Drywall @ Building F.
- » Continue DEFS @ Building F.
- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Brick @ Building E and Building F.
- » Continue Interior Framing @ Building E.
- » Continue Electrical Rough-In @ Building E.
- » Continue Hanging Exterior Soffit @ Building E.
- » Begin Downspouts @ Building F.
- » Continue Fire Protection @ Building E.
- » Continue Hanging Controllers @ Building E.
- » Continue Mechanical Rough-in @ Building E.

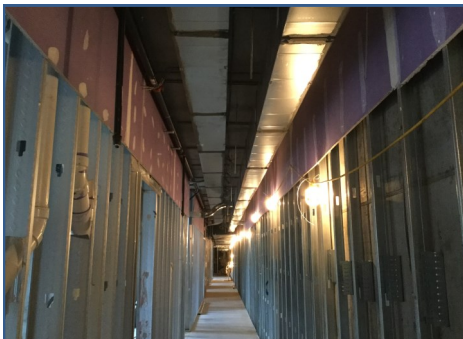

Bldg. A Overhead Rough-In




Bldg. B Transformer Pad



Bldg. D CIP Walls

SITE, HUB, & WEST ZONE

- » Continue CMU Walls @ HUB.
- » Continue Brick Relief Angle @ HUB.
- » Continue Brick Masonry @ Building A.
- » Continue Building D CIP Walls.
- » Continue Sequence 2 Precast @ Building B.
- » Pour Topping Slab @ Building B.
- » Continue Interior Framing @ Building A.
- » Continued Windows @ Building A.
- » Continue Exterior Framing @ HUB.
- » Place Stone Base @ Martin Street.
- » Continue Exterior Soffit Board @ Building A.

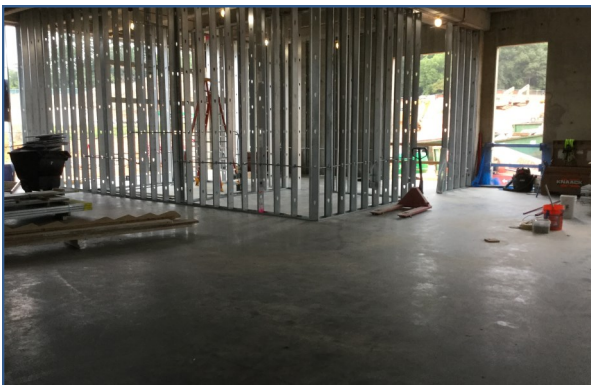

HUB Interior Framing



HUB Jib Crane

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #82
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	30	1500	70865
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	0	0	650
Carolina Fire Protection	Sprinklers	18	900	7525
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	17550
D.H. Griffin	Tank Foundation Removal	0	0	90
Feltman Brothers	West - Masonry	9	450	450
Gainesville Mechanical	Ductwork	40	2200	32629
Gill Plumbing	Plumbing	12	600	2500
Gregory Electric	Aboveground Electric	12	600	4500
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	270	5137
Johnson Controls	Building Controls	3	150	2025
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	28	1540	15792
King Asphalt	Asphalt	0	0	3169
Kone	Elevators	2	100	1203
Labor Finders	Labor Force	17	935	29103
Metro Power	Underground Electrical	4	160	18407
Nations Roofing	Roofing	0	0	775
Old North State Masonry	East - Masonry	20	1100	19599
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	30	1500	69270
Pyramid Masonry	Hub-Masonry	8	240	1650
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	17	850	50313
Rival Construction Inc.	Concrete	15	750	27526
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #82


Douthit Hills Student Community, Clemson University Project

Joe Jett




WEATHER

CURRENT WEEK



SAFETY REVIEW LOG

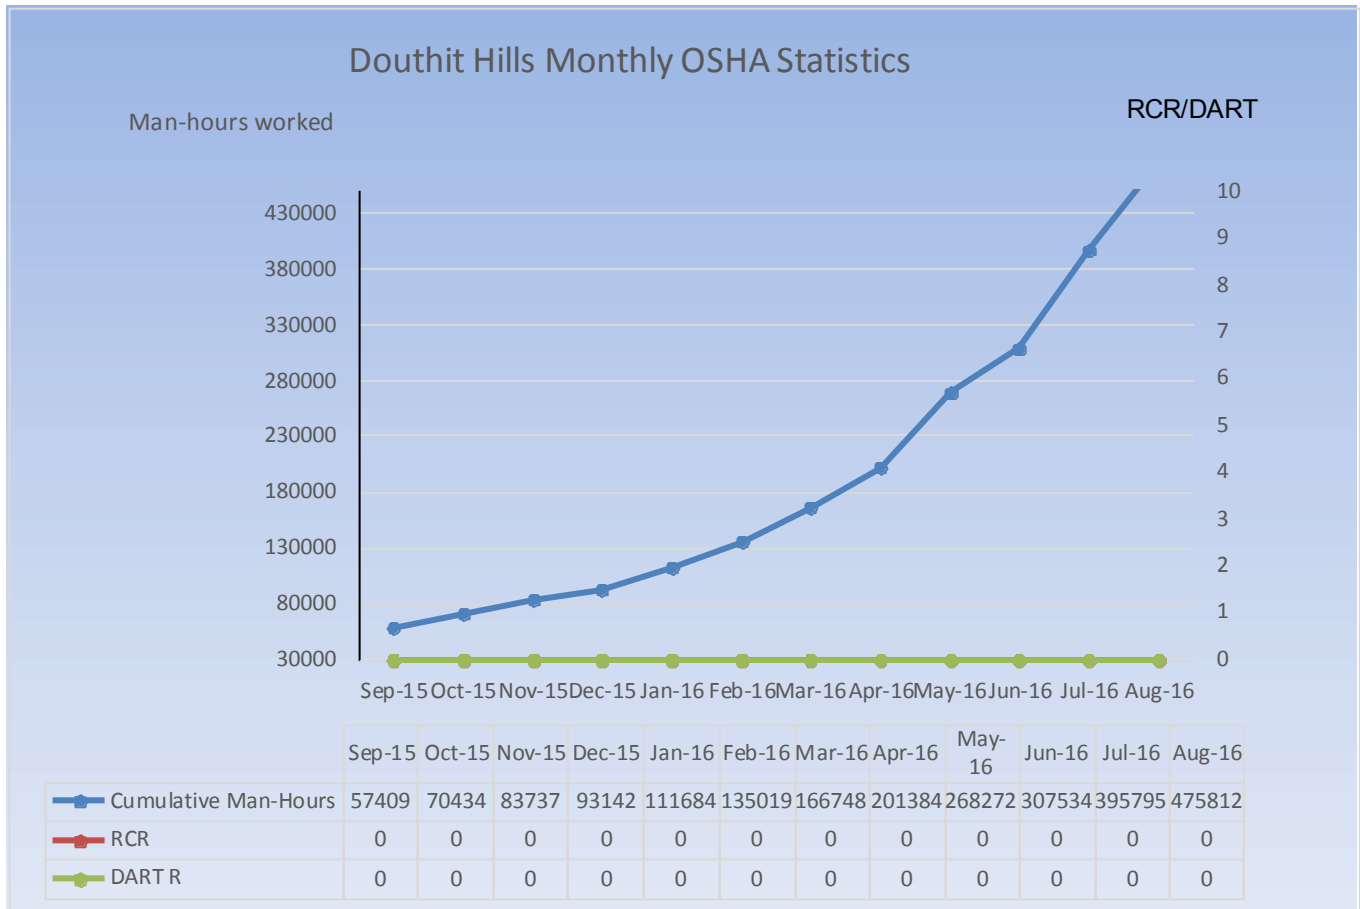

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #82
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

