

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #84
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 21770
- » Total Man Hours on Project: 519327
- » Crafts On Project This Week: 20
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued Brick @ Building E.
- » Poured Sidewalks South of Building G
- » Continued Elevators @ Buildings E and F.
- » Continued Mechanical Rough-In @ Building F and E.
- » Continued Framing Interior Soffits @ Building G.
- » Continued Installing DEFS @ Building E & F.
- » Continued Electrical Rough-In @ Building E.
- » Continued Interior Framing @ Building E.
- » Continued Setting Showers @ Building E.
- » Continued Fire Caulking @ Building G.
- » Continued AHU Tie In @ Building G.



Bldg. G Sidewalks



Bldg. E Areaway



Bldg. F Storefront

SITE, HUB, & WEST ZONE

- » Continued CMU Walls @ HUB.
- » Completed Foundations @ Building D.
- » Continued Exterior Wall Framing @ HUB.
- » Continued Chiller Piping @ HUB Basement.
- » Continued Plumbing Rough In @ Building A.
- » Continued Brick Masonry @ Building A.
- » Paved Martin Street.
- » Continued Precast @ Building C.
- » Continued Interior Framing @ Building A.
- » Continued Brick Relief Angle @ HUB.
- » Continued Interior Framing @ HUB.
- » Continued Final Grading Sidewalks @ Hwy 93.



Martin Street




East Zone



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Hanging Drywall @ Building E.
- » Continue DEFS @ Buildings F & E.
- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Brick @ Building E.
- » Continue Interior Framing @ Building E.
- » Continue Electrical Rough-In @ Building E.
- » Continue Downspouts @ Building F.
- » Continue Fire Protection @ Building E.
- » Continue Mechanical Rough-in @ Building E.
- » Continue Fire Caulking @ Building G.
- » Continue Interior Soffit Framing @ Building G.

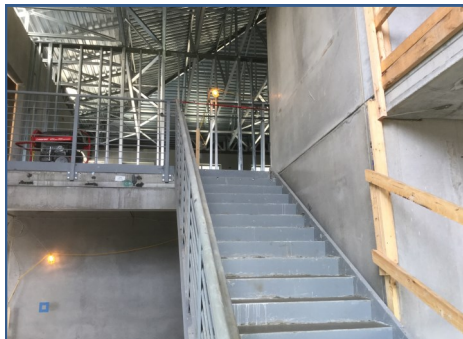

Bldg. A Metal Pan Stairs



Bldg. B Transformer



Bldg. C Precast

SITE, HUB, & WEST ZONE

- » Continue CMU Walls @ HUB.
- » Continue Brick Masonry @ Building A.
- » Continue Building C Precast.
- » Continue Backfill @ Building D.
- » Pour Topping Slab @ Building B.
- » Continue Interior Framing @ Building A.
- » Continue Brick @ Building A.
- » Continue Exterior Framing @ HUB.
- » Pave West Parking Lot.
- » Continue Exterior Soffit Board @ Building A.
- » Remove Tower Crane.



West Parking Lot Prep



HUB Prep For Roofing

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #84
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	38	1900	73165
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	0	0	650
Carolina Fire Protection	Sprinklers	18	900	8425
C&C Fence	Site Fence	0	0	794
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	600	18150
D.H. Griffin	Tank Foundation Removal	0	0	90
Feltman Brothers	West - Masonry	11	550	1000
Gainesville Mechanical	Ductwork	30	1650	34279
Gill Plumbing	Plumbing	20	1000	3500
Gregory Electric	Aboveground Electric	12	600	5100
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	6	270	5407
Johnson Controls	Building Controls	3	150	2175
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	20	1100	16892
King Asphalt	Asphalt	17	510	3679
Kone	Elevators	2	100	1303
Labor Finders	Labor Force	17	680	29783
Metro Power	Underground Electrical	4	160	18567
Nations Roofing	Roofing	3	60	835
Old North State Masonry	East - Masonry	18	990	20589
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	40	2000	71270
Pyramid Masonry	Hub-Masonry	10	300	1950
R.E. Mclean Tank	Tank Demo	0	0	660
Reeves Young	Site Grading & Utilities	18	900	51213
Rival Construction Inc.	Concrete	15	750	28276
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380





WEATHER


CURRENT WEEK

11	Tstorm		12	Tstorm		13	Scattered Clouds		14	Scattered Clouds		15	Clear		16	Partly Cloudy		17	Partly Cloudy	
Actual: 95° 71° 0.00 in	Actual: 90° 72° 0.11 in	Actual: 90° 69° 0.00 in	Actual: 95° 70° 0.00 in	Actual: 96° 71° 0.00 in	Actual: 90° 73° 0.00 in	Forecast: 87° 70° 0.0 in														
Average: 83° 60° 0.12 in	Average: 84° 61° 0.11 in	Average: 84° 61° 0.14 in	Average: 84° 60° 0.21 in	Average: 83° 60° 0.05 in	Average: 83° 61° 0.05 in	Average: 81° 60° 0.09 in														

Rain Days This Week = **0**

Rain Days To Date = **53**

SAFETY REVIEW LOG

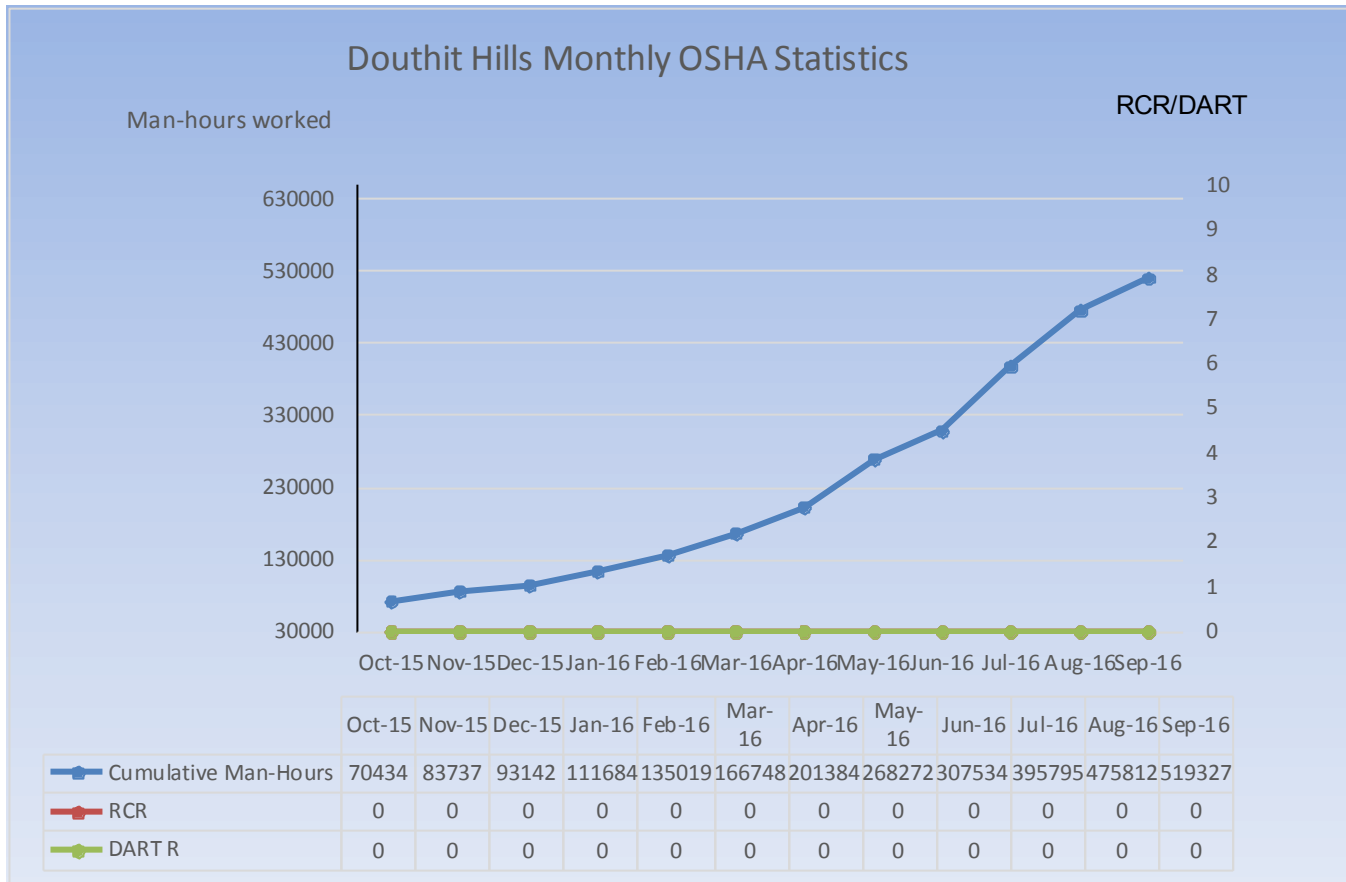

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #84
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER CHART

