

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #91
Douthitt Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 21450
- » Total Man Hours on Project: 669792
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Elevator Inspection @ Building F.
- » Continued Overhead Rough-In @ Buildings E & F.
- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued MEP Trim-out @ Building G.
- » Gas Water Heaters Start-up @ Buildings E & F.
- » Complete Fire Protection Upfit @ Building F.
- » Continued Setting Showers @ Building E.
- » Complete DEFS @ Building E.
- » Continued Hanging Drywall @ Buildings E & F.
- » Continued Finishing Drywall @ Building G.
- » Continued Priming Walls @ Building G.
- » Continued Tile Flooring @ Building G.



Bldg. E Interior Soffit Framing



Bldg. E & F Generators




Bldg. G Bathroom Tile

SITE, HUB, & WEST ZONE

- » Continued Curtain Wall Steel @ HUB.
- » Continued Brick Masonry @ HUB.
- » Continued MEP Rough-In @ HUB.
- » Continued Roofing @ HUB & Building B.
- » Continued Glass Installation @ HUB & Building B.
- » Began Brick Masonry @ Building B.
- » Completed Precast @ Building C.
- » Poured Topping Slab @ Building C.
- » Continued Interior Framing & Drywall @ Building A.
- » Continued DEFS @ Building A.
- » Continued MEP Rough-In @ Building A.
- » De-Mucked Detention Pond.
- » Poured Fire Lane @ East Courtyard.



HUB Brick Masonry

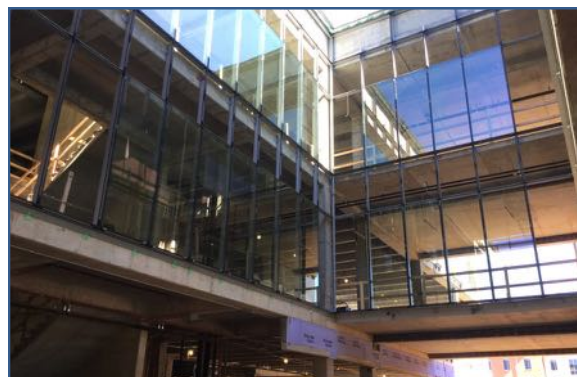


HUB Curtain Wall @ Spine



NEXT WEEK'S ACTIVITIES

East Zone


- » Elevator Inspection @ Building E.
- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue MEP Rough-In @ Building E.
- » Continue FCU Ductwork @ Buildings E & F.
- » Continue MEP Trim-out @ Building G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Setting Showers @ Building E.
- » Continue Hanging Drywall @ Buildings E & F.
- » Continue Finishing Drywall @ Building G.
- » Continue Priming Walls @ Building G.
- » Continue Tile Flooring @ Building G.
- » Pour Pedestrian Sidewalk North of Building F.

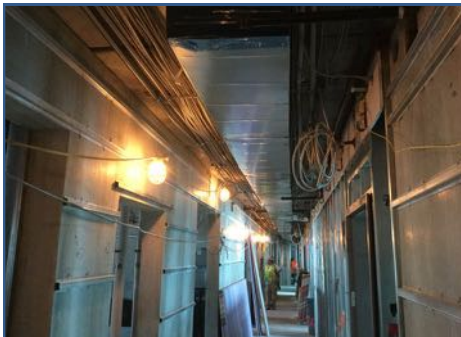

Bldg. A Overhead MEP Rough-In



Bldg. B Brick Masonry

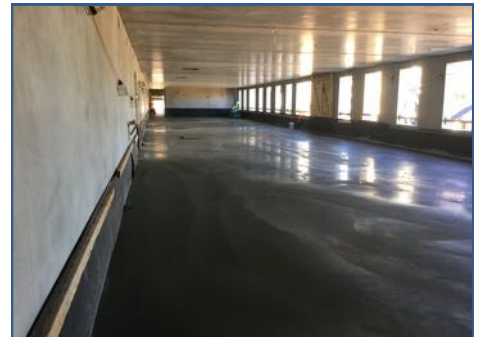

Bldg. C Topping Slab

SITE, HUB, & WEST ZONE

- » Begin Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB.
- » Continue MEP Rough-In @ HUB.
- » Continue Roofing @ HUB & Building B.
- » Continue Glass Installation @ HUB & Building B.
- » Continue Brick Masonry @ Building B.
- » Begin Precast @ Building D.
- » Pour Topping Slab and SOG @ Building C.
- » Continue Interior Framing & Drywall @ Building A.
- » Begin Interior Framing @ Building B.
- » Continue MEP Rough-In @ Building A.
- » Pour Steps @ East Monumental Stair.



Bldg. C Precast Finished



Fire Lane @ East Courtyard

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #91

Douthit Hills Student Community, Clemson University Project

Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

| Subcontractor | Trade | Employees | Man Hours | Total Man Hrs. |
|----------------------------------|-------------------------|-----------|-----------|----------------|
| Holder Construction Company | General Contractor | 39 | 1950 | 88615 |
| American Deep Foundation | Auger Cast Piles | 0 | 0 | 6166 |
| Baker Roofing | Sheathing and Shingles | 0 | 0 | 7194 |
| Brightview Landscape Development | Hardscape & Landscape | 5 | 200 | 2300 |
| Carolina Fire Protection | Sprinklers | 16 | 800 | 14825 |
| C&C Fence | Site Fence | 0 | 0 | 854 |
| Cowart Tree Mulch | Tree Removal | 0 | 0 | 710 |
| Davis Crane Erectors | Pre-Cast Erection | 12 | 600 | 22950 |
| D.H. Griffin | Tank Foundation Removal | 0 | 0 | 90 |
| Elite Flooring | Tile | 3 | 150 | 300 |
| Feltman Brothers | West – Masonry | 25 | 1250 | 8250 |
| Gainesville Mechanical | Ductwork | 33 | 1815 | 48634 |
| Gill Plumbing | Plumbing | 30 | 1500 | 14800 |
| Graham Hodge | Glass | 5 | 250 | 1350 |
| Gregory Electric | Aboveground Electric | 13 | 650 | 10550 |
| Hutch-N-Son | Early Site Work | 0 | 0 | 1337 |
| 1st Choice Glass | Glass | 8 | 360 | 8062 |
| Johnson Controls | Building Controls | 3 | 150 | 3375 |
| JBR Construction | Early Site Work | 0 | 0 | 2049 |
| Johnsons Modern Electric | Aboveground Electrical | 28 | 1540 | 28112 |
| King Asphalt | Asphalt | 0 | 0 | 4189 |
| Kone | Elevators | 2 | 100 | 2103 |
| Labor Finders | Labor Force | 16 | 640 | 35438 |
| Metro Power | Underground Electrical | 6 | 240 | 19967 |
| Nations Roofing | Roofing | 7 | 420 | 3435 |
| Old North State Masonry | East – Masonry | 3 | 165 | 27794 |
| Osteen | Chill Water pipe | 0 | 0 | 2122 |
| Precision | Concrete | 6 | 240 | 82500 |
| Pyramid Masonry | Hub—Masonry | 13 | 390 | 4710 |
| R.E. Mclean Tank | Tank Demo | 0 | 0 | 660 |



Superintendents Weekly Activity Report #91
Douthitt Hills Student Community, Clemson University Project
Joe Jett



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #91

Douthit Hills Student Community, Clemson University Project

Joe Jett



WEATHER


CURRENT WEEK

| | | | | | | | | | | | | | | | | | | | | |
|--------------------|-------|--|--------------------|-------|--|--------------------|------------------|--|--------------------|-----|--|--------------------|-------|--|---------------------|-------|--|---------------------|-------|--|
| 30 | Clear | | 31 | Clear | | 1 | Scattered Clouds | | 2 | Fog | | 3 | Clear | | 4 | Clear | | 5 | Clear | |
| Actual: 88° 55° | | | Actual: 86° 57° | | | Actual: 80° 60° | | | Actual: 84° 60° | | | Actual: 84° 60° | | | Forecast: 77° 50° | | | Forecast: 73° 48° | | |
| 0.00 in | | | 0.00 in | | | 0.00 in | | | 0.00 in | | | 0.00 in | | | 0.0 in | | | 0.0 in | | |
| Average: 69° 45° | | | Average: 68° 47° | | | Average: 68° 46° | | | Average: 70° 47° | | | Average: 70° 45° | | | Average: 69° 44° | | | Average: 66° 42° | | |
| 0.20 in | | | 0.12 in | | | 0.20 in | | | 0.22 in | | | 0.10 in | | | 0.12 in | | | 0.19 in | | |

Rain Days This Week = 0

Rain Days To Date = 53

SAFETY REVIEW LOG

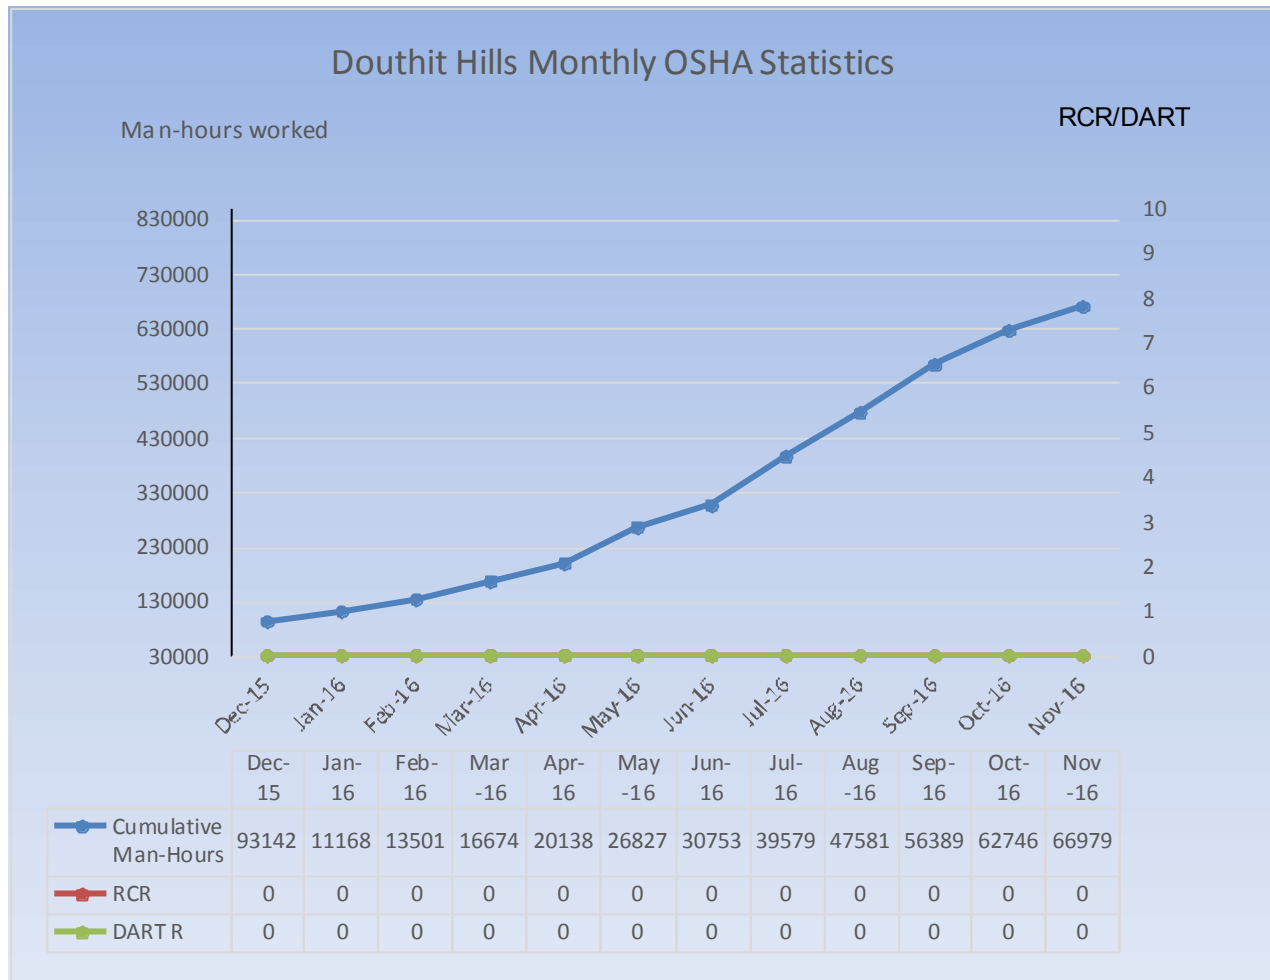

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #91
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

