

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #94
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 11880
- » Total Man Hours on Project: 721364
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued MEP Trim-out @ Building G.
- » Continued Wood Door Install @ Building.
- » Continued Setting Showers @ Building E.
- » Continued Hanging Drywall @ Buildings E & F.
- » Continued Priming Walls @ Building G.
- » Installed 1st Floor Storefront Doors @ Building G.
- » Continued Wall Tile @ Building G.
- » Poured Stairs @ East Monumental Stairs.
- » Installed Lights and Devices @ Building G.
- » Continued Fire Protection Bracing @ Building F.
- » Continued ACT Grid @ Building G.



Bldg. G Storefront Door



Bldg. F Exterior Soffit




Bldg. E 3rd Floor Rough-In

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Building B.
- » Continued MEP Rough-In @ HUB & Building B.
- » Continued Roofing @ Building B.
- » Continued Glass Installation @ HUB & Building B.
- » Poured SOG @ Building D.
- » Continued Interior Framing & Drywall @ Building A.
- » Continued DEFS @ Building A.
- » Continued MEP Rough-In @ Building A.
- » Continued Coil Piping to AHU @ HUB.
- » Continued Exterior Framing @ HUB.
- » Began Framing Load Bearing Walls @ Building C.



East Monumental Stair

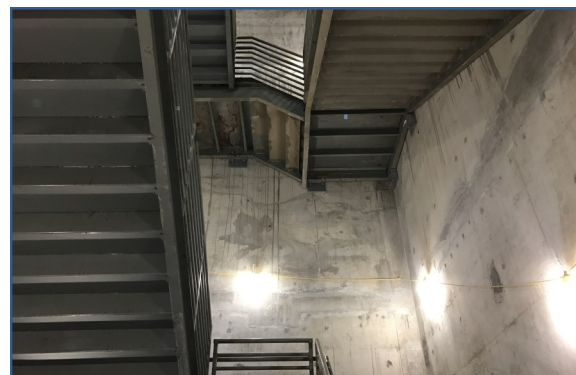

HUB Metal Pan Stairs



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue MEP Rough-In @ Building E.
- » Continue FCU Ductwork @ Buildings E.
- » Continue MEP Trim-out @ Building G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Setting Showers @ Building E.
- » Continue Hanging Drywall @ Buildings E.
- » Continue Finishing Drywall @ Building G & F.
- » Continue Wall Tile @ Building G.
- » Continue Installing Lights & Devices @ Building G.
- » Grade Building G Courtyard and East Spine.
- » Continue Wood Door Installation @ Building G.



Bldg. A Flat Roof




Bldg. B Switchgear



Bldg. D Precast

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB & Building B.
- » Continue MEP Rough-In @ HUB.
- » Continue Roofing @ Building B.
- » Continue Glass Installation @ HUB & Building B.
- » Continue Interior Framing & Drywall @ Building A.
- » Continue Interior Framing @ Building B.
- » Continue MEP Rough-In @ Building A.
- » Continue Interior Framing @ Building B.
- » Continue Site Lighting @ West Parking Lot
- » Pour Site Wall @ Building A.

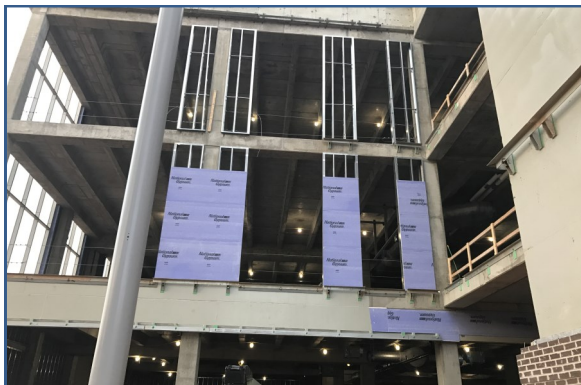

HUB Exterior Framing



Building D SOG

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #94
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE				
Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1170	93685
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	5	150	2850
Carolina Fire Protection	Sprinklers	16	480	16905
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	360	23910
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	6	180	930
Feltman Brothers	West - Masonry	20	600	11100
Gainesville Mechanical	Ductwork	30	900	52999
Gill Plumbing	Plumbing	27	810	18510
Graham Hodge	Glass	6	180	2130
Gregory Electric	Aboveground Electric	14	420	12370
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	8	240	9022
Johnson Controls	Building Controls	3	90	3765
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	20	600	31352
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	60	2363
Labor Finders	Labor Force	17	510	37308
Metro Power	Underground Electrical	4	120	20327
Nations Roofing	Roofing	11	330	5085
Old North State Masonry	East - Masonry	0	0	28619
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	1	30	82810
Pyramid Masonry	Hub-Masonry	13	390	5880
R.E. Mclean Tank	Tank Demo	0	0	660



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #94

Douthit Hills Student Community, Clemson University Project

Joe Jett




WEATHER

CURRENT WEEK

20	Clear		21	Clear		22	Clear		23	Partly Cloudy		24	Partly Cloudy		25	Fog		26	Clear	
Actual: 63° 37°	0.00 in	Actual: 64° 33°	0.00 in	Actual: 60° 35°	0.00 in	Actual: 63° 39°	0.00 in	Actual: 73° 54°	0.00 in	Actual: 75° 48°	0.00 in	Forecast: 67° 36°	0.0 in							
Average: 62° 40°	0.12 in	Average: 61° 38°	0.11 in	Average: 59° 36°	0.15 in	Average: 60° 36°	0.15 in	Average: 60° 37°	0.16 in	Average: 61° 37°	0.19 in	Average: 60° 37°	0.18 in							

Rain Days This Week = 0 Rain Days To Date = 53

SAFETY REVIEW LOG

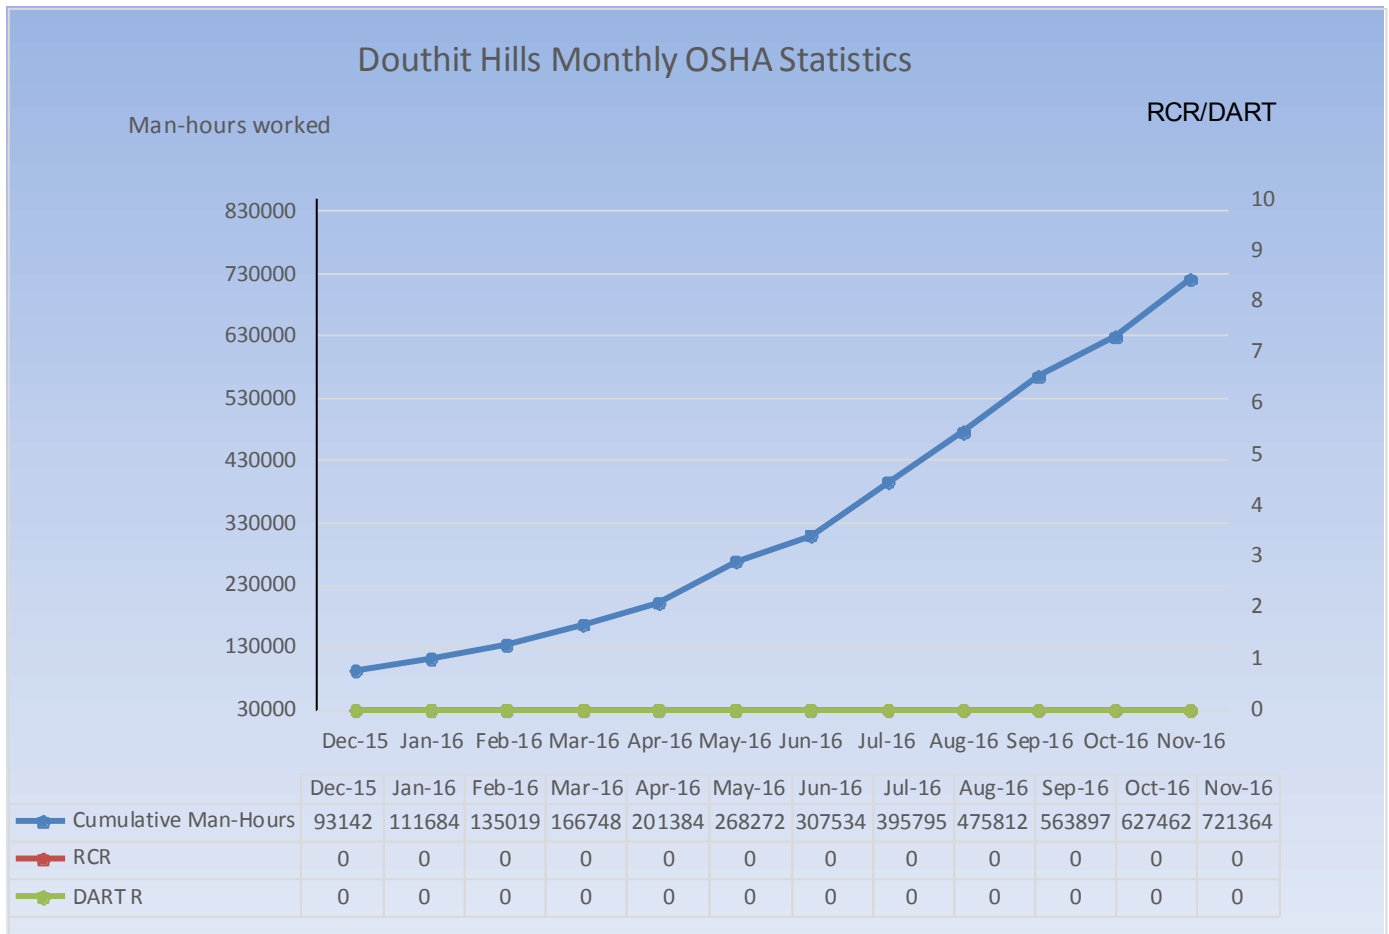

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #94
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

