

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 18610
- » Total Man Hours on Project: 776399
- » Crafts On Project This Week: 22
- » OSHA Recordable Rate: 0



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
Douthit Hills Student Community, Clemson University Project
Joe Jett



CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued Wood Door Install @ Building F.
- » Continued Hanging Drywall @ Building E.
- » Continued Painting Walls @ Building F.
- » Continued Wall Tile @ Building G.
- » Poured Fire Lane @ East Spine.
- » Poured Door Stoops @ Buildings G & F.
- » Installed Lights and Devices @ Building G.
- » Continued Fire Protection Upfit @ Building E.
- » Installed Storefront Doors @ Building E.
- » Continued ACT Grids @ Building G.
- » Installed Thermostats @ Building F.



Bldg. G Drip Edge



Bldg. F Door Stoop




Bldg. E Storefront Doors

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Building B.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Roofing @ Building B.
- » Continued Glass Installation @ HUB.
- » Continued Window Frames @ Building C
- » Continued Elevator Install @ Bldg. A.
- » Continued Exterior Framing @ HUB.
- » Install Storm Line @ Building B.
- » Continued Precast @ Building D.
- » Began Brick Masonry @ Building C.



East Spine – Fire Lane

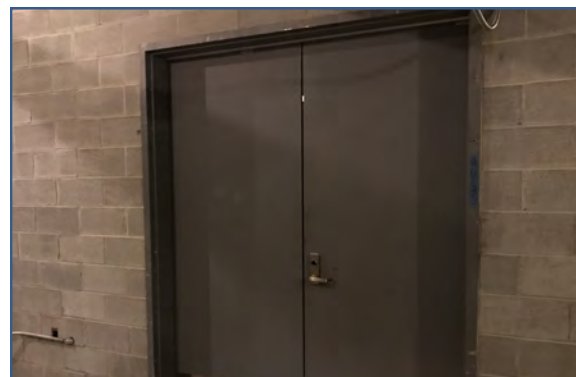

HUB Hollow Metal Doors



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Install Door Hardware @ Building G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Hanging Drywall @ Buildings E.
- » Continue Finishing Drywall @ Building E & F.
- » Continue Wall Tile @ Building G.
- » Continue Installing Lights & Devices @ Building F.
- » Pour Door Stoops @ Building E.
- » Continue Drip Edge @ Building G.
- » Begin Sawcuts @ East Spine Firelane.



Bldg. B Interior Framing



Bldg. C Window Frames



Bldg. D Precast

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB & Buildings B & C.
- » Continue MEP Rough-In @ Bldg. A, Bldg. B, & HUB.
- » Continue Roofing @ Building B.
- » Continue Interior Framing & Drywall @ Bldg A.
- » Continue Interior Framing @ Building B.
- » Continue Roof Decking @ Building C.
- » Continue Window Frames @ Building C.
- » Continue Precast @ Building D.
- » Continue Storm Line @ Building B.



HUB Curtain Wall



Storm Line - West Of Building B

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1560	98365
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	10	350	3950
Carolina Fire Protection	Sprinklers	16	800	19145
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	420	25110
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	6	300	1770
Feltman Brothers	West - Masonry	22	770	13745
Gainesville Mechanical	Ductwork	19	950	56399
Gill Plumbing	Plumbing	29	1450	22930
Graham Hodge	Glass	5	200	2730
Gregory Electric	Aboveground Electric	16	800	14430
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	10	500	10242
Johnson Controls	Building Controls	7	350	4385
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	25	1250	34582
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	2643
Labor Finders	Labor Force	17	680	39508
Metro Power	Underground Electrical	5	200	20847
Nations Roofing	Roofing	6	210	6010
Old North State Masonry	East - Masonry	0	0	28619
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	0	0	82810
Pyramid Masonry	Hub-Masonry	13	520	7440
R.E. Mclean Tank	Tank Demo	0	0	660

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CONTINUED

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Reeves Young	Site Grading & Utilities	8	360	57943
Rival Construction Inc.	Concrete	0	0	35816
RJ Coogan	Deck Installers	0	0	560
Ruppert Landscaping	Landscape/ Hardscape	0	0	380
Sears Contract	Drywall/Metal Trusses	82	4100	93162
Silt Fence Installation	Site Erosion Control	0	0	1031
Southern Mechanical Inc.	Electrical/Plumbing	44	1980	47600
Specialty Finishes	Painting	8	360	2205
Steel Toe	Labor Force	10	400	10415
Tree South	Arborist	0	0	2073
Upstate Curb	Curb and Gutter	0	0	684
Valley Farm Construction	Tree removal/Grading	0	0	395
Waterproofing Specialties	Waterproofing	0	0	3104
Total		411	18610	776399



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

11	Partly Cloudy	12	Rain	13	Rain	14	Partly Cloudy	15	Clear	16	Partly Cloudy	17	Overcast
Actual: 44° 28° 0.00 in	Actual: 68° 42° 0.00 in	Actual: 53° 43° 0.01 in	Actual: 55° 44° 0.00 in	Actual: 50° 32° 0.00 in	Actual: 37° 28° 0.00 in	Forecast: 50° 48° 0.17 in	Average: 55° 33° 0.13 in	Average: 54° 34° 0.19 in	Average: 55° 32° 0.12 in	Average: 56° 34° 0.11 in	Average: 54° 32° 0.27 in	Average: 54° 34° 0.19 in	Average: 55° 30° 0.13 in

Rain Days This Week = 0

Rain Days To Date = 58

SAFETY REVIEW LOG

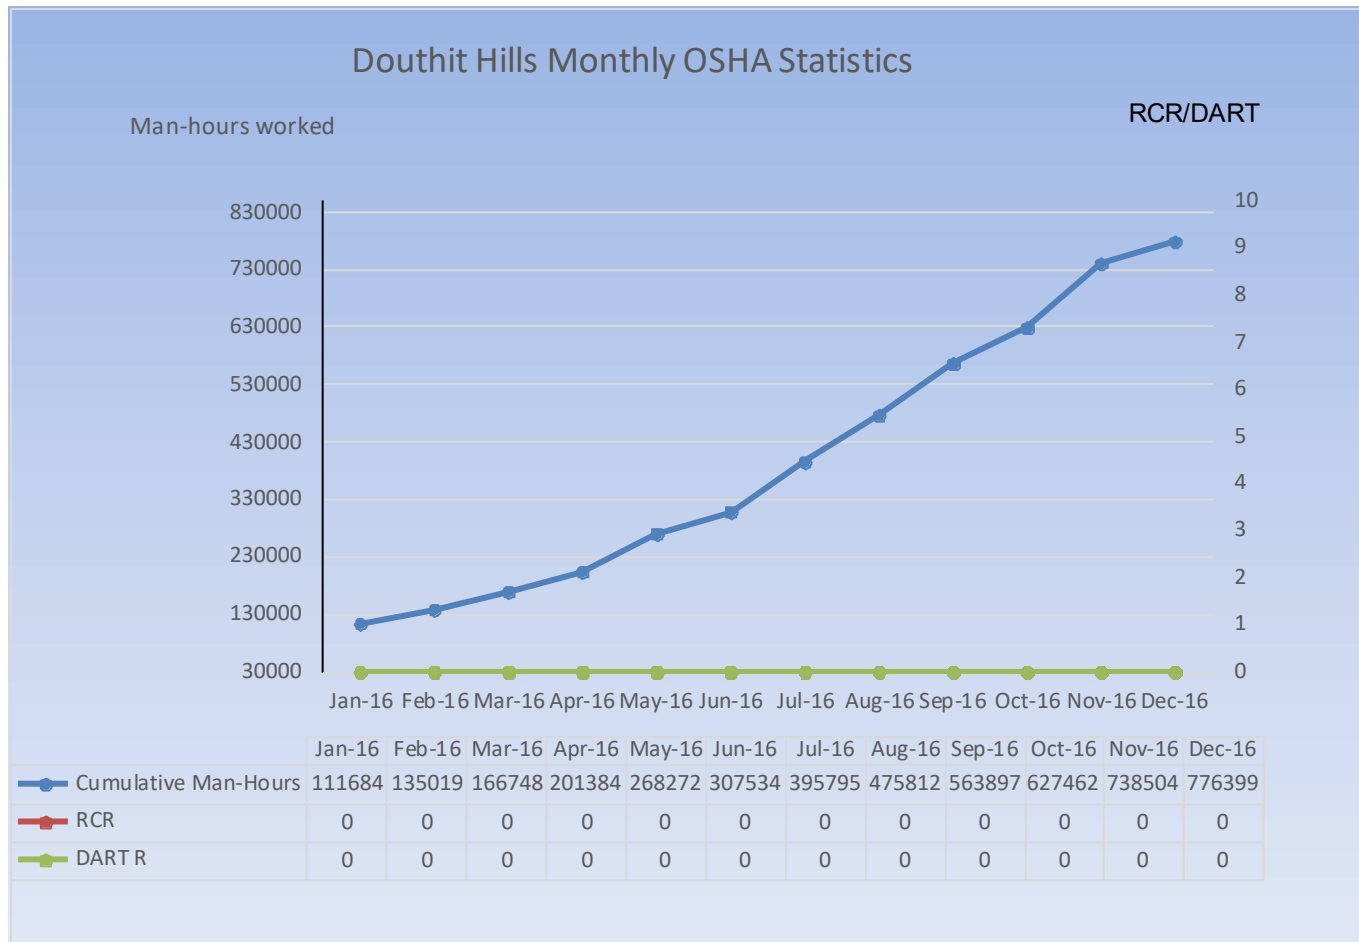


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #97
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

Douthit Hills Workforce

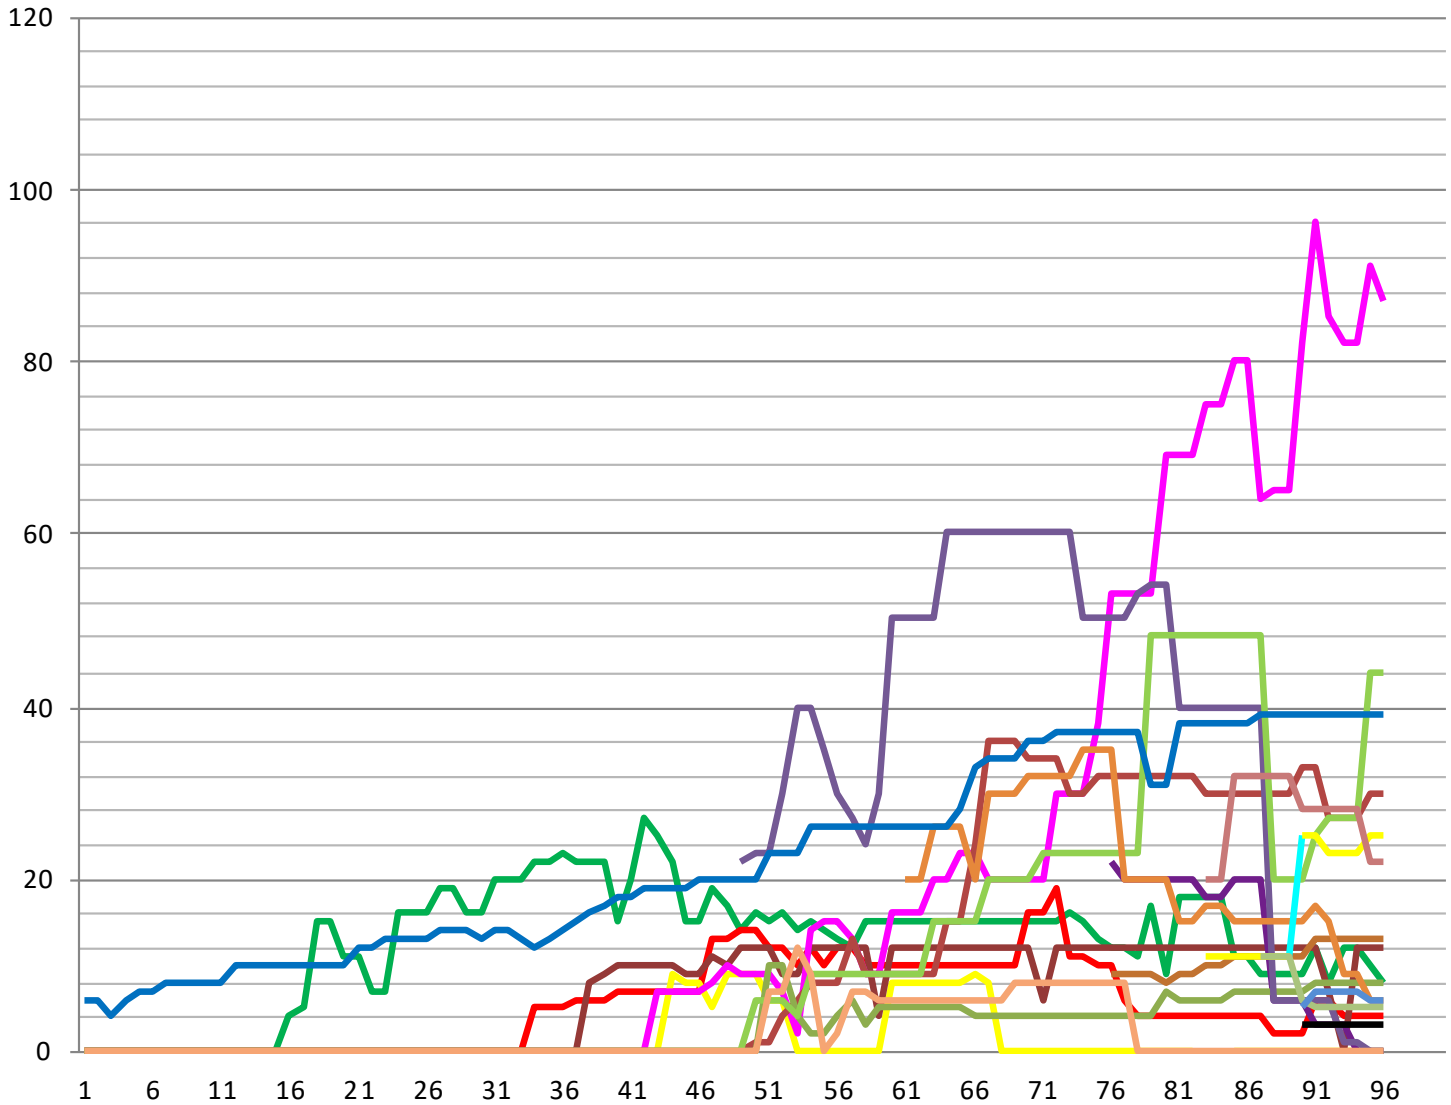

- Reeves Grading
- Davis Crane Erectors
- Sears Contract
- Precision Concrete
- Feltman Brothers
- Elite Flooring
- Holder
- Metro Power
- Old North State Masonry
- Gainesville Mechanical
- Southern Mechanical
- JME
- Speacialty Finishes
- American Deep Foundations
- Pyramid Masonry
- 1st Choice Glass
- Rival Construction
- Graham Hodge
- Baker Roofing

