



SAFETY

- » Total Man Hours Worked This Week: 17140
- » Total Man Hours on Project: 738504
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0





CURRENT CONSTRUCTION ACTIVITIES

East Zone


- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued Fire Protection Upfit @ Building G.
- » Continued Wood Door Install @ Building G.
- » Continued Setting Showers @ Building E.
- » Continued Hanging Drywall @ Buildings E & F.
- » Continued Priming Walls @ Building G.
- » Continued Wall Tile @ Building G.
- » Poured Landings @ East Monumental Stairs.
- » Installed Lights and Devices @ Building G.
- » Continued Fire Protection Bracing @ Building F.
- » Continued ACT Grid @ Building G.
- » Installed Storefront Doors @ Building F.



Bldg. G Light Fixtures and Ceiling Grid



Bldg. F Storefront Doors

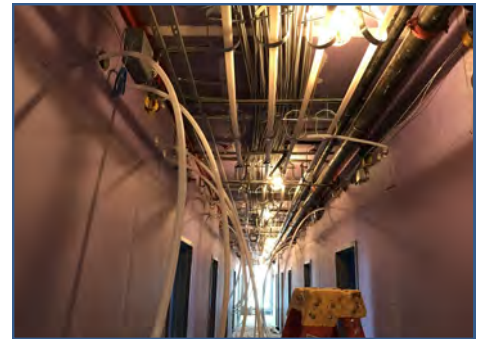


Bldg. E 4th Floor Overhead Rough-In

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Building B.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Roofing @ Building B.
- » Continued Glass Installation @ HUB & Building B.
- » Continued Interior Framing & Drywall @ Building A.
- » Continued DEFS @ Building A.
- » Began Window Frames @ Building C
- » Continued Elevator Install @ Bldg. A.
- » Poured Site Wall @ Building A.
- » Continued Exterior Framing @ HUB.
- » Began Roof Trusses @ Building C.



HUB Brick – East Wall

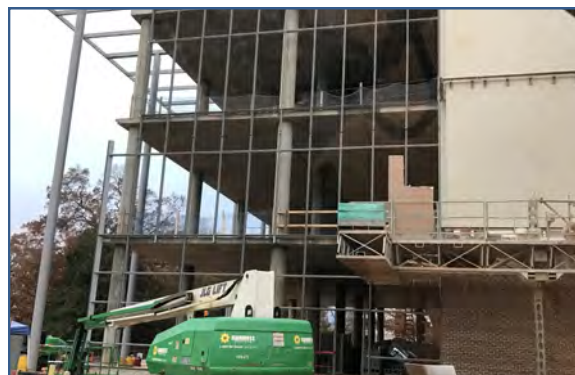

HUB Curtain Wall



T WEEK' S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue MEP Rough-In @ Building E.
- » Continue MEP Trim-out @ Building G.
- » Continue Fire Protection Upfit @ Building G.
- » Continue Setting Showers @ Building E.
- » Continue Hanging Drywall @ Buildings E.
- » Continue Finishing Drywall @ Building G & F.
- » Continue Wall Tile @ Building G.
- » Continue Installing Lights & Devices @ Building G and Building F.
- » Continue Mechanical Piping @ Building E.
- » Pour Stair Landings @ East Monumental Stair.
- » Continue Wood Door Installation @ Building G.



Bldg. A Interior Soffit Framing



Bldg. B Flat Roof




Bldg. D Precast

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB & Building B.
- » Continue MEP Rough-In @ Bldg. A, Bldg. B, & HUB.
- » Continue Roofing @ Building B.
- » Continue Glass Installation @ HUB & Building B.
- » Continue Interior Framing & Drywall @ Building A.
- » Continue Interior Framing @ Building B.
- » Continue Roof Trusses @ Building C.
- » Continue Window Frames @ Building C.
- » Continue Precast @ Building D.
- » Pour Generator Pads @ HUB.



Bldg. C Roof Trusses

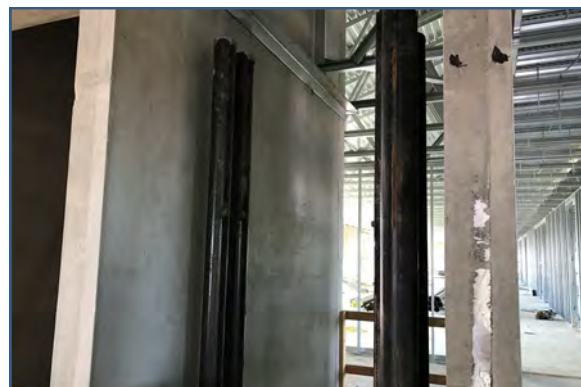

Bldg. B Supply & Return Chilled Water Piping

HOLDER CONSTRUCTION COMPANY



MANPOWER


TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1560	95245
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	10	400	3250
Carolina Fire Protection	Sprinklers	16	640	17545
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	12	360	24270
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	6	240	1170
Feltman Brothers	West - Masonry	25	1000	12100
Gainesville Mechanical	Ductwork	30	1200	54199
Gill Plumbing	Plumbing	33	1320	19830
Graham Hodge	Glass	5	200	2330
Gregory Electric	Aboveground Electric	14	560	12930
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	8	320	9342
Johnson Controls	Building Controls	3	120	3885
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	22	880	32232
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	80	2443
Labor Finders	Labor Force	17	680	37988
Metro Power	Underground Electrical	4	160	20487
Nations Roofing	Roofing	11	330	5415
Old North State Masonry	East - Masonry	0	0	28619
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	0	0	82810
Pyramid Masonry	Hub-Masonry	13	520	6400
R.E. Mclean Tank	Tank Demo	0	0	660



WEATHER

CURRENT WEEK



SAFETY REVIEW LOG

