

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #101
Douthitt Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 24034
- » Total Man Hours on Project: 865903
- » Crafts On Project This Week: 23
- » OSHA Recordable Rate: 0



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #101

Douthitt Hills Student Community, Clemson University Project


Joe Jett



CURRENT CONSTRUCTION ACTIVITIES

East Zone

- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Installed Lounge Doors @ Building G.
- » Continued Hanging Drywall @ Building E.
- » Continued Painting Walls @ Buildings G, F, & E.
- » Continued Wall Tile @ Building G & F.
- » Continued Lights and Devices @ Building F.
- » Continued Fire Protection Upfit @ Building E.
- » Continued ACT Grid @ Buildings E, F, & G.
- » Set Vanities @ Building G.
- » Installed Closet Trim @ Building G.
- » Continued Point Up @ Building G.

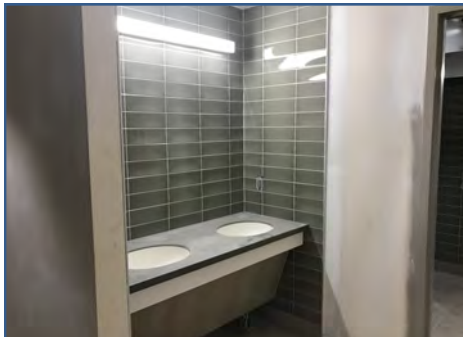

Bldg. G Vanity




ACT Grid @ Bldg. E



Bldg. E Terrace

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Bldg. C.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Hanging Duct @ HUB.
- » Continued Glass Installation @ HUB.
- » Continued Window Frames @ Building C.
- » Poured CIP Walls @ Building E Terrace.
- » Continued Topping Slab Prep @ Building D.
- » Poured Loading Dock Footings @ HUB.
- » Poured Topping Slab @ Building D.
- » Continued Bldg E Terrace.
- » Continued Site Lighting.

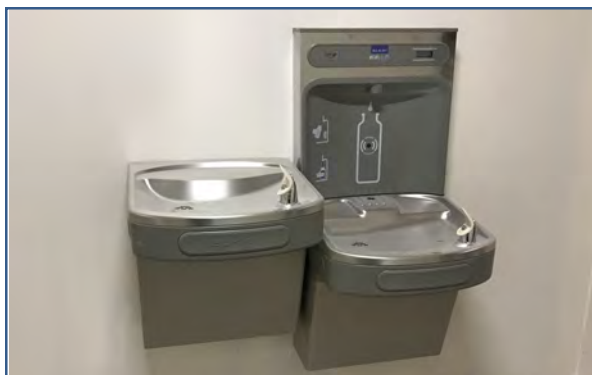

Building G Water Fountain



HUB - Loading Dock Reinforcing

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #101

Douthitt Hills Student Community, Clemson University Project


Joe Jett



NEXT WEEK'S ACTIVITIES

East Zone


- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Wall Tile @ Buildings F & G.
- » Continue ACT Grid @ Buildings E & F.
- » Continue Installing Lights & Devices @ Buildings F & E.
- » Continue Point Up @ Building G.
- » Continue Install Doors & Hardware @ Bldgs. F & G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Hanging Drywall @ Building E.

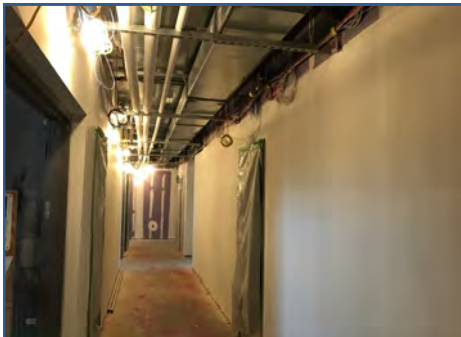

Building A Corridor Paint



Building C Masonry-East Elevation

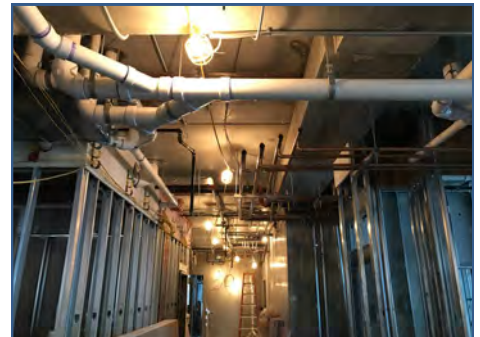

Building B - Overhead Rough-In

SITE, HUB, & WEST ZONE

- » Continue Sunshade Infill @ HUB.
- » Continue Pouring Building E Terrace.
- » Continue Topping Slab Prep @ Building D.
- » Begin Framing Interior Walls @ Building C.
- » Continue Coring @ Building C For Plumbing.
- » Continue Grading Pouring Inverts.
- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB & Building C.
- » Continue MEP Rough-In @ Bldgs A, B, & HUB.
- » Continue Interior Framing & Drywall @ Bldg B.
- » Continue Roof Decking @ Building C.
- » Continue Window Frames @ Building C.



Loading Dock Ramp Footers



Building D SOG Prep

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #101
Douthitt Hills Student Community, Clemson University Project
Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1560	104125
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	5	200	4500
Cabinets By Design	Millwork	2	80	160
Carolina Fire Protection	Sprinklers	16	800	21845
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	10	500	2870
Feltman Brothers	West - Masonry	19	950	17185
Gainesville Mechanical	Ductwork	14	700	59719
Gill Plumbing	Plumbing	32	1600	28230
Graham Hodge	Glass	9	360	3970
Gregory Electric	Aboveground Electric	15	750	17100
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	17	850	12452
Johnson Controls	Building Controls	9	450	5435
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	30	1500	40522
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	2963
Labor Finders	Labor Force	17	680	42228
Metro Power	Underground Electrical	3	120	21547
Nations Roofing	Roofing	10	400	6995
Old North State Masonry	East - Masonry	0	0	28769
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	7	350	83410
Pro Door	Doors & Hardware	5	250	250

Superintendents Weekly Activity Report #101
Douthitt Hills Student Community, Clemson University Project
Joe Jett

[illegible]

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #101






















Douthit Hills Student Community, Clemson University Project

Joe Jett




WEATHER

CURRENT WEEK

8	Clear		9	Clear		10	Partly Cloudy		11	Rain		12	Partly Cloudy		13	Scattered Clouds		14	Partly Cloudy	
Actual: 37° 21°  0.00 in			Actual: 37° 23°  0.00 in			Actual: 50° 28°  0.00 in			Actual: 59° 44°  0.06 in			Actual: 72° 48°  0.00 in			Actual: 79° 50°  0.00 in			Forecast: 63° 53°  0.0 in		
Average: 52° 30°  0.35 in			Average: 48° 28°  0.22 in			Average: 47° 29°  0.28 in			Average: 48° 28°  0.15 in			Average: 49° 26°  0.14 in			Average: 49° 27°  0.16 in			Average: 50° 28°  0.09 in		
Rain Days This Week = <u>1</u>										Rain Days To Date = <u>60</u>										

SAFETY REVIEW LOG

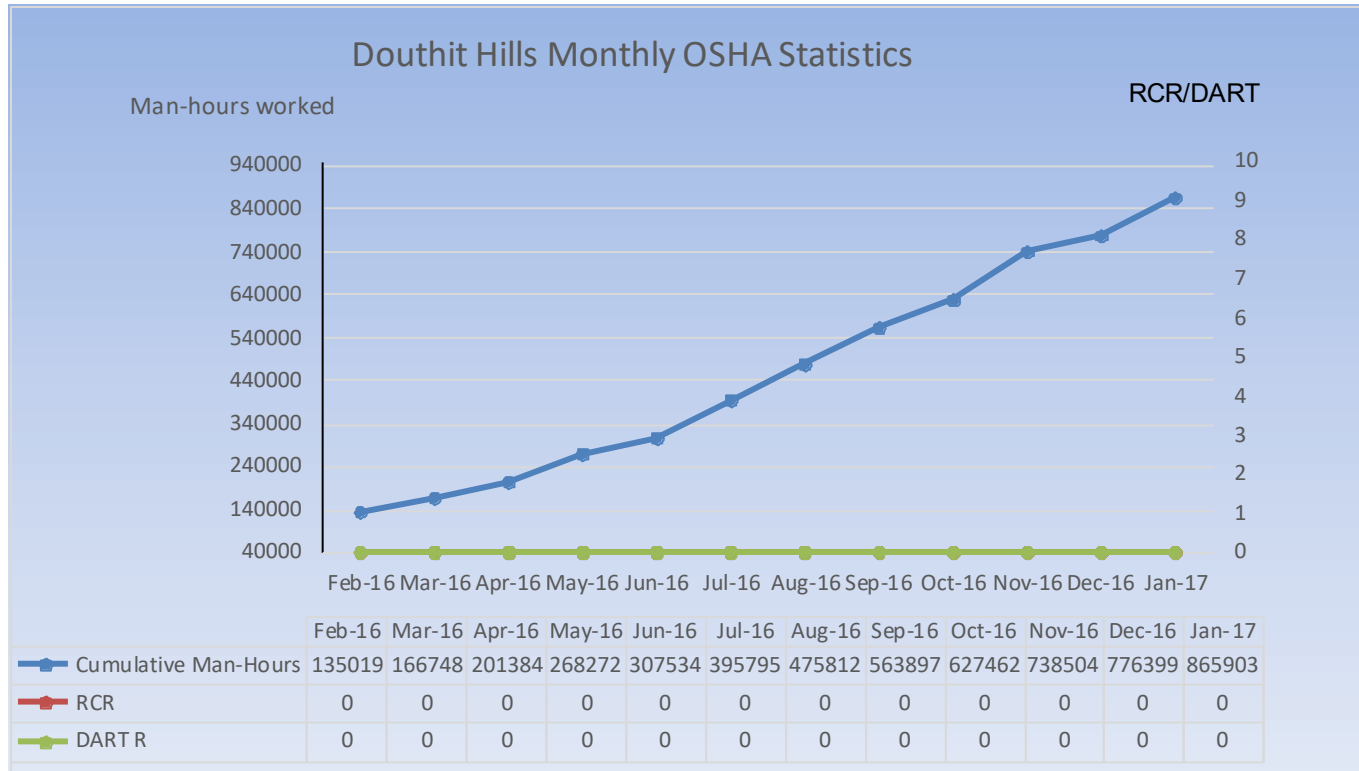



MANPOWER CHART

Douthit Hills Workforce

