

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #100
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 18965
- » Total Man Hours on Project: 840489
- » Crafts On Project This Week: 23
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

East Zone


- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued Wood Door Install @ Building F.
- » Continued Hanging Drywall @ Building E.
- » Continued Painting Walls @ Buildings F & E.
- » Continued Wall Tile @ Building G.
- » Continued Lights and Devices @ Building F.
- » Continued Fire Protection Upfit @ Building E.
- » Continued ACT Grid @ Buildings G & F.
- » Installed Dorm Lights @ Building F.
- » Set Plumbing Fixtures @ Building G.
- » Set Water Fountains @ Building G.
- » Continued Point Up @ Building G.



Bldg. G Window Sill

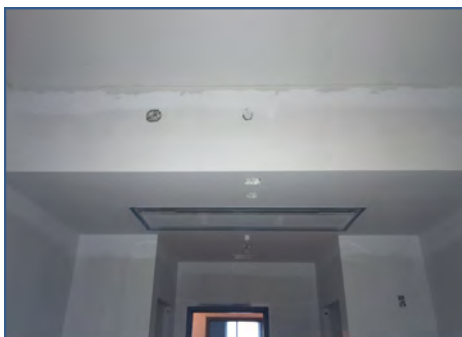


Paint in Bldg. E

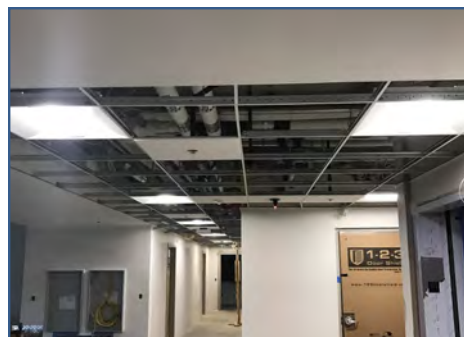

Bldg. F Ceiling Grid

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB & Bldg. C.
- » Continued MEP Rough-In @ HUB, Bldg. B, & Bldg. A.
- » Continued Hanging Duct @ HUB.
- » Continued Glass Installation @ HUB.
- » Continued Window Frames @ Building C.
- » Continued Elevator Install @ Bldg. A.
- » Poured Footings @ Building E Terrace.
- » Continued Topping Slab Prep @ Building D.
- » Began Prep For Loading Dock @ HUB.
- » Continued Hydrostatic Testing of H2O System

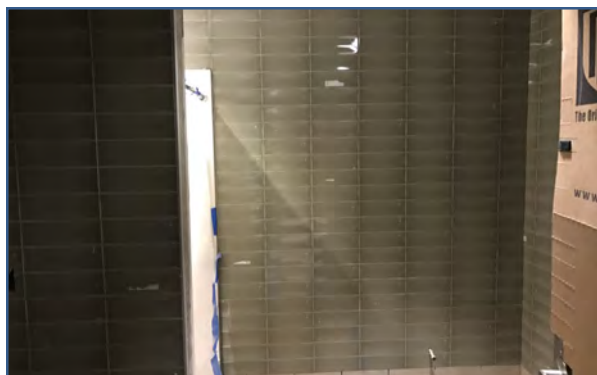

Building G Wall Tile



Corridor Lights @ Building G



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Install Doors & Hardware @ Bldgs. F & G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Hanging Drywall @ Building E.
- » Continue Finishing Drywall @ Building E & F.
- » Continue Wall Tile @ Building G.
- » Continue ACT Grid @ Building F.
- » Continue Installing Lights & Devices @ Building F.
- » Continue Plumbing Fixtures @ Building G.



Bedding & Taping @ Bldg. A



HUB Masonry - West Elevation



Building B - Mechanical Room

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB, Building B & C.
- » Continue MEP Rough-In @ Bldgs. A, B, & HUB.
- » Continue Interior Framing & Drywall @ Bldg A.
- » Continue Interior Framing @ Building B.
- » Continue Roof Decking @ Building C.
- » Continue Window Frames @ Building C.
- » Continue Sunshade Infill @ HUB.
- » Continue Pouring Building E Terrace.
- » Continue Topping Slab Prep @ Building D.
- » Begin Newman Road Intersection Improvements @ Hwy 93.
- » Install 2 Storm Structures North of Bldg. B.



HUB Curtain Wall



HUB Generator

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #100
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1560	102565
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	5	175	4300
Carolina Fire Protection	Sprinklers	11	550	21045
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	0	0	25900
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	6	300	2370
Feltman Brothers	West - Masonry	19	665	16235
Gainesville Mechanical	Ductwork	19	950	59019
Gill Plumbing	Plumbing	25	1250	26630
Graham Hodge	Glass	8	320	3610
Gregory Electric	Aboveground Electric	12	600	16350
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	10	500	11602
Johnson Controls	Building Controls	6	300	4985
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	30	1500	39022
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	2863
Labor Finders	Labor Force	17	680	41548
Metro Power	Underground Electrical	4	160	21427
Nations Roofing	Roofing	5	175	6595
Old North State Masonry	East - Masonry	3	150	28769
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	5	250	83060
Pyramid Masonry	Hub-Masonry	13	520	9080
R.E. Mclean Tank	Tank Demo	0	0	660

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #100
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

Day	Weather	Actual High/Low	Precipitation	Average High/Low	Average Precipitation
1	Rain	50° 39°	0.37 in	53° 34°	0.27 in
2	Rain	55° 50°	0.91 in	53° 33°	0.11 in
3	Rain	64° 52°	0.25 in	52° 32°	0.18 in
4	Clear	57° 43°	0.00 in	52° 32°	0.27 in
5	Partly Cloudy	50° 34°	0.00 in	52° 30°	0.14 in
6	Snow	46° 33°	MM in	51° 30°	0.10 in
7	Snow	39° 26°	MM in	51° 30°	0.11 in

Rain Days This Week = 1

Rain Days To Date = 60

SAFETY REVIEW LOG

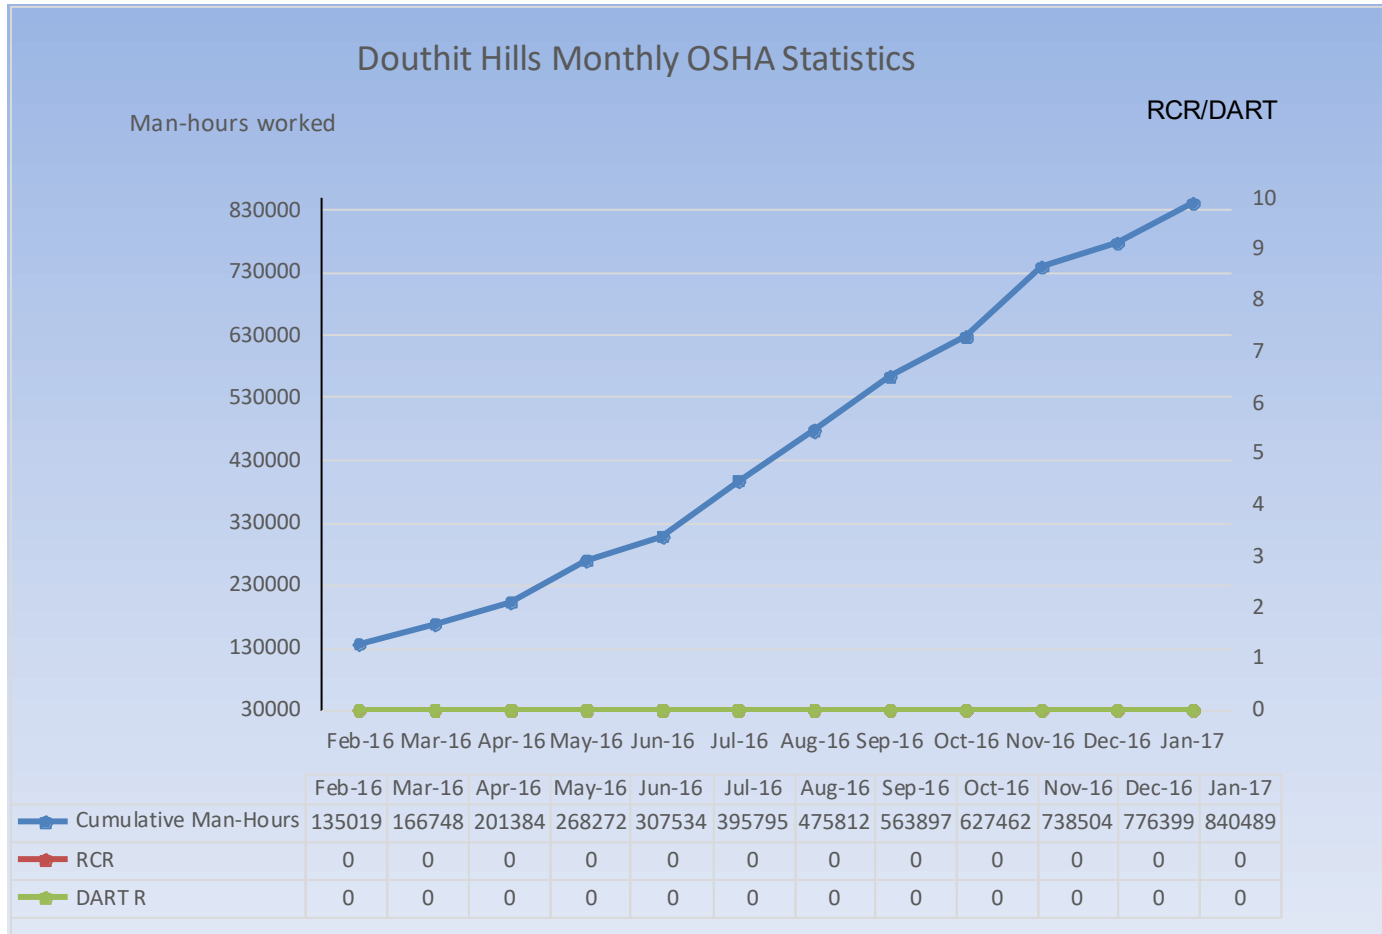


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #100
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

Douthit Hills Workforce

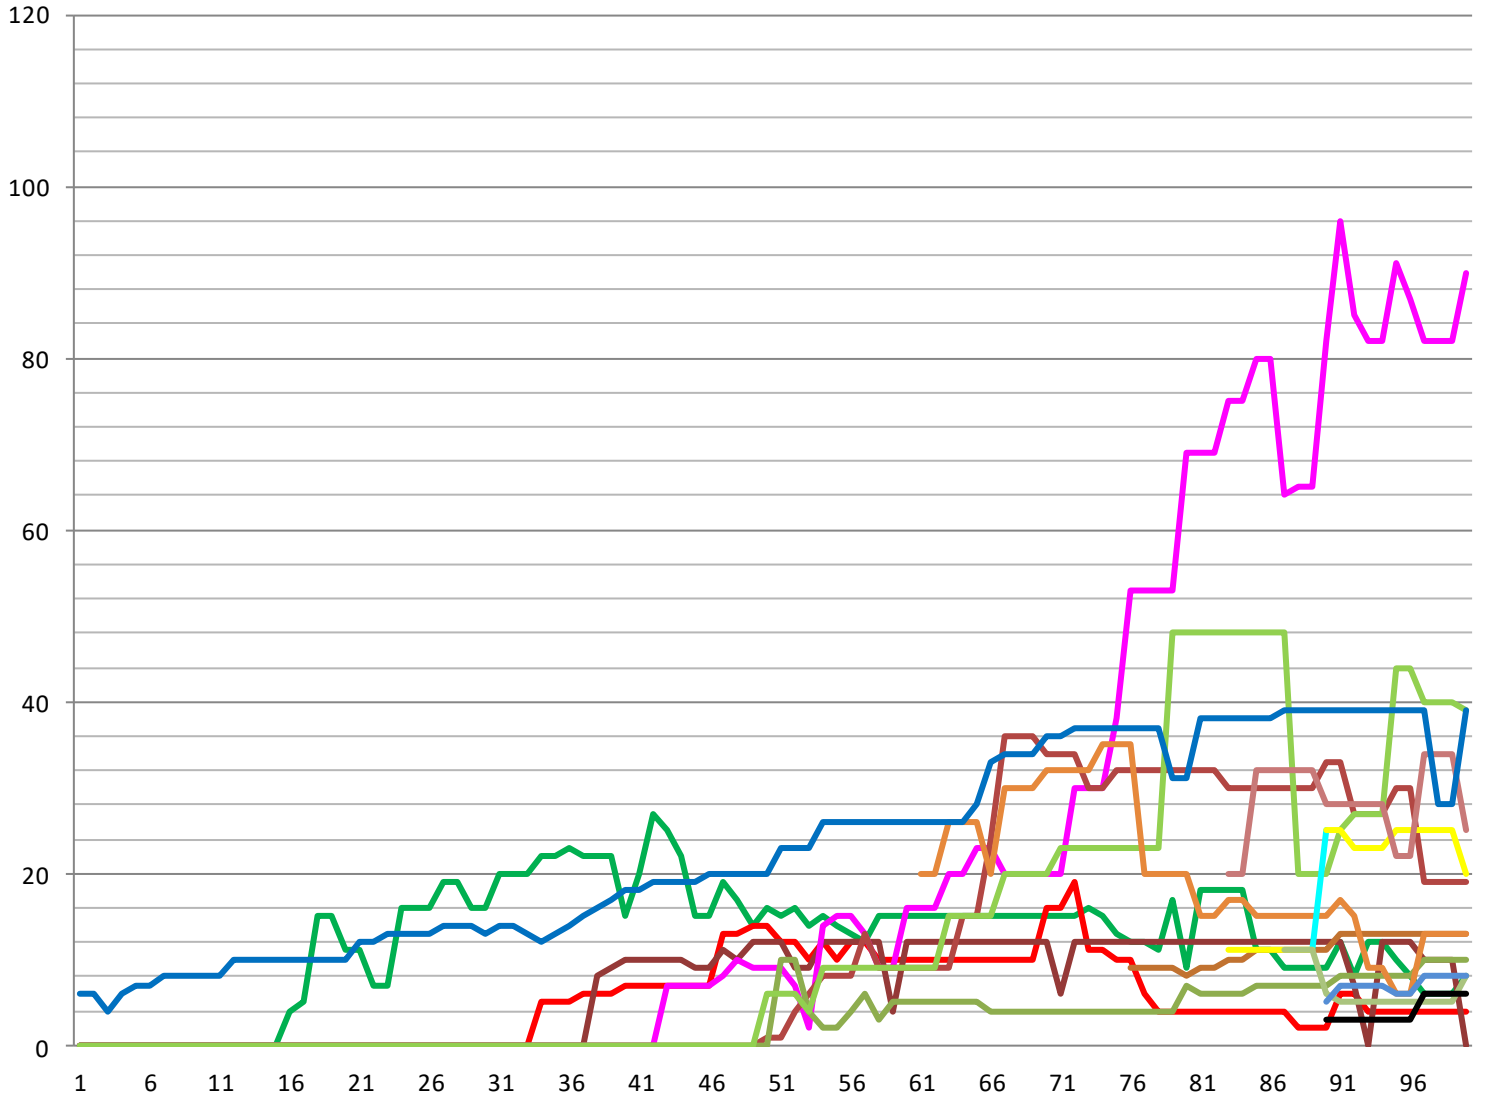

- Reeves Grading
- Metro Power
- Davis Crane Erectors
- Pyramid Masonry
- Sears Contract
- Gainesville Mechanical
- 1st Choice Glass
- Southern Mechanical
- Rival Construction
- Feltman Brothers
- JME
- Graham Hodge
- Elite Flooring
- Specialty Finishes
- Holder

