

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #98
Douthit Hills Student Community, Clemson University Project
Joe Jett



SAFETY

- » Total Man Hours Worked This Week: 19705
- » Total Man Hours on Project: 797224
- » Crafts On Project This Week: 24
- » OSHA Recordable Rate: 0






CURRENT CONSTRUCTION ACTIVITIES

East Zone


- » Continued MEP Rough-In @ Building E.
- » Continued FCU Ductwork @ Buildings E & F.
- » Continued Wood Door Install @ Building F.
- » Continued Hanging Drywall @ Building E.
- » Continued Painting Walls @ Building F.
- » Continued Wall Tile @ Building G.
- » Poured Door Stoops @ Building E.
- » Continued Lights and Devices @ Building G.
- » Continued Fire Protection Upfit @ Building E.
- » Finished Storefront Doors @ Building E.
- » Continued ACT Grid @ Buildings G & F.
- » Installed Dorm Lights @ Building F.
- » Set Plumbing Fixtures @ Building G.

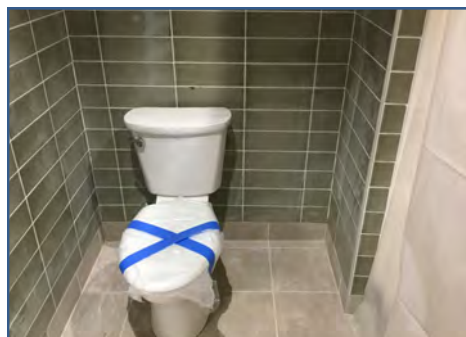

Bldg. G Plumbing Fixtures



Bldg. F ACT Grid

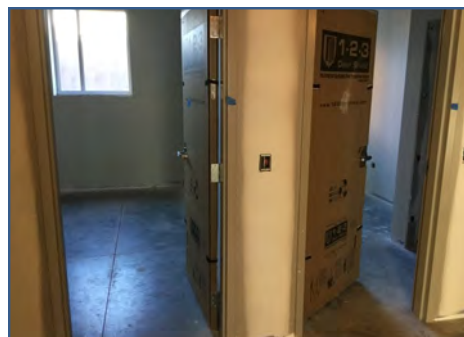

Bldg. F Door Hardware

SITE, HUB, & WEST ZONE

- » Continued Interior Framing @ Building B.
- » Continued Brick Masonry @ HUB, Bldgs B & C.
- » Continued MEP Rough-In @ HUB, Bldgs B & A.
- » Continued Roofing @ Building B.
- » Continued Glass Installation @ HUB.
- » Continued Window Frames @ Building C.
- » Continued Elevator Install @ Bldg. A.
- » Continued Exterior Framing @ HUB.
- » Installed Storm Line @ Building B.
- » Continued Precast @ Building D.
- » Continued Drywall Finishing @ Building A.



East Spine – Fire Lane




HUB Breezeway



NEXT WEEK'S ACTIVITIES

East Zone

- » Continue Overhead Rough-In @ Buildings E & F.
- » Continue Install Door Hardware @ Building G.
- » Continue Fire Protection Upfit @ Building E.
- » Continue Hanging Drywall @ Buildings E.
- » Continue Finishing Drywall @ Building E & F.
- » Continue Wall Tile @ Building G.
- » Continue ACT Grid @ Building G & F.
- » Continue Installing Lights & Devices @ Building F.
- » Continue Plumbing Fixtures @ Building G.
- » Continue Painting Walls @ Building F.

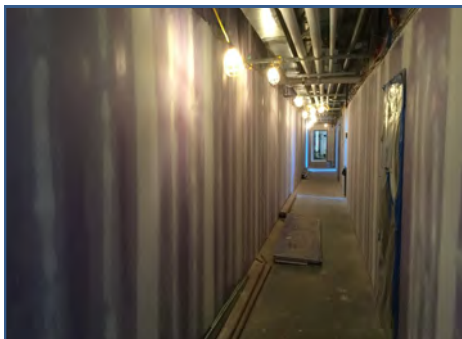

Bldg. A Drywall Finishing



Bldg. B DEFS Board




Bldg. C Brick Masonry

SITE, HUB, & WEST ZONE

- » Continue Curtain Wall Framing @ HUB.
- » Continue Brick Masonry @ HUB, Building B & C.
- » Continue MEP Rough-In @ Bldg. A, Bldg. B, & HUB.
- » Continue Roofing @ Building B.
- » Continue Interior Framing & Drywall @ Bldg. A.
- » Continue Interior Framing @ Building B.
- » Continue Roof Decking @ Building C.
- » Continue Window Frames @ Building C.
- » Continue Precast @ Building D.
- » Install Storm Line @ Building B Courtyard.



HUB Curtain Wall

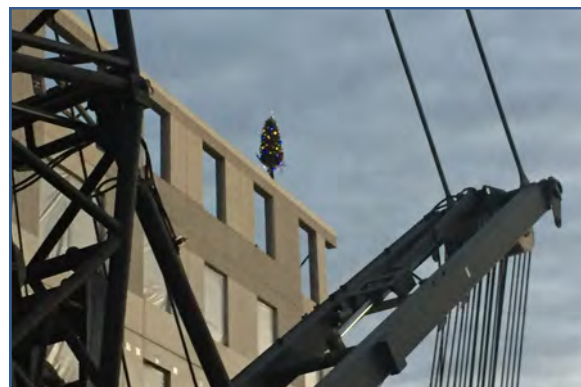

Topped-Out Building D

HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #98
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



MANPOWER

TRADE CONTRACTORS ON SITE

Subcontractor	Trade	Employees	Man Hours	Total Man Hrs.
Holder Construction Company	General Contractor	39	1560	99925
American Deep Foundation	Auger Cast Piles	0	0	6166
Baker Roofing	Sheathing and Shingles	0	0	7194
Brightview Landscape Development	Hardscape & Landscape	5	175	4125
Carolina Fire Protection	Sprinklers	16	800	19945
C&C Fence	Site Fence	0	0	854
Cowart Tree Mulch	Tree Removal	0	0	710
Davis Crane Erectors	Pre-Cast Erection	10	350	25460
D.H. Griffin	Tank Foundation Removal	0	0	90
Elite Flooring	Tile	6	300	2070
Feltman Brothers	West - Masonry	25	875	14620
Gainesville Mechanical	Ductwork	19	950	57349
Gill Plumbing	Plumbing	29	1450	24380
Graham Hodge	Glass	5	200	2930
Gregory Electric	Aboveground Electric	16	800	15230
Hutch-N-Son	Early Site Work	0	0	1337
1st Choice Glass	Glass	10	500	10742
Johnson Controls	Building Controls	6	300	4685
JBR Construction	Early Site Work	0	0	2049
Johnsons Modern Electric	Aboveground Electrical	34	1700	36282
King Asphalt	Asphalt	0	0	4189
Kone	Elevators	2	100	2743
Labor Finders	Labor Force	17	680	40188
Metro Power	Underground Electrical	7	280	21127
Nations Roofing	Roofing	6	210	6220
Old North State Masonry	East - Masonry	0	0	28619
Osteen	Chill Water pipe	0	0	2122
Precision	Concrete	0	0	82810
Pyramid Masonry	Hub-Masonry	13	520	7960
R.E. Mclean Tank	Tank Demo	0	0	660



HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #98
 Douthit Hills Student Community, Clemson University Project
 Joe Jett



WEATHER


CURRENT WEEK

18	Rain		19	Overcast		20	Fog		21	Fog		22	Partly Cloudy		23	Clear		24	Overcast	
Actual: 66° 45°	Actual: 50° 43°	Actual: 45° 32°	Actual: 57° 30°	Forecast: 68° 39°	Forecast: 55° 44°	Forecast: 60° 49°	0.02 in	0.00 in	0.00 in	0.00 in	0.00 in	0.0 in	0.0 in	0.0 in	0.0 in	0.0 in	0.0 in	0.0 in	0.0 in	0.21 in
Average: 53° 29°	Average: 54° 29°	Average: 54° 33°	Average: 53° 33°	Average: 51° 31°	Average: 50° 32°	Average: 52° 32°	0.04 in	0.04 in	0.09 in	0.19 in	0.18 in	0.07 in	0.07 in	0.21 in	0.07 in	0.07 in	0.07 in	0.07 in	0.07 in	0.21 in

Rain Days This Week = 0

Rain Days To Date = 58

SAFETY REVIEW LOG

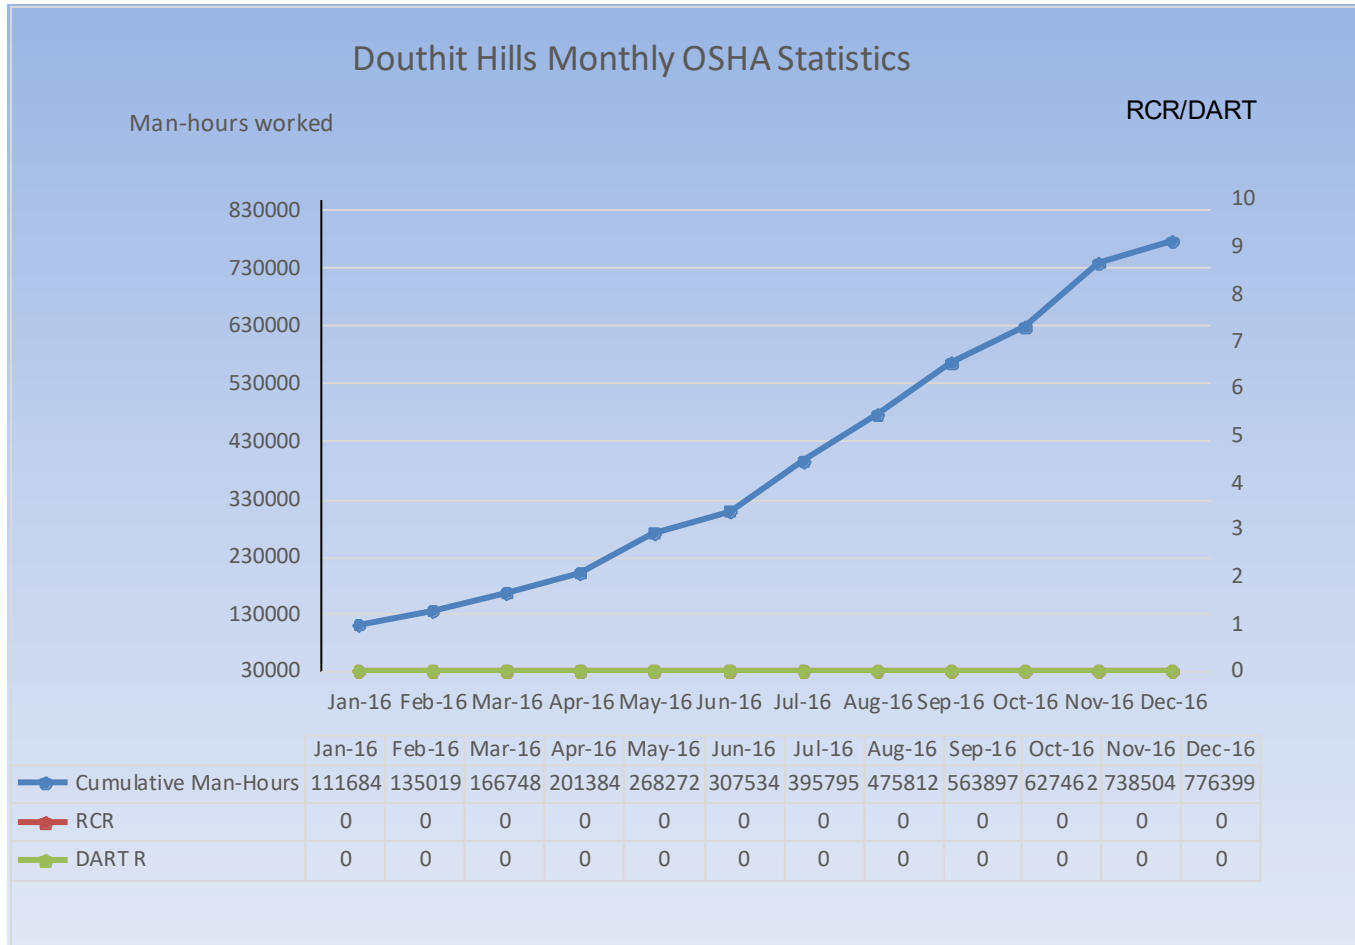


HOLDER CONSTRUCTION COMPANY

Superintendents Weekly Activity Report #98
Douthit Hills Student Community, Clemson University Project
Joe Jett



MANPOWER CHART

Douthit Hills Workforce

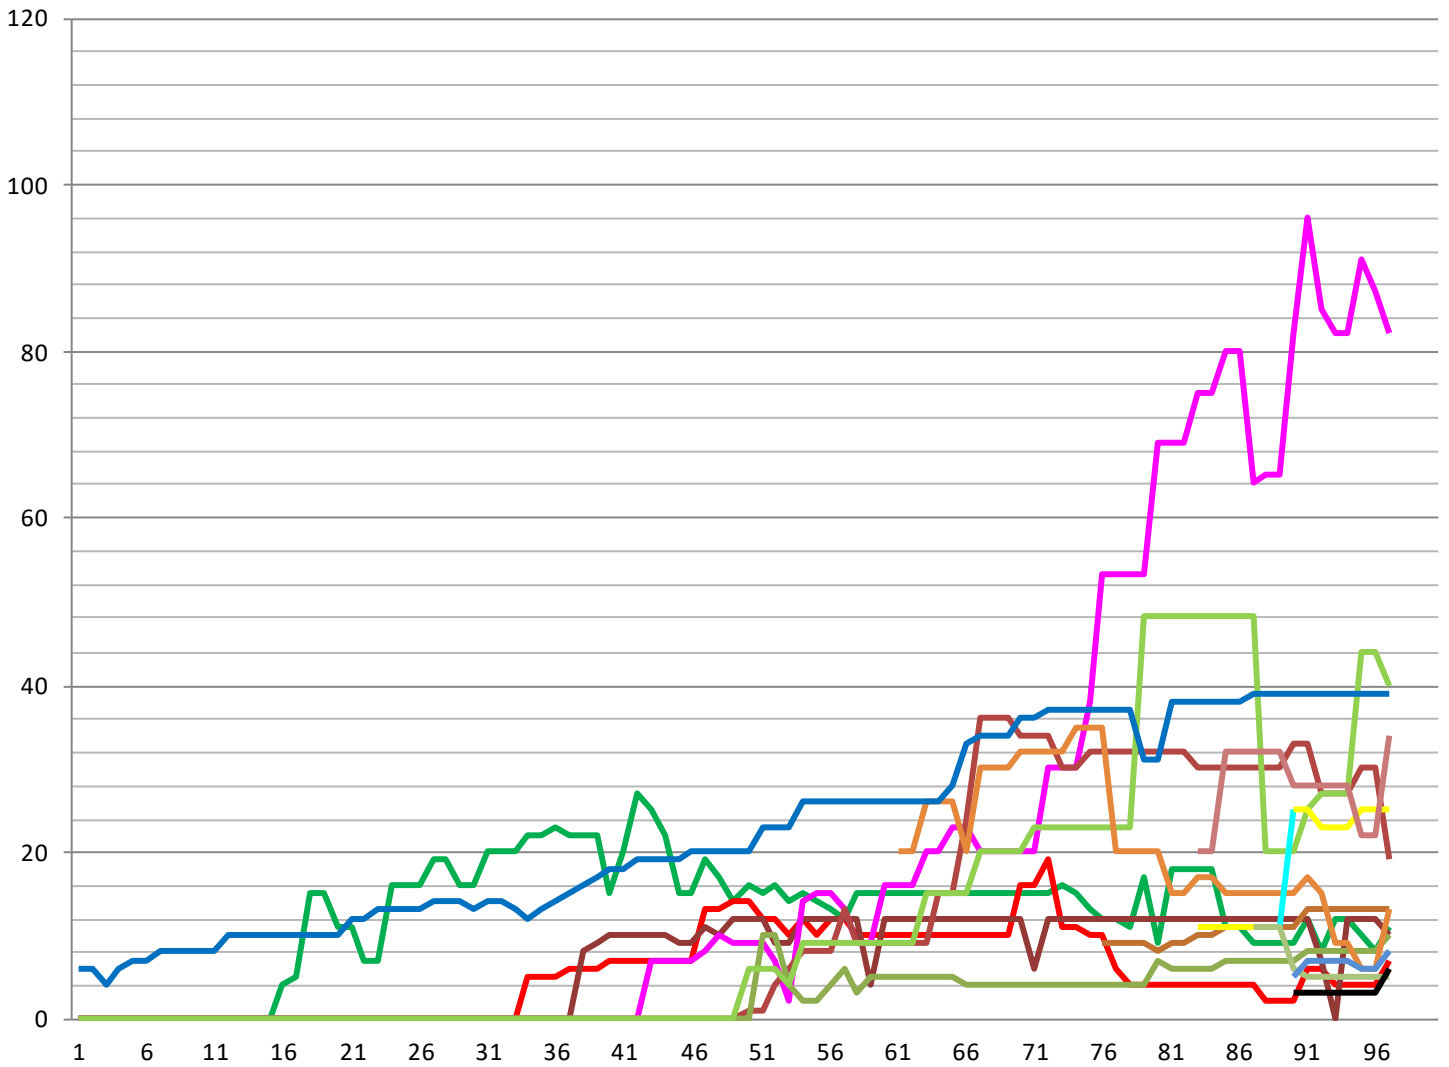

- Reeves Grading
- Metro Power
- Davis Crane Erectors
- Pyramid Masonry
- Sears Contract
- Gainesville Mechanical
- 1st Choice Glass
- Southern Mechanical
- Rival Construction
- Feltman Brothers
- JME
- Graham Hodge
- Elite Flooring
- Specialty Finishes
- Holder

